PLAINTIFF'S EXHIBIT
PX-715

THE PORT AUTHORITY OF NEW YORK AND NEW JERSEY

MEMORANDUM

To: August Preschle, Manager, World Trade Center Operations
From: Harry R. Pool, Jr.
Date: March 24, 1988
Subject: THE WORLD TRADE CENTER - ASBESTOS INVESTIGATION AND ANALYSIS REPORT
Copy to: F. Boyce, N. Budeiri, D. Darcy, J. Davison, D. Hahn, P. LaRocco, D. Leahy, R. Linn, P. Maurer, D. Moncalbano, J. Pearse, S. Samperi, V. Strom

The baseline asbestos survey of the World Trade Center, whose objective was to locate, identify and assess the condition of asbestos containing materials (ACM) throughout the complex, has been completed. This investigation consisted of three phases: the identification of the location of possible ACM throughout the facility; the collection and laboratory analysis of bulk samples; and the development of an environmental risk assessment.

Air monitoring to date at the facility indicates air quality levels are well within current Federal standards.

Buildings One, Two, Four, Five, and the associated sub-grades were sampled for the presence of ACM in some or all of the following materials: sprayed-on fire retardant on structural support beams, concrete slabs and metal deck ceilings; insulation on heat transfer pipes and insulation on heating and cooling equipment; ceiling tiles; floor tiles; and other materials serving as insulation or acoustical barriers. Sampling of materials, products and locations will continue on an as needed basis at the request of the facility to further define ACM locations and to further define ACM in the vicinity of proposed building alterations.

The Vista Hotel (Building Three) received limited sampling since this structure was built well past the moratorium on the use of asbestos products for insulation and as a fire retardant.

This survey was conducted over the period January 1986 through August 1987, during which time over 15,000 bulk and air samples were collected and analyzed.

The investigation was accomplished by entering areas, both occupied and vacant, to locate possible sources of ACM. The type of possible ACM as well as the building number, sample location, and area description were indicated on the bulk sampling form. In addition, the sampling results are being plotted by WTC staff on the layout plan of each floor for distribution to the applicable operations, planning and construction personnel.

A prioritization system has been developed which will inform the facility as to those areas requiring an Immediate Response. In addition, this system will rate other locations as Priority, Operations and Maintenance, Controlled Condition, or free of asbestos materials (ACM free). The categorization of all surveyed areas and the definitions used in the risk assessment are as follows:

Immediate Response Condition

An Immediate Response Condition (IRC) exists if there is an unavoidable risk potential due to the disturbance of asbestos fallout material within a specific area, which includes evidence of asbestos material separated from initial installation, deteriorated condition of existing asbestos material, high risk of contact, or the possibility of causing unacceptable levels of airborne asbestos fibers in areas frequented by employees and/or patrons. Air sampling should be initiated in all areas rated as IRC (Immediate Response Condition). Redesignation of these locations should take place after the Immediate Response has been completed.

The following locations at the World Trade Center are defined as IRC: the roofs of elevator cars in Tower One within the shafts where delamination has occurred and the B-6 Level Mechanical Room which has fallout material present in one localized area.

World Trade Center management has been briefed on these conditions and provided with a list of specific locations. In addition, the World Trade Center has requested the Inspection and Safety Division to employ the cleanup and disposal call-in contractor to assist in cleaning these areas. A regular monitoring program to detect similar fallout materials in the future should also be initiated.

After receiving immediate notification from the Inspection and Safety Division, the facility responded by initiating and carrying out cleanup and repair activities utilizing the services of licensed asbestos contracting firms to alleviate those conditions existing as IRC designated locations.

These efforts have resulted in the reclassification of the following IRC areas:

Location	Site	Reclassification
Roofs of elevator cars within the shafts.	1 WTC	Operations & Maintenance
B-6 level mechanical equipment room.	1 WTC	Operations & Maintenance

Priority Area

In order for a location to be designated a Priority Area, the asbestos material must be in disrepair or accessible to the extent that worker activity, or other forces, could produce an increase in the level of airborne

asbestos fibers. As with an IRC, Priority Areas should receive air sampling as an additional input for the risk assessment analysis. Periodic re-inspection of conditions in a Priority Area is mandatory. Once a Priority Area is identified by the Inspection and Safety Division, the facility must institute the appropriate measures. All aspects of an Operations and Maintenance Area must also be followed.

The following locations at the World Trade Center are defined as Priority Areas: the northwest corner of the B-2 Level Parking Lot and the northwest corner of the B-4 Level Parking Lot. In addition, all areas in Zone One, One World Trade Center, which did not have the fire safety sprinkler system installed because of the presence of ACM should be considered a Priority Area.

Operations and Maintenance

This type of asbestos condition is frequently found where the ACM is installed in a location that is not directly accessible to employees or the public. However, for operational or maintenance purposes, employees may be required to work in close proximity and thereby increase the risk of disturbance to the asbestos. In these areas, workers and building occupants must be alerted to the location of the ACM as applicable, and personnel must be trained in proper cleaning, maintenance, repairs, and renovations. All such areas must be periodically reinspected by the facility.

Based upon our investigation, it has been determined that the Mechanical Equipment rooms where asbestos containing fireproofing and pipe insulation has been identified fall under the category of Operations and Maintenance. In addition, all other World Trade Center areas where asbestos containing sprayed-on fireproofing has been identified (see Summary Tables which follow) also fall under the category of Operations and Maintenance.

Controlled Condition

Routine monitoring should be performed when asbestos material is found to be in a Controlled Condition, i.e., when the potential for disturbance is remote (e.g. asbestos within a steel fire floor, most asbestos vinyl tile installations, completely encased ACM, etc.). This type of condition often involves nonfriable material or friable material that is inaccessible under normal circumstances. Reinspection in a Controlled Condition Area is less important than for Operations and Maintenance Areas, however should be performed periodically by the facility to insure the continuity of the controlled condition.

The following locations at the World Trade Center are defined as Controlled Areas: all vinyl floor tiles containing asbestos material, the steel doors containing asbestos fireproofing, and all structurally contained ACM areas. A local exhaust ventilation and collection system equipped with a HEPA (High Efficiency Particulate Absolute) filtration unit designed and operated to capture particulate asbestos material produced by the stripping, cutting or disturbing of asbestos containing materials shall be utilized when work is performed in these areas.

A summary table of all areas and their respective risk assessment ratings immediately follows this memo.

The United States Customs House (Building Six) was surveyed and sampled by an outside consulting firm in accordance with the U.S. General Services Administration Contract. We have secured a copy of the consultant's report on Building Six and it reveals that there are various locations which contain ACM. Although somewhat concerned about the limited number of samples taken by the U.S. Customs consultant, we have nevertheless passed this report along to World Trade Center staff for their edification.

We have consulted, and will continue to consult, with World Trade Center staff on all aspects of the asbestos control program. It is also important to maintain a continuing awareness that any operations and maintenance or construction activity that may disturb ACM shall be carried out in a manner which assures the safety of employees, the public, and the environment in accordance with applicable regulations as well as Port Authority specifications.

The attached report describes conditions as observed at the time and date of the investigation. Physical conditions in some areas may have since changed, thereby altering the attached report. Prior to the development of any abatement plan or control procedure(s), those areas should be visually inspected to determine actual conditions.

A statistical analysis has been completed to establish numbers of samples required per floor to obtain a statistically significant determination and to verify the findings of the survey.

We would like to extend our thanks for the excellent cooperation we have received from the World Trade Center Operations and Maintenance staff. In particular, we acknowledge the outstanding assistance provided by Mr. Frank Boyce and Mr. Jeff Pearse during this investigation.

We will continue to provide further assistance on asbestos related matters. Should you have any questions regarding these findings, please call me at PATHside (201) 963-7476.

Harry R. Pool, Jr., Acting Manager
Environmental Management Division

AN/wgo
Att.



ASBESTOS INVESTIGATION AND ANALYSIS REPORT
WORLD TRADE CENTER
VOLUME I OF II

ENVIRONMENTAL MANAGEMENT DIVISION
MARCH 21, 1988

PA0001288

HD00044200

A prioritization system has been developed which will inform the facility as to those areas requiring an Immediate Response. In addition, this system will rate other locations as Priority, Operations and Maintenance, Controlled Condition, or free of asbestos materials (ACM free). The categorization of all surveyed areas and the definitions used in the risk assessment are as follows:

Immediate Response Condition

An Immediate Response Condition (IRC) exists if there is an unavoidable risk potential due to the disturbance of asbestos fallout material within a specific area, which includes evidence of asbestos material separated from initial installation, deteriorated condition of existing asbestos material, high risk of contact, or the possibility of causing unacceptable levels of airborne asbestos fibers in areas frequented by employees and/or patrons. Air sampling should be initiated in all areas rated as IRC (Immediate Response Condition). Redesignation of these locations should take place after the Immediate Response has been completed.

The following locations at the World Trade Center are defined as IRC: the roofs of elevator cars in Tower One within the shafts where delamination has occurred and the B-6 Level Mechanical Room which has fallout material present in one localized area.

World Trade Center management has been briefed on these conditions and provided with a list of specific locations. In addition, the World Trade Center has requested the Inspection and Safety Division to employ the cleanup and disposal call-in contractor to assist in cleaning these areas. A regular monitoring program to detect similar fallout materials in the future should also be initiated.

After receiving immediate notification from the Inspection and Safety Division, the facility responded by initiating and carrying out cleanup and repair activities utilizing the services of licensed asbestos contracting firms to alleviate those conditions existing as IRC designated locations.

These efforts have resulted in the reclassification of the following IRC areas:

Location	Site	Reclassification
Roofs of elevator cars within the shafts.	1 WTC	Operations & Maintenance
B-6 level mechanical equipment room.	1 WTC	Operations & Maintenance

Priority Area

In order for a location to be designated a Priority Area, the asbestos material must be in disrepair or accessible to the extent that worker activity, or other forces, could produce an increase in the level of airborne

asbestos fibers. As with an IRC, Priority Areas should receive air sampling as an additional input for the risk assessment analysis. Periodic re-inspection of conditions in a Priority Area is mandatory. Once a Priority Area is identified by the Inspection and Safety Division, the facility must institute the appropriate measures. All aspects of an Operations and Maintenance Area must also be followed.

The following locations at the World Trade Center are defined as Priority Areas: the northwest corner of the B-2 Level Parking Lot and the northwest corner of the B-4 Level Parking Lot. In addition, all areas in Zone One, One World Trade Center, which did not have the fire safety sprinkler system installed because of the presence of ACM should be considered a Priority Area.

Operations and Maintenance

This type of asbestos condition is frequently found where the ACM is installed in a location that is not directly accessible to employees or the public. However, for operational or maintenance purposes, employees may be required to work in close proximity and thereby increase the risk of disturbance to the asbestos. In these areas, workers and building occupants must be alerted to the location of the ACM as applicable, and personnel must be trained in proper cleaning, maintenance, repairs, and renovations. All such areas must be periodically reinspected by the facility.

Based upon our investigation, it has been determined that the Mechanical Equipment rooms where asbestos containing fireproofing and pipe insulation has been identified fall under the category of Operations and Maintenance. In addition, all other World Trade Center areas where asbestos containing sprayed-on fireproofing has been identified (see Summary Tables which follow) also fall under the category of Operations and Maintenance.

Controlled Condition

Routine monitoring should be performed when asbestos material is found to be in a Controlled Condition, i.e., when the potential for disturbance is remote (e.g. asbestos within a steel fire floor, most asbestos vinyl tile installations, completely encased ACM, etc.). This type of condition often involves nonfriable material or friable material that is inaccessible under normal circumstances. Reinspection in a Controlled Condition Area is less important than for Operations and Maintenance Areas, however should be performed periodically by the facility to insure the continuity of the controlled condition.

The following locations at the World Trade Center are defined as Controlled Areas: all vinyl floor tiles containing asbestos material, the steel doors containing asbestos fireproofing, and all structurally contained ACM areas. A local exhaust ventilation and collection system equipped with a HEPA (High Efficiency Particulate Absolute) filtration unit designed and operated to capture particulate asbestos material produced by the stripping, cutting or disturbing of asbestos containing materials shall be utilized when work is performed in these areas.

A summary table of all areas and their respective risk assessment ratings immediately follows this memo.

The United States Customs House (Building Six) was surveyed and sampled by an outside consulting firm in accordance with the U.S. General Services Administration Contract. We have secured a copy of the consultant's report on Building Six and it reveals that there are various locations which contain ACM. Although somewhat concerned about the limited number of samples taken by the U.S. Customs consultant, we have nevertheless passed this report along to World Trade Center staff for their edification.

We have consulted, and will continue to consult, with World Trade Center staff on all aspects of the asbestos control program. It is also important to maintain a continuing awareness that any operations and maintenance or construction activity that may disturb ACM shall be carried out in a manner which assures the safety of employees, the public, and the environment in accordance with applicable regulations as well as Port Authority specifications.

The attached report describes conditions as observed at the time and date of the investigation. Physical conditions in some areas may have since changed, thereby altering the attached report. Prior to the development of any abatement plan or control procedure(s), those areas should be visually inspected to determine actual conditions.

A statistical analysis has been completed to establish numbers of samples required per floor to obtain a statistically significant determination and to verify the findings of the survey.

We would like to extend our thanks for the excellent cooperation we have received from the World Trade Center Operations and Maintenance staff. In particular, we acknowledge the outstanding assistance provided by Mr. Frank Boyce and Mr. Jeff Pearse during this investigation.

We will continue to provide further assistance on asbestos related matters. Should you have any questions regarding these findings, please call me at PATHside (201) 963-7476.

Harry R. Pool, Jr., Acting Manager
Environmental Management Division

AN/wgo
Att.

PA0001292

HD00044204

WORLD TRADE CENTER

BUILDING ONE

SUMMARY TABLE

IMMEDIATE RESPONSE CONDITION AREA	PRIORITY AREA	OPERATIONS MAINTENANCE AREA	NON-ACM AREA
* None	B 2 NW corner	Floors:	Floors:
	B 2 NW corner	32 & 39	43-47
		41/42	49-73
	Floors:	48	77-81
	1 - 31	74	84-103
	33 - 37	75/76 MER	105 & 106
	40	82,83	108/109
		104	B3, B4 & B5
		107	
		B-1	
		B-2	
		B-6	
		Elevator shafts:	Elevator shafts:
		01 - 68	69 - 71
		72 - 74	75 - 98
		Elevator pits:	Elevator pits:
		01 - 47	6,7
		01 - 05	
		08 - 47	

* The IRC areas: Elevator car tops and B-6 MER have been reclassified as Operations and Maintenance areas.

WORLD TRADE CENTER

BUILDING TWO

SUMMARY TABLE

IMMEDIATE RESPONSE CONDITION AREA	PRIORITY AREA	OPERATIONS MAINTENANCE AREA	NON-ACM AREA
None	None	Floors: 1,6 7/8 MER 10 - 13 26 32 & 33 40 41/42 MER 43 74 75/76 MER B2 B5/B6 MER	Floors: 2 - 5 9 14 - 25 27 - 31 34 - 39 44 - 73 77 - 110 B1 B3 & B4
		Elevator shafts: 03 - 05 10 & 11 14 & 15 24 - 50 54 - 59 66 - 68	Elevator shafts: 1 & 2 6 - 9 12 & 13 16 - 23 51 - 53 60 - 65 69 - 98
		Elevator pits: 24 & 25 28 - 48	Elevator pits: 01 - 21 27

PA0001294

WORLD TRADE CENTER

BUILDINGS 3, 4, 5, 6 AND SUB-LEVELS

SUMMARY TABLE

BUILDING NUMBER	IMMEDIATE RESPONSE CONDITION	PRIORITY AREA	OPERATIONS MAINTENANCE AREA	NON-ACM AREA
Three	None	None	None	1, B1
Four	None	None	None	Floors: 2 - 9 B1 & B2
Five	None	None	None 2 5 9 B1	Floors: 3,4 6 - 8 B2 & B4 2
Six	None	None	None	None
Northeast Sub-levels	None	None	None	Floors: Concourse B1 & B2
Southeast Sub-levels	None	None	None	Floors: Concourse B2 & B4
Northwest Sub-Levels	None	None	Floors: B1, B2 & B4	Floors: Concourse B3, B5 & B6
Southwest Sub-Levels	None	None	Floor: B1, B2 & B6	Floors: B5

PA0001295

HD00044207

ASBESTOS INVESTIGATION AND ANALYSIS REPORT

THE WORLD TRADE CENTER

Acting Manager:	Harry R. Pool, Jr.
Project Supervisor:	Joseph Mullen
Laboratory Supervisor:	Austin Krautz
Field Supervisor:	Philip Taylor
Field Inspectors:	Michael Denisen
	John Driscoll
	Mark Jakubek
	Charles Landi
	Ramon Leston
	Richard Lighthiser
	Frank Losagio
	Alfonse Niedermeyer
	Dushyant Patel
	David Platt
	Glenn Small
	Philip Taylor
Laboratory Analysts:	Hans Brown
	Mark Fish
	Austin Krautz
	David W. Platt
Data Base Management:	David W. Platt
	Angel Rios
	Glenn Small
Data Base Entry:	W. Garrett Otte
	Angel Rios
	Glenn Small
Report Preparation:	Michael Denisen
	Andrew Driver
	Ramon Leston
	Richard Lighthiser
	Uday Mehta
	Alfonse Niedermeyer
	Glenn Small
	Philip Taylor

ENVIRONMENTAL MANAGEMENT DIVISION

PA0001296

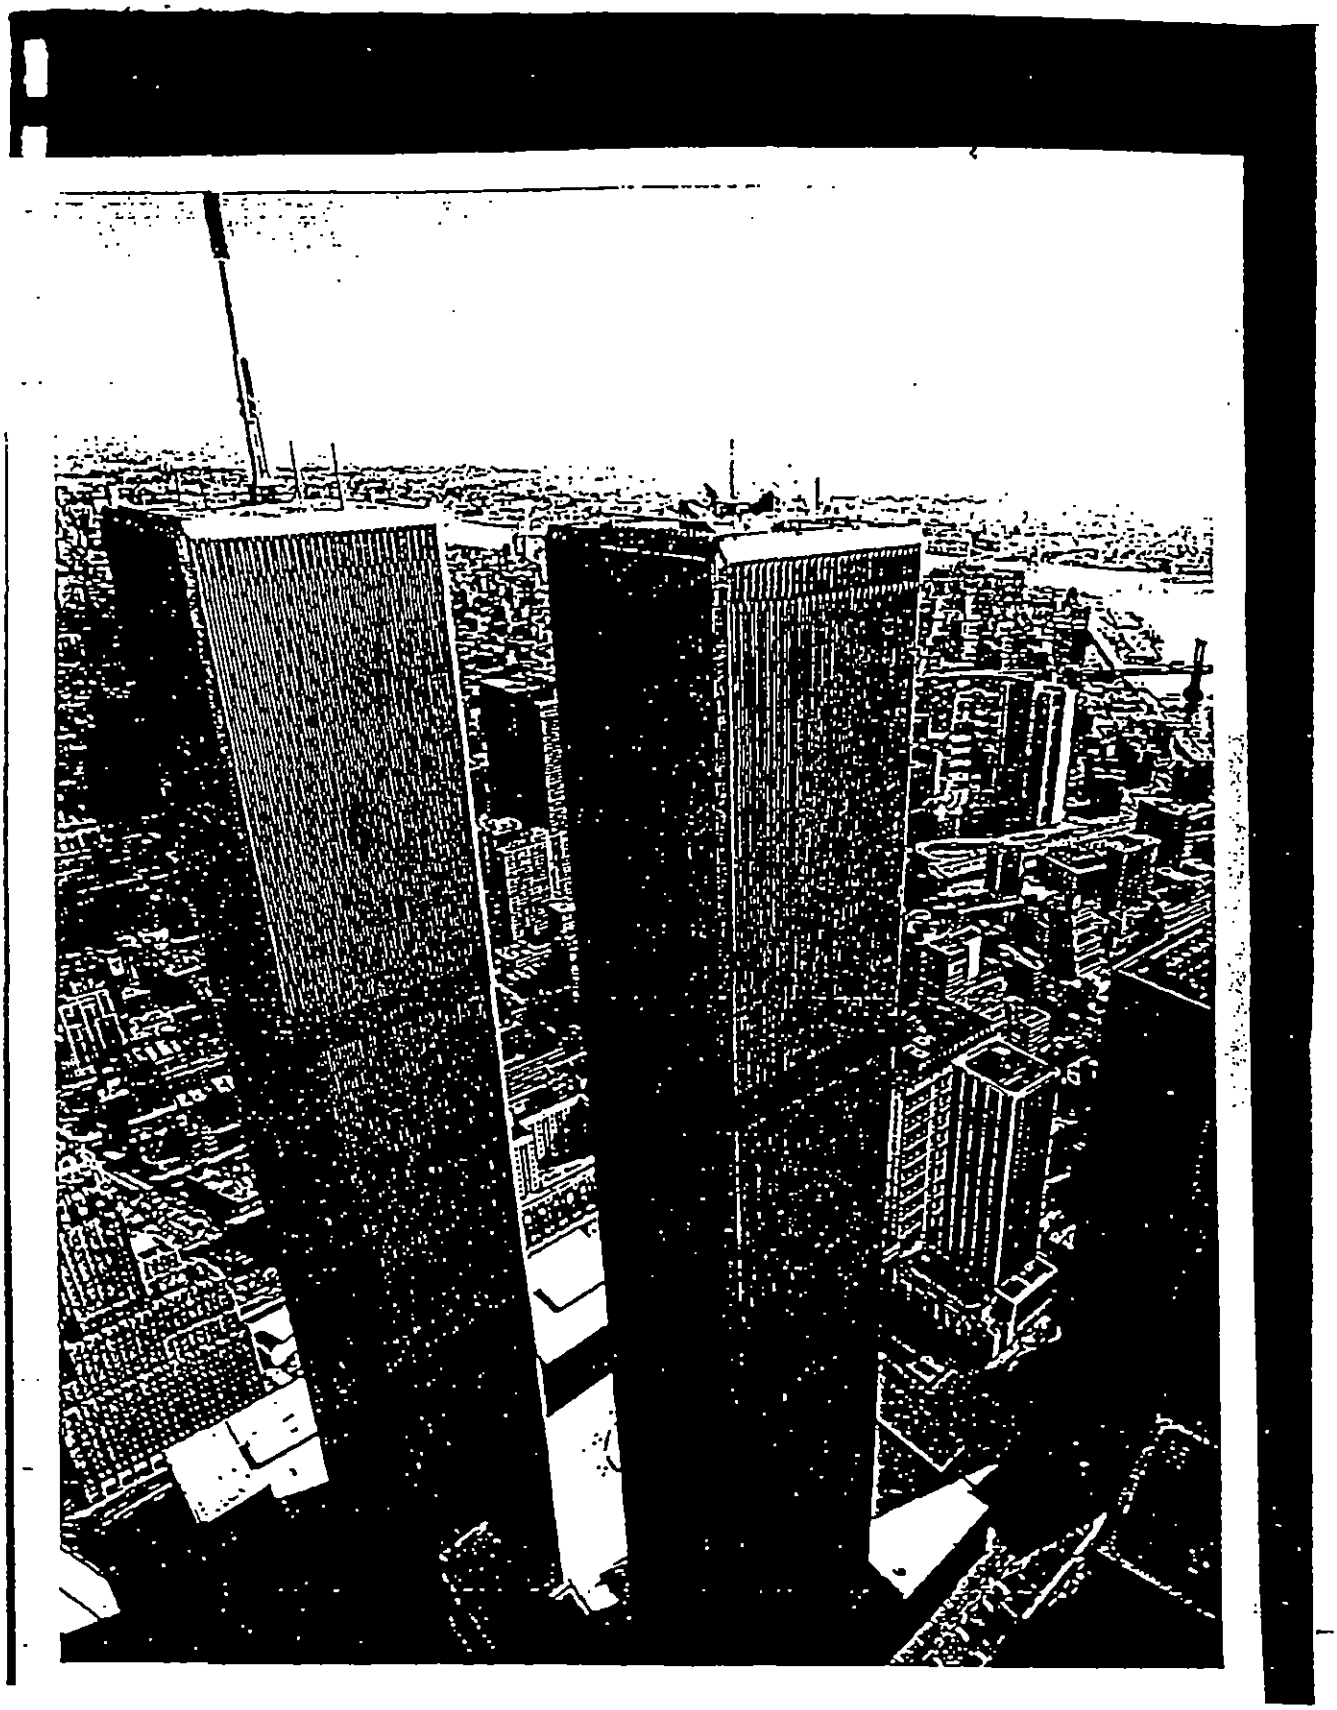

HD00044209

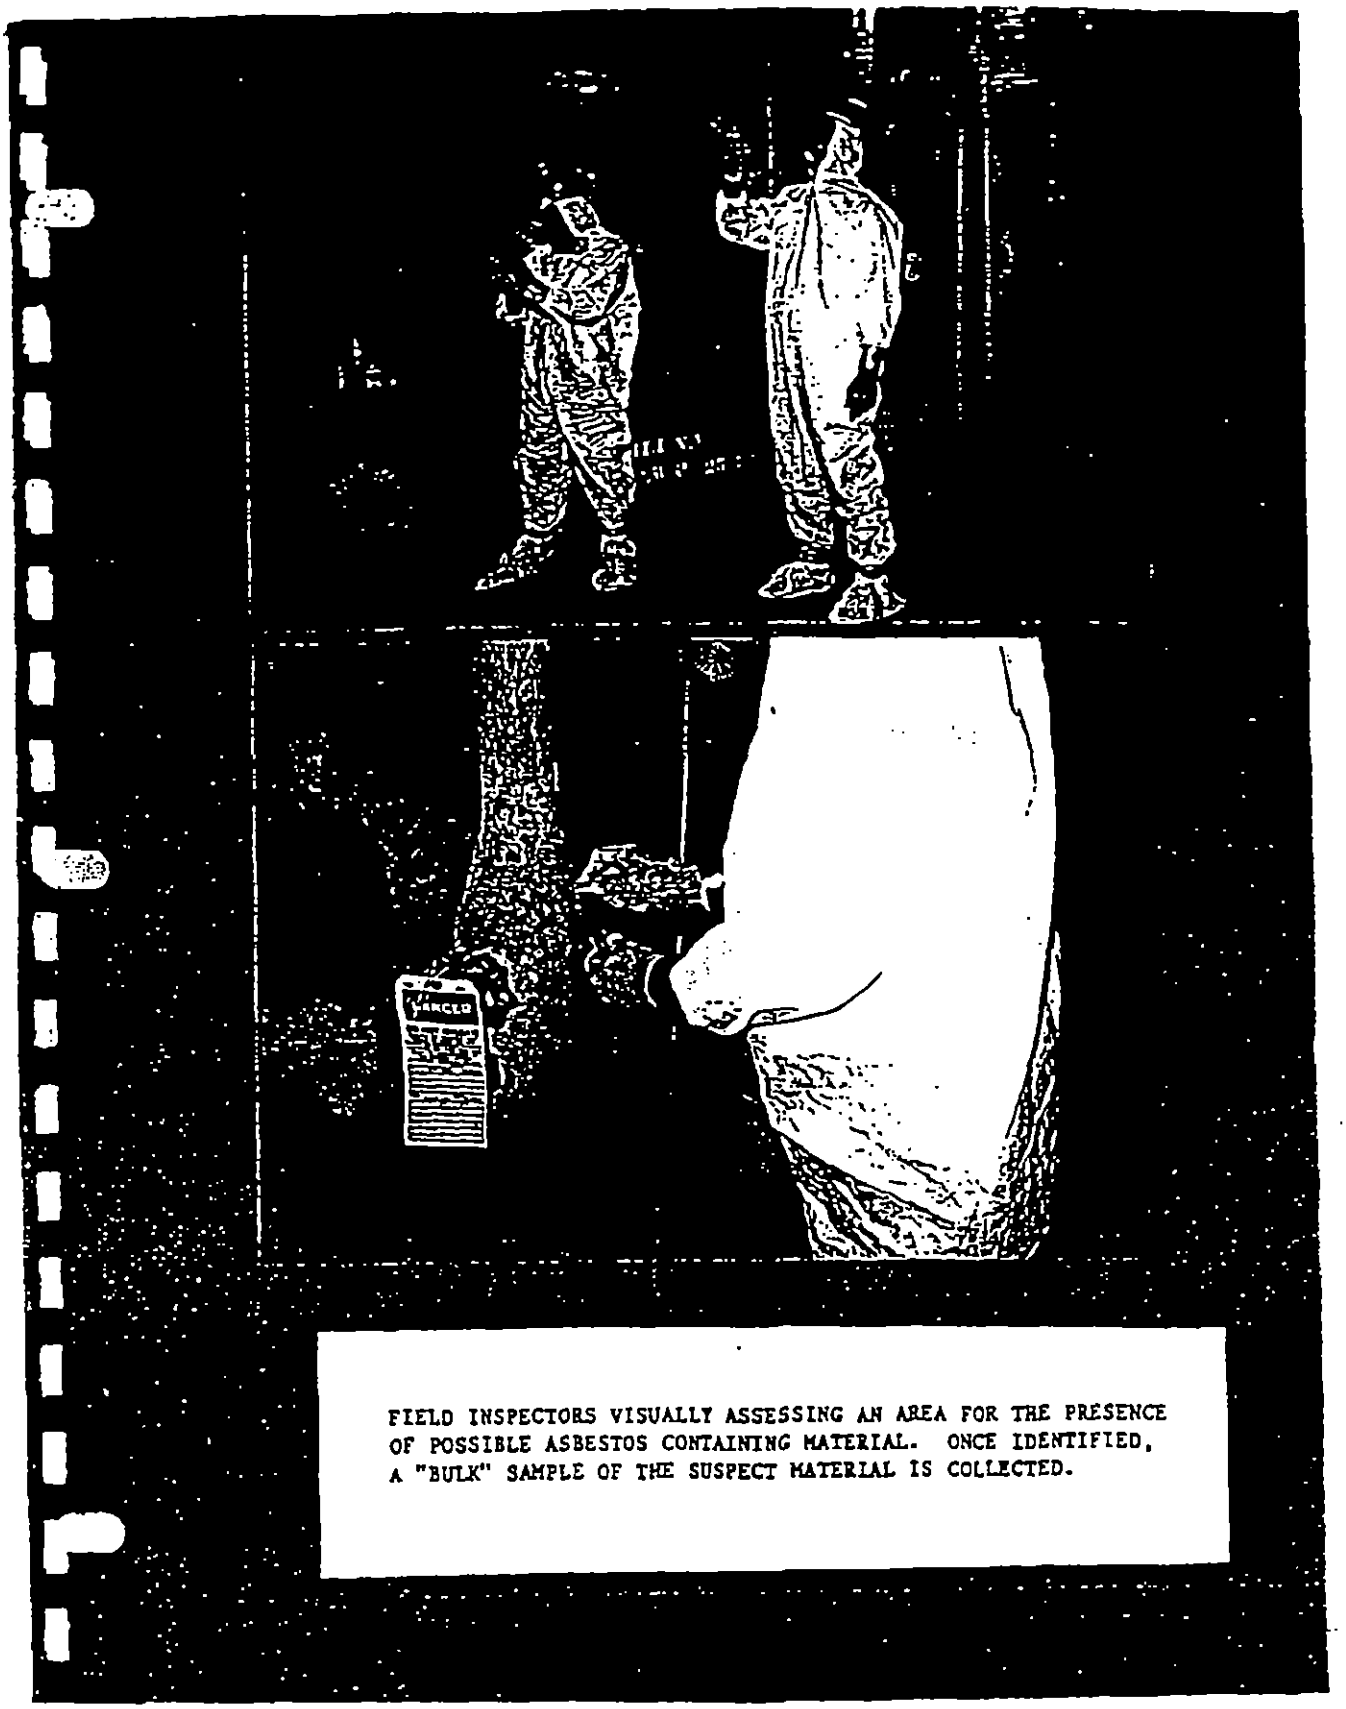

FIELD INSPECTORS VISUALLY ASSESSING AN AREA FOR THE PRESENCE OF POSSIBLE ASBESTOS CONTAINING MATERIAL. ONCE IDENTIFIED, A "BULK" SAMPLE OF THE SUSPECT MATERIAL IS COLLECTED.

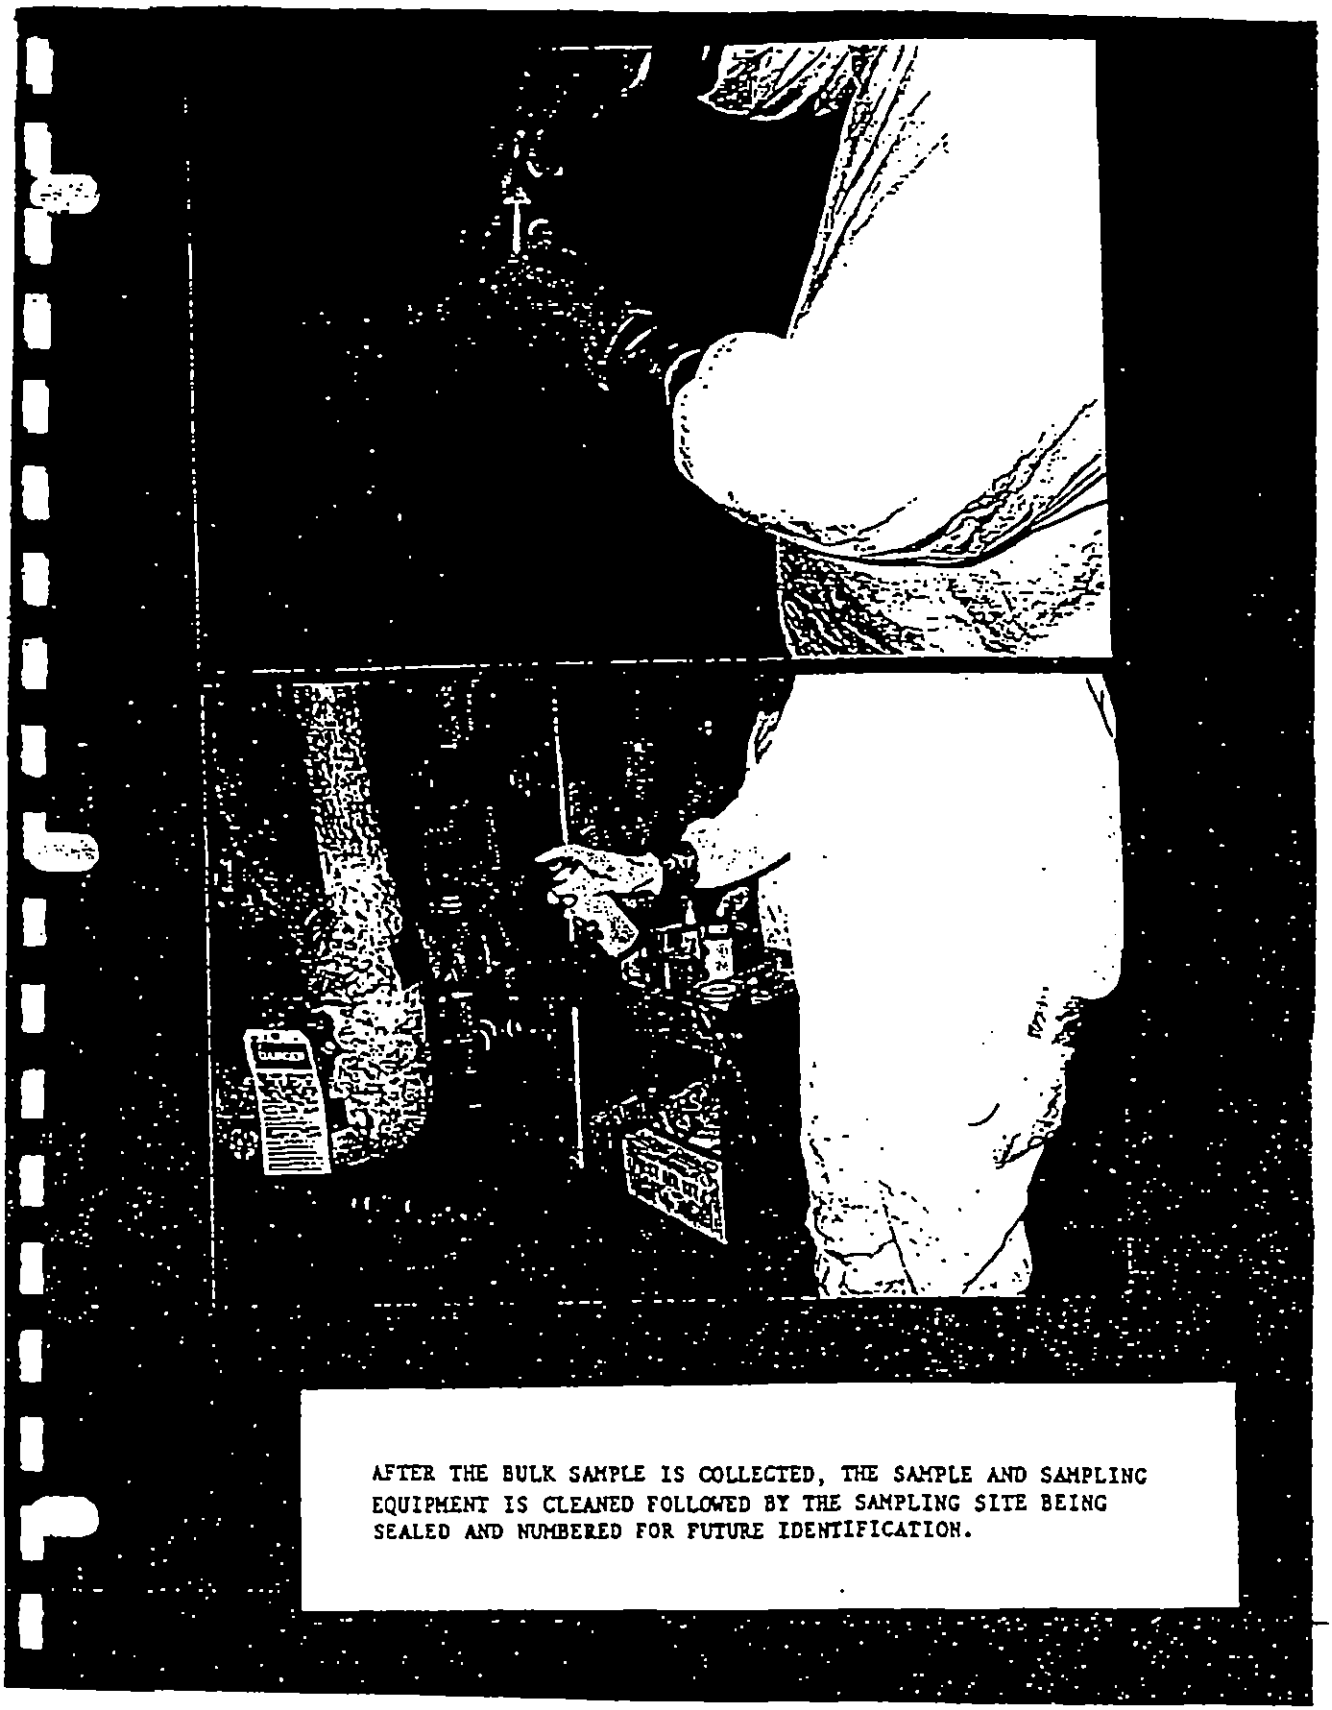

AFTER THE BULK SAMPLE IS COLLECTED, THE SAMPLE AND SAMPLING EQUIPMENT IS CLEANED FOLLOWED BY THE SAMPLING SITE BEING SEALED AND NUMBERED FOR FUTURE IDENTIFICATION.

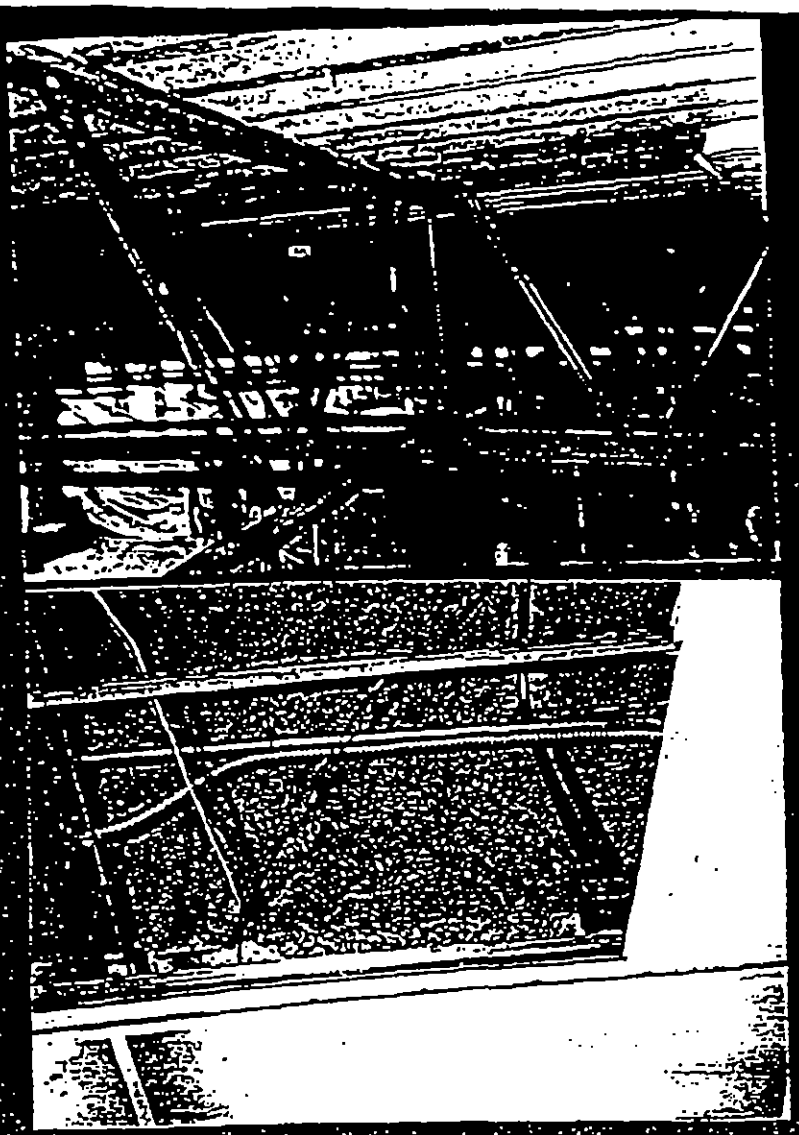

THIS IS A TYPICAL FLOOR SUPPORT SYSTEM WITH JOIST AND METAL DECK COMPONENTS. AS CAN BE OBSERVED, THE TOP PHOTOGRAPH REPRESENTS A FLOOR SYSTEM WITHOUT SPRAYED-ON FIREPROOFING. THE BOTTOM PHOTOGRAPH EXHIBITS THE PHYSICAL CONDITION WITH ENCAPSULATED SPRAYED-ON FIREPROOFING ON A TYPICAL FLOOR.

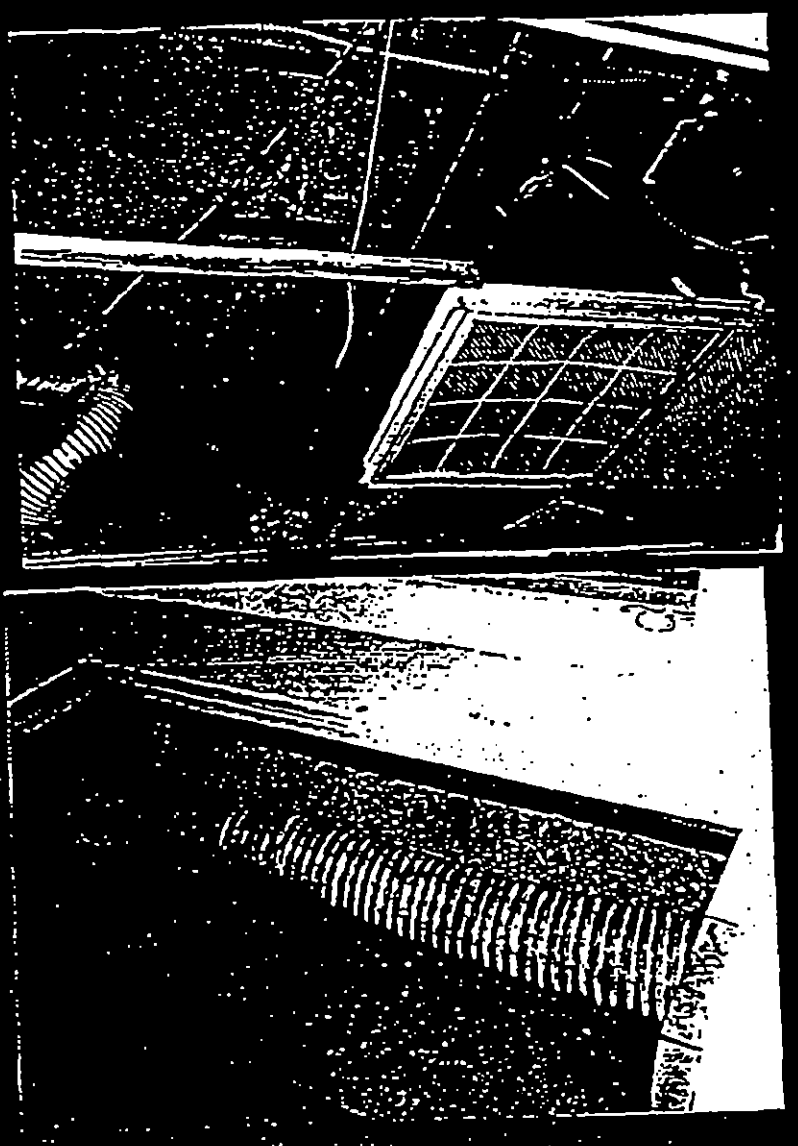

THE TOP PHOTOGRAPH SHOWS A TYPICAL FLOOR SUPPORT SYSTEM WITH SPRAYED-ON FIREPROOFING TO WHICH IS MOUNTED AN AIR HANDLING UNIT. THE BOTTOM PHOTOGRAPH IS A TYPICAL WINDOW CONVECTOR UNIT WITH CEMENTITIOUS FIREPROOFING ON THE EXTERIOR FLOOR BEAMS.

THE FOLLOWING PHOTOGRAPHS REPRESENT VARIOUS MECHANICAL SYSTEMS IN THE EQUIPMENT ROOMS.

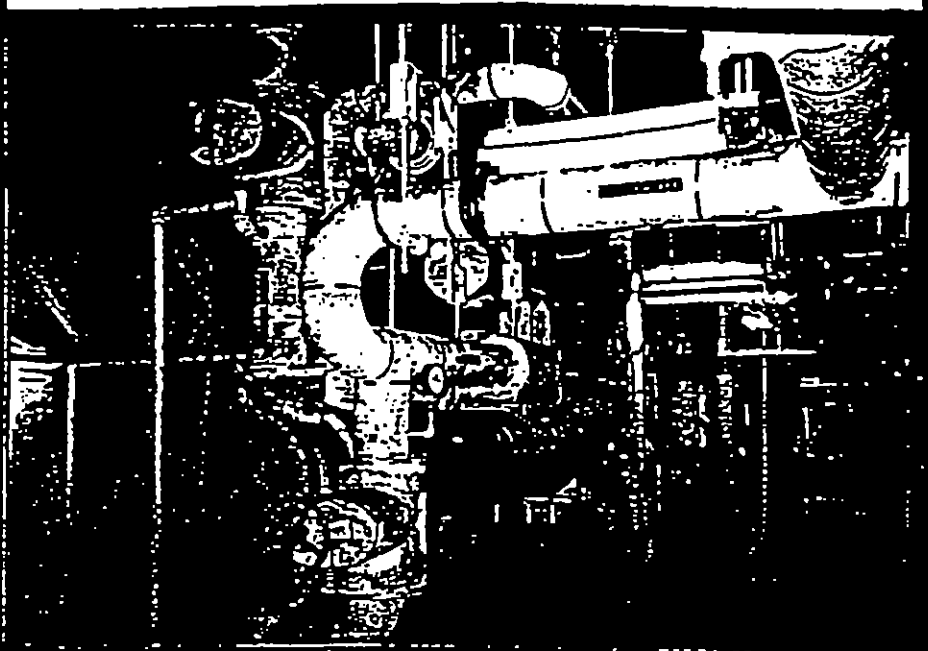

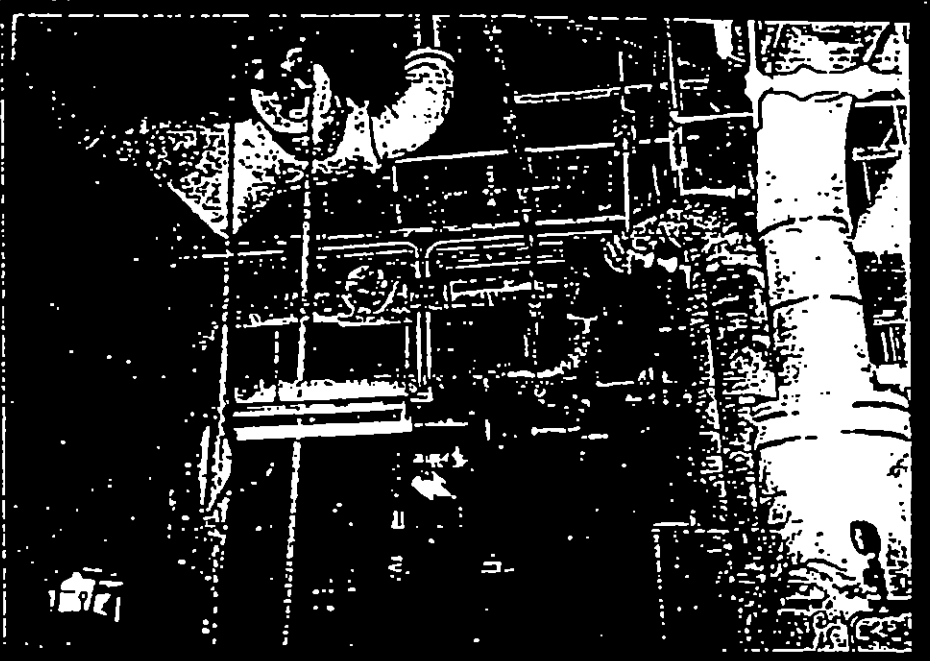

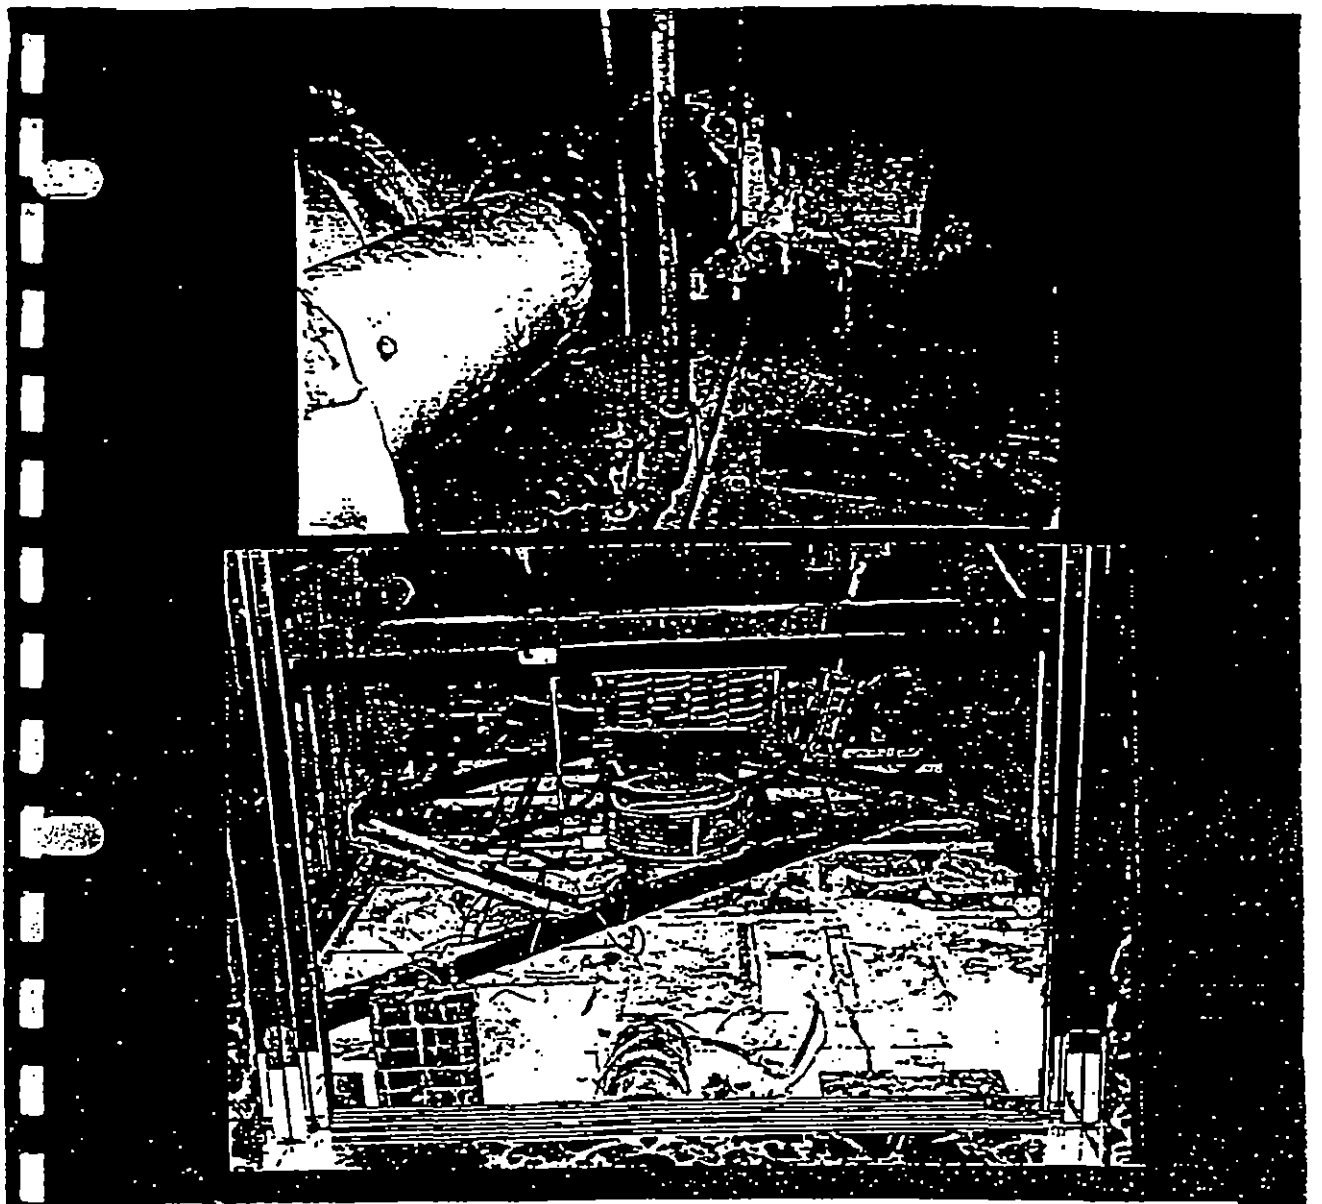

IMMEDIATE RESPONSE CONDITION

AN IMMEDIATE RESPONSE CONDITION EXISTS IF THERE IS AN UNAVOIDABLE RISK POTENTIAL DUE TO THE DISTURBANCE OF ASBESTOS FALLOUT MATERIAL WITHIN A SPECIFIC AREA, WHICH INCLUDES EVIDENCE OF ASBESTOS MATERIAL SEPARATED FROM INITIAL INSTALLATION, DETERIORATED CONDITION OF EXISTING ASBESTOS MATERIAL, HIGH RISK OF CONTACT AND/OR THE POSSIBILITY OF CAUSING UNACCEPTABLE LEVELS OF AIRBORNE ASBESTOS FIBERS IN AREAS FREQUENTED BY EMPLOYEES AND/OR PATRONS. AIR SAMPLING SHALL BE INITIATED IN ALL AREAS RATED AS IRC (IMMEDIATE RESPONSE CONDITION). THE AIR SAMPLING WILL BE CONDUCTED BY THE INSPECTION AND SAFETY DIVISION. REDESIGNATION OF THESE LOCATIONS SHOULD TAKE PLACE AFTER THE IMMEDIATE RESPONSE HAS BEEN COMPLETED.

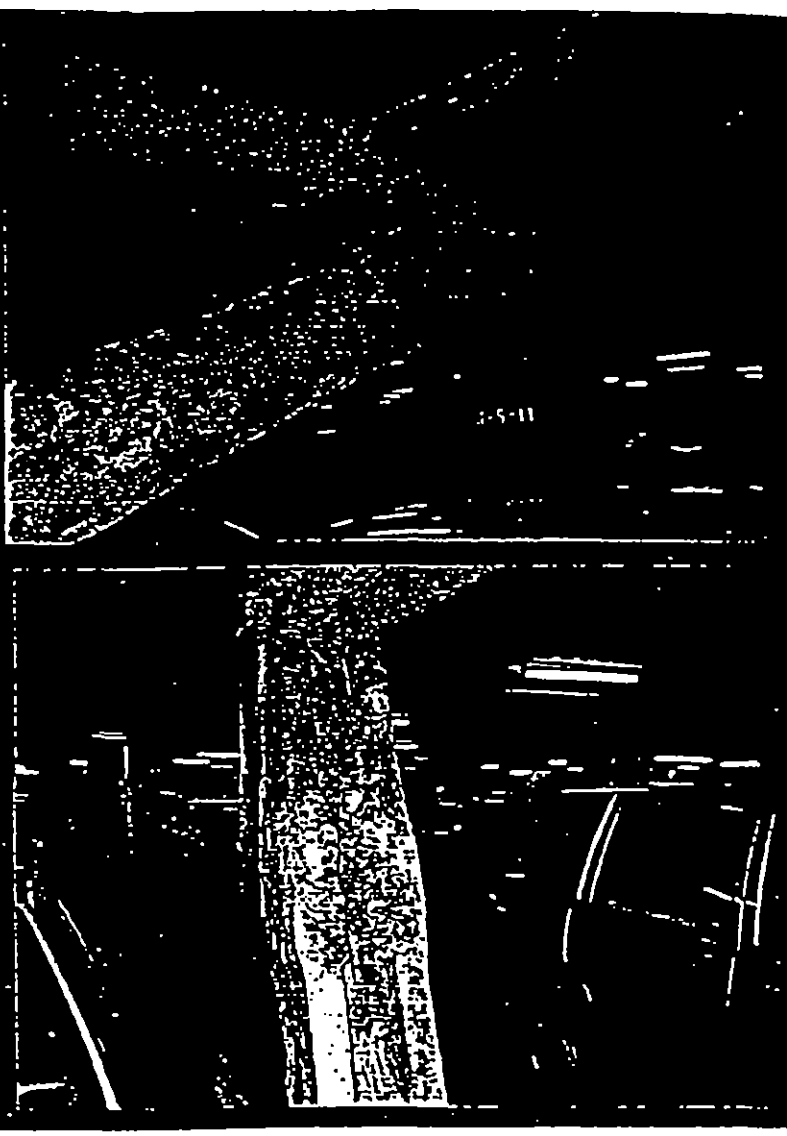

PRIORITY AREA

IN ORDER FOR A LOCATION TO BE DESIGNATED A PRIORITY AREA, THE ASBESTOS MATERIAL MUST BE IN DISREPAIR OR ACCESSIBLE TO THE EXTENT THAT WORKER ACTIVITY OR OTHER FORCES COULD PRODUCE AN INCREASE IN THE LEVEL OF AIRBORNE ASBESTOS FIBERS. AS WITH AN IRC, PRIORITY AREAS SHOULD RECEIVE AIR SAMPLING AS ADDITIONAL INPUT FOR THE RISK ASSESSMENT ANALYSIS. PERIODIC REINSPECTION OF CONDITIONS IN A PRIORITY AREA ARE MANDATORY AND THESE AREAS SHOULD TOP THE LIST OF AREAS THAT WILL RECEIVE REMEDIAL ATTENTION. ONCE A PRIORITY AREA IS IDENTIFIED BY THE INSPECTION AND SAFETY DIVISION THE FACILITY MUST INSTITUTE THE APPROPRIATE MEASURES. ALL ASPECTS OF AN OPERATIONS AND MAINTENANCE AREA MUST ALSO BE FOLLOWED.

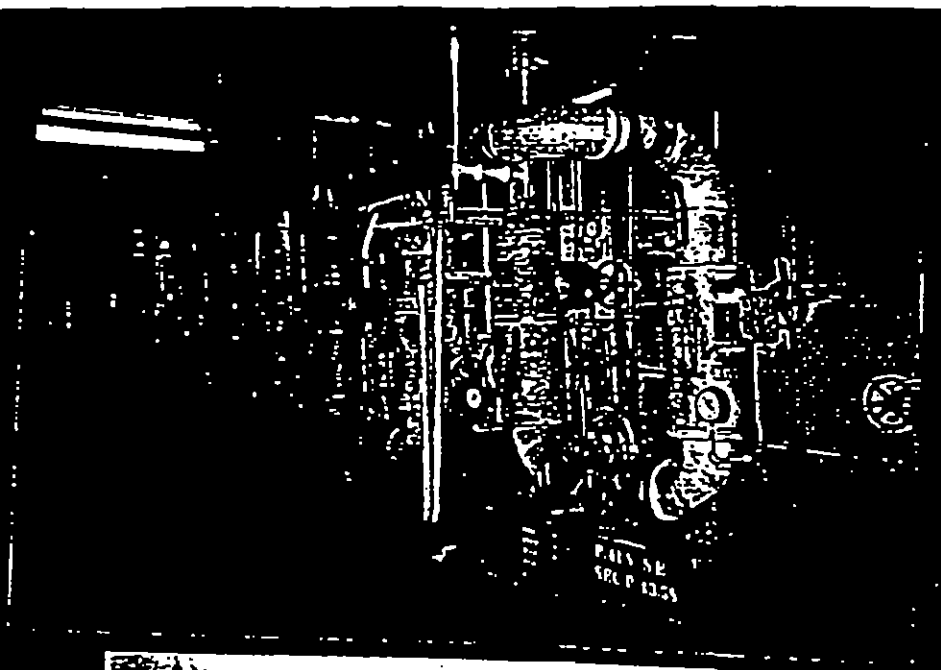

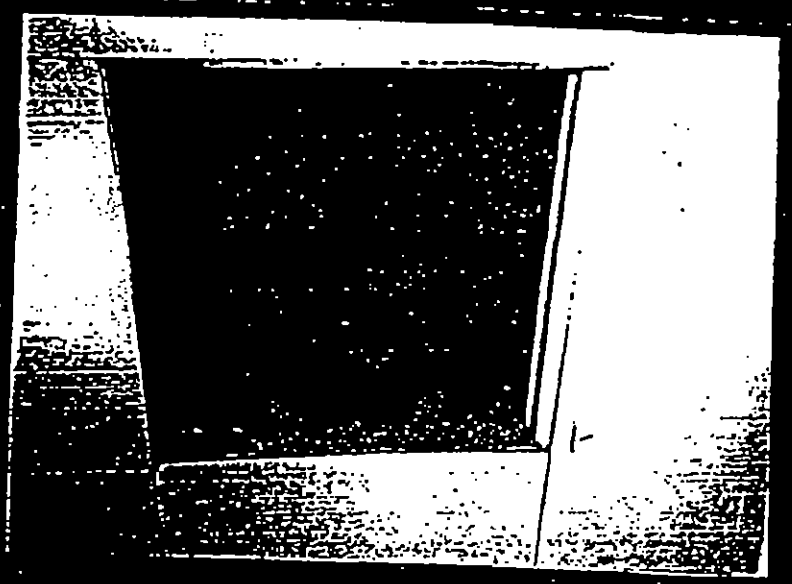

OPERATIONS AND MAINTENANCE AREA

THIS TYPE OF ASBESTOS CONDITION IS FREQUENTLY FOUND WHERE THE ACM IS USUALLY INSTALLED IN A LOCATION THAT IS NOT DIRECTLY ACCESSIBLE TO EMPLOYEES OR THE PUBLIC. HOWEVER, FOR OPERATIONAL OR MAINTENANCE PURPOSES EMPLOYEES MAY BE REQUIRED TO WORK IN CLOSE PROXIMITY AND INCREASE THE RISK OF DISTURBANCE TO THE ASBESTOS. IN THESE AREAS, WORKERS AND BUILDING OCCUPANTS MUST BE ALERTED TO THE LOCATION OF THE ACM AS APPLICABLE; PERSONNEL MUST BE TRAINED IN PROPER CLEANING, MAINTENANCE, REPAIRS, AND RENOVATIONS; AND ALL SUCH AREAS MUST BE PERIODICALLY REINSPECTED BY THE FACILITY.

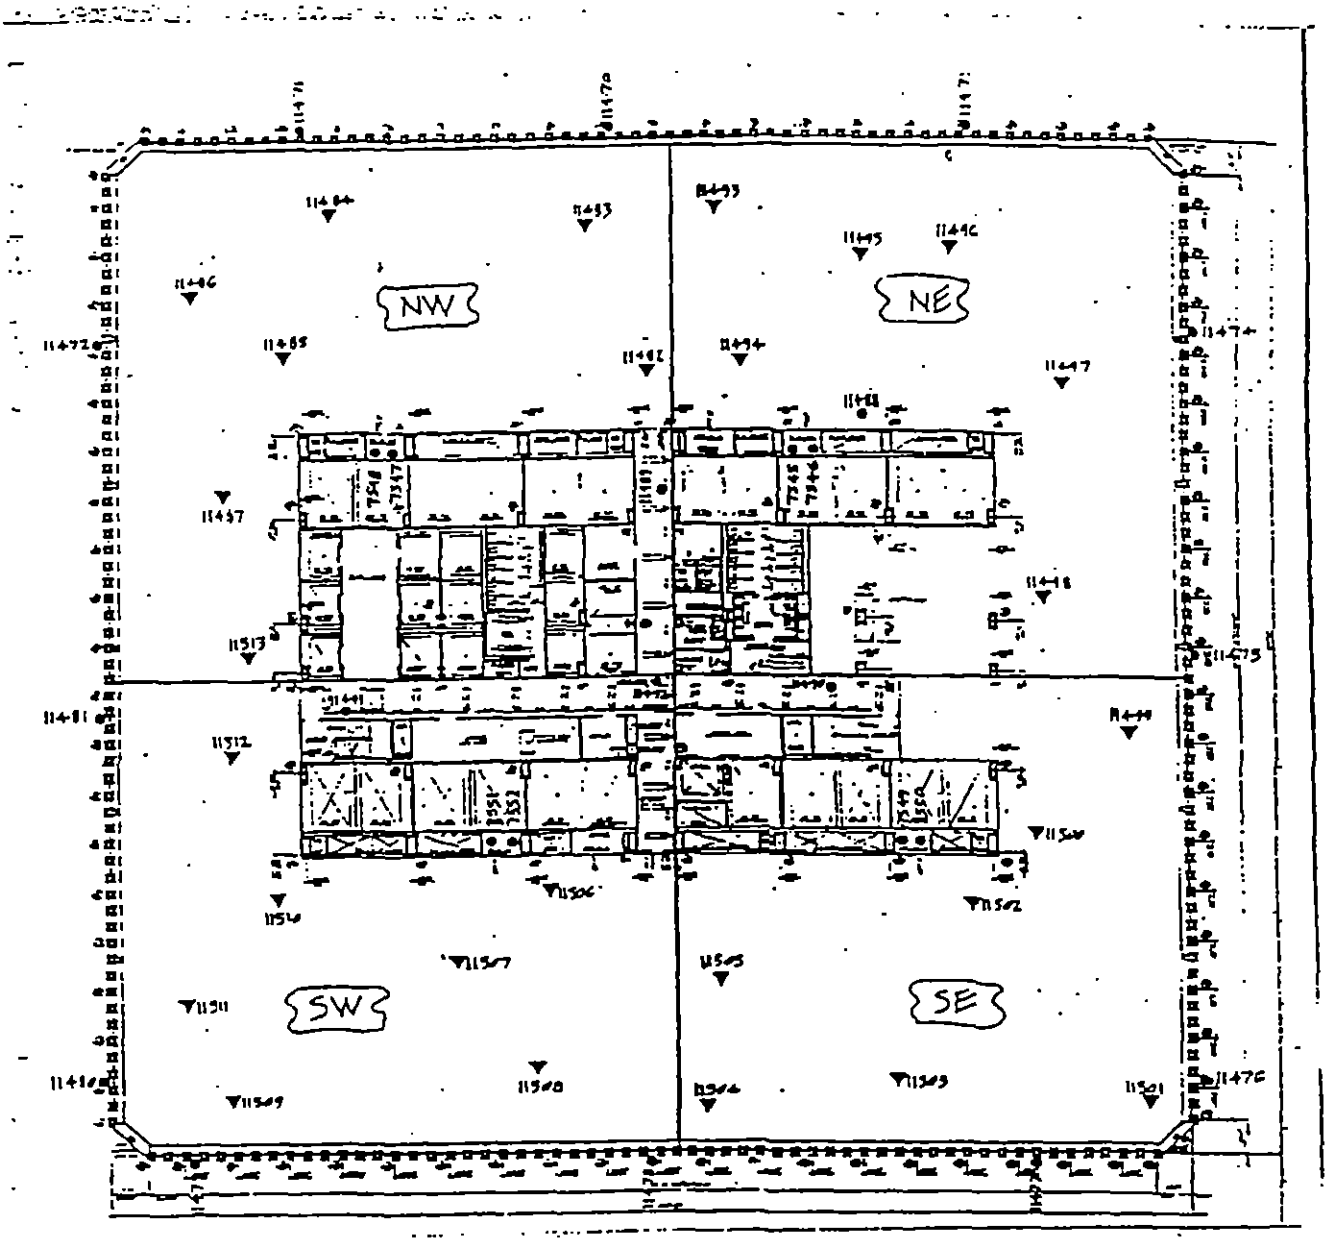

TYPICAL FLOOR PLAN

BUILDING ASBESTOS SURVEY

LEGEND

- ● NON-ASBESTOS MATERIAL
- ▼ ASBESTOS CONTAINING MATERIAL
- ◆ AIR SAMPLING LOCATION

PA0001307

EXPLANATION OF THE DATA REPORT

This report is a collation of a computer generated analysis of the World Trade Center bulk sample database, the results of a statistical analysis of portions of the same database performed by a consultant, and a qualitative interpretation of the data-base by the staff of the Inspection and Safety Division. The following notes describe the format of the data summary and the terms used in the summary.

Format

The report consists of a summary, laboratory procedures and sixteen sections, one for each of the buildings and sub-grade areas. Each of the major sections is further divided into three sub-sections. The first of each sub-section is a list of floors where no asbestos containing material (ACM) was found and the number of samples taken on those floors. The second sub-section is a list of the floors where ACM was found. Included in this sub-section are the number of samples and the number of samples found to contain ACM according to the location of the sample (e.g. ceiling, convector etc.). The last sub-section is a listing of all samples, including location and laboratory result, taken from sampling areas that were found to be positive for ACM.

Definitions

Sample: A single container of material obtained for the purpose of submission to the laboratory for the analysis of the presence, type and proportion of asbestos.

Resample: A sample taken for the purpose of resolving inconclusive or anomalous analytical results from a previous sample.

Sampling area: The location where a sample, or a sample and one or more resamples, were taken.

Positive: A sample or sampling area found to contain greater than one percent asbestos.

Trace: A barely perceivable indication of asbestos that is much less than the USEPA limit for ACM.

Ceiling structures: The metal decking, concrete slab or other structure that is the inside or top covering of a room, opposite the floor, and its supporting beams, trusses and joists.

Piping/HVAC: Any duct, boiler, chiller, heat transfer or other pipe that make up the internal plumbing or heating, ventilation and air-conditioning system.

Convector: The area containing the heat diffuser units along the perimeter of the building.

Fallout: Debris found on horizontal or nearly horizontal surfaces.

Other: Miscellaneous materials such as ceiling tiles, wall board and air-conditioner filters.

Inspection and Safety Division'S Determination: The results of Inspection and Safety Division's qualitative examination of the data on the ceiling structures.

Non-ACM: Floors where all samples from the ceiling structure were found negative, or may have a single positive result with a low percentage of asbestos. Abatement may not be necessary.

Localized Abatement: Floors where the majority of samples were negative for ACM but had a few samples positive for ACM where spot or partial abatement may be advisable.

Full abatement: Floors on which the number of samples testing positive for ACM are high enough to indicate that spot or partial abatement is not advisable.

TABLE OF CONTENTS

VOLUME I

SURVEY AND BULK SAMPLES

World Trade Center Concourse	1
One World Trade Center Floors	4
One World Trade Center Elevator Shafts	131
One World Trade Center Elevator Pits	173

VOLUME II

SURVEY AND BULK SAMPLES - (CONTINUED....)

Two World Trade Center Floors	192
Two World Trade Center Elevator Shafts	281
Two World Trade Center Elevator Pits	304
Three World Trade Center Floors	323
Four World Trade Center Floors	325
Five World Trade Center Floors	328
Six World Trade Center Floors	335
Northeast World Trade Center Sub-levels	337
Northwest World Trade Center Sub-levels	340
Southeast World Trade Center Sub-levels	347
Southwest World Trade Center Sub-levels	349
World Trade Center River Water Pumping Station	357
Summary	358
Laboratory Procedures	386

PA0001310

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
CONCOURSE

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
1	170	170

PA0001311

HD00044223

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
CONCOURSE

FLOOR - 1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	10	0	0	10	0	0
TOTAL	199	170	0	21	7	1

PA0001312

HD00044224

WORLD TRADE CENTER
CONCOURSE

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3447	SWTC-03447	CEMENTITIOUS TROWELED ON DUCT INSULATION MATERIAL ABOVE THE GARBAGE BINS BEHIND THE EAT AND DRINK RESTAURANT.	70% CHRYSOTILE ASBESTOS
3448	SWTC-03448	FLUFFY PREFORMED DUCT PADS INSULATION MATERIAL ABOVE THE GARBAGE BINS BEHIND THE EAT AND DRINK RESTAURANT.	60% CHRYSOTILE ASBESTOS
3449	SWTC-03449	FLUFFY TROWELED ON DUCT INSULATION MATERIAL ABOVE THE RAILING OF THE GARBAGE BIN AREA BEHIND THE EAT AND DRINK RESTAURANT.	75% CHRYSOTILE ASBESTOS
3450	SWTC-03450	FLUFFY PREFORMED DUCT PADS INSULATION MATERIAL ABOVE THE RAILING OF THE GARBAGE BIN AREA BEHIND THE EAT AND DRINK RESTAURANT.	60% CHRYSOTILE ASBESTOS
3454	SWTC-03454	FLUFFY FALLOUT MATERIAL ON TOP OF DUCT OVER STORAGE ROOM BEHIND THE EAT AND DRINK RESTAURANT.	15% CHRYSOTILE ASBESTOS
3455	SWTC-03455	CEMENTITIOUS TROWELED ON DUCT INSULATION MATERIAL ABOVE THE STORAGE ROOM BEHIND THE EAT AND DRINK RESTAURANT.	75% CHRYSOTILE ASBESTOS
3456	SWTC-03456	FLUFFY PREFORMED DUCT PADS INSULATION MATERIAL ABOVE THE STORAGE ROOM BEHIND THE EAT AND DRINK RESTAURANT.	30% CHRYSOTILE ASBESTOS
13397	SWTC-13397	CEMENTITIOUS INSULATION MATERIAL FROM A 3" O.D. HEAT TRANSFER PIPE ELBOW LOCATED NEAR COLUMN 16B OF THE CHESS KING STORE.	65% CHRYSOTILE ASBESTOS
13402	SWTC-13402	CEMENTITIOUS INSULATION MATERIAL FROM A 4" O.D. HEAT TRANSFER PIPE COUPLING LOCATED IN THE CENTER OF THE CHESS KING STORE.	65% CHRYSOTILE ASBESTOS
13406	SWTC-13406	CEMENTITIOUS INSULATION MATERIAL FROM A 5" O.D. HEAT TRANSFER PIPE ELBOW LOCATED AT THE WEST WALL OF THE CHESS KING STORE.	60% CHRYSOTILE ASBESTOS

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
83	3	3
43	35	35
44	35	35
45	48	48
46	28	28
47	29	29
49	36	36
50	41	41
51	44	44
52	32	32
53	32	32
54	57	57
55	40	40
56	32	32
57	43	43
58	32	32
59	32	32
60	32	32
61	40	40
62	44	44
63	32	32
64	31	31
65	47	47
66	42	42
67	47	47
68	41	41
69	31	31
70	43	43
71	38	38
72	68	64
73	50	50
77	32	32
78	41	41
*79	33	33
80	41	41
81	45	45
84	42	42
85	32	32
86	25	25
87	38	38
88	32	32
89	32	32
90	32	32
91	30	30
92	30	30
93	25	25

PA0001314

HD00044226

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
94	31	31
95	32	32
96	37	37
97	32	32
98	32	32
99	32	32
100	45	45
101	33	33
102	60	58
103	32	32
105	40	40
106	54	54
108	51	51
110	7	7

PA0001315

HD00044227

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 91

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	47	44	0	1	1	1
TOTAL	86	58	0	23	1	4

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 82

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	8	6	0	1	1	0
TOTAL	20	9	0	10	1	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 83

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	0	1	0	0
TOTAL	2	0	0	1	0	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 84

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	0	1	0	0
TOTAL	4	0	0	2	1	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 85

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	11	3	0	8	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001316

HD00044228

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 86

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	42	30	0	8	4	0
TOTAL	187	81	0	99	7	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	1	0	2	0	0
TOTAL	11	9	0	2	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	17	17	0	0	0	0
TOTAL	20	20	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 3

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	13	13	0	0	0	0
TOTAL	13	13	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 4

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	10	10	0	0	0	0
TOTAL	12	12	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0001317

HD00044229

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 5

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	9	9	0	0	0	0
TOTAL	12	12	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 6

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	27	27	0	0	0	0
TOTAL	33	33	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 7

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	37	31	0	4	2	0
TOTAL	84	39	0	43	2	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 9

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	7	6	1	0	0	0
TOTAL	16	16	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 10

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	21	21	0	0	0	0
TOTAL	25	23	0	0	2	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0001318

HD00044230

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 11

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	14	14	0	0	0	0
TOTAL	21	21	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 12

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	14	13	1	0	0	1
TOTAL	20	15	1	0	0	4

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 13

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	32	30	2	0	0	0
TOTAL	47	35	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 14

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	14	12	2	0	0	0
TOTAL	19	16	2	0	0	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 15

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	12	12	0	0	0	0
TOTAL	19	16	2	0	0	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0001319

HD00044231

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 16

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	21	21	0	0	0	0
TOTAL	33	28	5	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 17

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	24	24	0	0	0	0
TOTAL	47	35	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 18

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	18	14	1	0	0	1
TOTAL	24	19	1	0	0	4

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 19

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	33	33	0	0	0	0
TOTAL	48	36	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 20

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	9	9	0	0	0	0
TOTAL	21	17	1	0	0	3

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0001320

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 21

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	23	23	0	0	0	0
TOTAL	43	32	8	0	0	3

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 22

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	29	29	0	0	0	0
TOTAL	43	36	5	0	0	2

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 23

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	14	14	0	0	0	0
TOTAL	28	27	0	0	0	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 24

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	40	39	1	0	0	0
TOTAL	58	46	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 25

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	32	32	0	0	0	0
TOTAL	42	40	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0001321

HD00044233

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 26

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	17	15	0	0	0	2
TOTAL	21	20	1	0	0	2

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 27

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	34	34	0	0	0	0
TOTAL	54	42	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 28

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	21	21	0	0	0	0
TOTAL	27	24	0	0	0	3

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 29

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	8	8	0	0	0	0
TOTAL	12	12	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 30

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	27	27	0	0	0	0
TOTAL	52	40	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0001322

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 31

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	31	31	0	0	0	0
TOTAL	55	51	4	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 32

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	29	29	0	0	0	0
TOTAL	147	142	5	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 33

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	13	13	0	0	0	0
TOTAL	64	52	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 34

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	7	7	0	0	0	0
TOTAL	19	18	0	0	0	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 35

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	26	26	0	0	0	0
TOTAL	47	35	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0001323

HD00044235

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 36

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	27	26	1	0	0	0
TOTAL	47	35	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 37

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	39	39	0	0	0	0
TOTAL	97	84	13	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 38

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	2	0	0	0	0
TOTAL	78	67	9	0	0	2

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 39

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	2	0	0	0	0
TOTAL	67	61	6	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 40

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	33	33	0	0	0	0
TOTAL	63	51	7	0	0	3

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0001324

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 41

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	10	3	0	6	1	0
TOTAL	85	30	0	52	2	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 43

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	50	35	12	0	3	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 44

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	0	1	0	0
TOTAL	48	35	12	1	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 45

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	49	48	1	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 46

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	3	0	0
TOTAL	30	28	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001325

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 47

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	30	29	1	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 48

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	8	8	0	0	0	0
TOTAL	77	74	3	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ASATEMENT

FLOOR - 49

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	38	36	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 50

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	53	41	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 51

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	46	44	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001326

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 52

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 53

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 54

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	60	57	3	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 55

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	41	40	1	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 56

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	0	2	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001327

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 57

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	55	43	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 58

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0.	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 59

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 60

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 61

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	42	40	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001328

HD00044240

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 62

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	44	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 63

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	47	32	15	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 64

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	31	31	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 65

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	0	2	0	0	0
TOTAL	67	47	20	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 66

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	42	42	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001329

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 67

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	50	47	3	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 68

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	41	41	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 69

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	31	31	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 70

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	43	43	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 71

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	38	38	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001330

HD00044242

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 72

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	4	4	0	0	0	0
TOTAL	48	48	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 73

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	34	30	4	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 74

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	20	20	0	0	0	0
TOTAL	29	29	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 75

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	18	6	0	10	2	0
TOTAL	90	32	0	41	17	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 77

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	0	2	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001331

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 78

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	53	41	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 79

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	45	33	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 80

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	47	41	6	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 81

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	48	45	2	1	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 82

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	18	18	0	0	0	0
TOTAL	96	96	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

PA0001332

HD00044244

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 83

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	5	5	0	0	0	0
TOTAL	58	56	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 84

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	43	42	1	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 85

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 86

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	25	25	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 87

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	39	38	1	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001333

HD00044245

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 88

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 89

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 90

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 91

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	31	30	1	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 92

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	32	30	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001334

HD00044246

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 93

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	28	25	3	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 94

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	43	31	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 95

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 96

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	33	37	16	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 97

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	0	2	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001335

HD00044247

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 98

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	63	32	11	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 99

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 100

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	57	45	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 101

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	45	33	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 102

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	2	0	0	0	0
TOTAL	60	60	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PAG001336

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 103

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	0	2	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 104

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	16	16	0	0	0	0
TOTAL	85	82	3	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 105

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	44	40	4	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 106

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	66	54	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 107

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	30	25	5	0	0	0
TOTAL	51	39	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0001337

HD00044249

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

FLOOR - 108

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	0	0	3	0	0
TOTAL	95	51	0	35	9	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 110

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	7	7	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0001338

ONE WORLD TRADE CENTER
FLOOR: 51

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
848	1WTC-00848	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM ABOVE THE ENTRANCE TO THE ALLIED OFFICES.	30% CHRYSOTILE ASBESTOS 10% TREMOLITE ASBESTOS
850	1WTC-00850	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE FRONT ALLIED OFFICE.	15% CHRYSOTILE ASBESTOS
851	1WTC-00851	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE REAR ALLIED OFFICE.	10% CHRYSOTILE ASBESTOS
852	1WTC-00852	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A DUCT IN THE PLENUM OF THE REAR ALLIED OFFICE.	10% TREMOLITE ASBESTOS
853	1WTC-00853	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE REAR ALLIED OFFICE.	10% CHRYSOTILE ASBESTOS 5% TREMOLITE ASBESTOS
854	1WTC-00854	FLUFFY INSULATION MATERIAL FROM THE CORE OF A SWINGING DOOR AT THE ENTRANCE TO THE ALLIED OFFICES.	20% AMOSITE ASBESTOS 10% CHRYSOTILE ASBESTOS
856	1WTC-00856	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF THE EAST WALL CORRIDOR.	15% CHRYSOTILE ASBESTOS
857	1WTC-00857	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF THE EAST WALL CORRIDOR.	20% CHRYSOTILE ASBESTOS
858	1WTC-00858	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM LOCATED IN THE PLENUM OF THE EAST WALL CORRIDOR.	15% CHRYSOTILE ASBESTOS
860	1WTC-00860	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF THE EAST WALL CORRIDOR.	25% CHRYSOTILE ASBESTOS
861	1WTC-00861	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF THE EAST WALL CORRIDOR.	25% CHRYSOTILE ASBESTOS
862	1WTC-00862	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF THE EAST WALL CORRIDOR.	20% CHRYSOTILE ASBESTOS
863	1WTC-00863	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF THE EAST WALL CORRIDOR.	25% CHRYSOTILE ASBESTOS
12593	1WTC-12593	FLUFFY SPRAYED ON BEAM INSULATION MATERIAL EXPOSED AT THE NORTH-EAST AREA OF THE PUMP ROOM.	30% CHRYSOTILE ASBESTOS
12595	1WTC-12595	FLUFFY SPRAYED ON BEAM INSULATION MATERIAL EXPOSED AT THE SOUTH-EAST AREA OF THE PUMP ROOM.	30% CHRYSOTILE ASBESTOS
12598	1WTC-12598	FLUFFY SPRAYED ON BEAM INSULATION MATERIAL EXPOSED AT THE SOUTH SIDE OF THE PUMP ROOM.	30% CHRYSOTILE ASBESTOS
12603	1WTC-12603	FLUFFY SPRAYED ON BEAM INSULATION MATERIAL EXPOSED IN THE WEST SIDE AREA OF THE PUMP ROOM.	30% CHRYSOTILE ASBESTOS

PA0001339

HD00044251

ONE WORLD TRADE CENTER
FLOOR: B1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12607	1WTC-12607	FLUFFY SPRAYED ON BEAM INSULATION MATERIAL EXPOSED IN THE NORTH WEST CORNER OF PUMP ROOM.	30% CHRYSOTILE ASBESTOS
12609	1WTC-12609	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE MAIN CORRIDOR AT THE STRUCTURAL SHOP ENTRANCE.	30% CHRYSOTILE ASBESTOS
12610	1WTC-12610	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OF THE STRUCTURAL SHOP.	5% CHRYSOTILE ASBESTOS
12612	1WTC-12612	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE WEST WALL OF THE STRUCTURAL SHOP.	30% CHRYSOTILE ASBESTOS
12615	1WTC-12615	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE CENTER OF THE STRUCTRAL SHOP.	30% CHRYSOTILE ASBESTOS
12617	1WTC-12617	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE NORTH WALL OFTHE STRUCTURAL SHOP.	40% CHRYSOTILE ASBESTOS
12618	1WTC-12618	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED ON THE NORTH WALL OF THE ELECTRICAL SUB- STATION.	25% CHRYSOTILE ASBESTOS
12619	1WTC-12619	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE NORTH WALL OF THE ELECTRICAL SUB-STATION.	25% CHRYSOTILE ASBESTOS
12620	1WTC-12620	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED ON THE EAST WALL OF THE ELECTRICAL SUB-STATION.	25% CHRYSOTILE ASBESTOS
12621	1WTC-12621	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE SOUTH WALL OF THE ELECTRICAL SUB-STATION.	60% CHRYSOTILE ASBESTOS
12622	1WTC-12622	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE SOUTH WALL OF THE ELECTRICAL SUB-STATION.	60% CHRYSOTILE ASBESTOS
12623	1WTC-12623	FLUFFY FALLOUT MATERIAL ON TOP OF THE ELEVATOR DISTRIBUTION PANEL AT THE NORTH WALL OF THE ELECTRICAL SUB-STATION.	60% CHRYSOTILE ASBESTOS
12624	1WTC-12624	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED ABOVE THE P-3 TRANSFORMED UNIT IN THE ELECTRICAL SUB- STATION.	40% CHRYSOTILE ASBESTOS
12625	1WTC-12625	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED ON THE WEST WALL OF THE ELECTRICAL SUB-STATION.	70% CHRYSOTILE ASBESTOS
12626	1WTC-12626	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED ON THE SOUTH WALL OF THE ELECTRICAL SUB- STATION.	70% CHRYSOTILE ASBESTOS
13030	1WTC-13030	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTH EAST CORRIDOR AT THE SOUTH WALL.	35% CHRYSOTILE ASBESTOS
13031	1WTC-13031	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE AIR CONDITIONING FAN ROOM.	30% CHRYSOTILE ASBESTOS

PA0001340

HD00044252

ONE WORLD TRADE CENTER
FLOOR: B1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13053	1WTC-13053	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE AIR CONDITIONING FAN ROOM.	30% CHRYSOTILE ASBESTOS
13055	1WTC-13055	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE AIR CONDITIONING FAN ROOM AT COLUMN 454.	30% CHRYSOTILE ASBESTOS
13057	1WTC-13057	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE SOUTHWEST CORNER OF THE ATTIC STOCKROOM.	30% CHRYSOTILE ASBESTOS
13058	1WTC-13058	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE ATTIC STOCKROOM.	30% CHRYSOTILE ASBESTOS
13061	1WTC-13061	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED EAST OF COLUMN 1101 IN THE ATTIC STOCKROOM.	30% CHRYSOTILE ASBESTOS
13064	1WTC-13064	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED SOUTH OF COLUMN 1104 IN THE STOCKROOM.	30% CHRYSOTILE ASBESTOS
13065	1WTC-13065	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED SOUTH OF COLUMN 1103 IN THE STOCKROOM.	30% CHRYSOTILE ASBESTOS
13066	1WTC-13066	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
13067	1WTC-13067	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	50% AMOSITE ASBESTOS 5% CHRYSOTILE ASBESTOS
13092	1WTC-13092	FLUFFY SPRAYED ON INSULATION MATERIAL TAKEN FROM A BEAM IN THE COMPRESSOR ROOM NEAR THE TRUCK DOCK AREA.	60% CHRYSOTILE ASBESTOS
13366	1WTC-13366	FLUFFY SPRAYED ON INSULATION MATERIAL FROM A BEAM IN THE PLENUM NEAR THE WEST END OF THE MAIN CORRIDOR.	40% CHRYSOTILE ASBESTOS
13367	1WTC-13367	CEMENTITIOUS SPRAYED ON INSULATION MATERIAL TAKEN FROM A BEAM IN THE PLENUM IN FRONT OF ELEVATOR CAR #50.	1-3% CHRYSOTILE ASBESTOS
13368	1WTC-13368	FLUFFY SPRAYED ON INSULATION MATERIAL TAKEN FROM A BEAM IN THE PLENUM OF THE SOUTH MAIN CORRIDOR.	30% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR: 32

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
333	1WTC-00333	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE FOREMAN'S LAVATORY.	25% CHRYSOTILE ASBESTOS
699	1WTC-00699	FLUFFY FALLOUT MATERIAL FROM THE GRID DECKING OF THE STEAM RISER SHAFT CLOSET.	40% AMOSITE ASBESTOS
700	1WTC-00700	CEMENTITIOUS INSULATION MATERIAL FROM AN 8" O.D. HEAT TRANSFER PIPE LOCATED WITHIN THE ELECTRICAL ADMINISTRATION OFFICE.	20% AMOSITE ASBESTOS
769	1WTC-00769	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE MEN'S LAVATORY.	20% CHRYSOTILE ASBESTOS
771	1WTC-00771	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE MEN'S LAVATORY.	25% CHRYSOTILE ASBESTOS
772	1WTC-00772	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE LOCKSMITH SHOP.	10% CHRYSOTILE ASBESTOS
773	1WTC-00773	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE LOCKSMITH SHOP.	10% CHRYSOTILE ASBESTOS
774	1WTC-00774	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE LOCKSMITH SHOP.	20% CHRYSOTILE ASBESTOS

PA0001342

HD00044254

ONE WORLD TRADE CENTER
FLOOR: B3

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
434	1WTC-00434	CEMENTITIOUS INSULATION MATERIAL FROM A MAIN STEAM PIPE IN THE CLOTHING STORAGE AREA IN THE NORTHWEST QUADRANT.	15% AMOSITE ASBESTOS

PA0001343

HD00044255

ONE WORLD TRADE CENTER
FLOOR: 84

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
432	1WTC-CC432	CEMENTITIOUS INSULATION MATERIAL ON A HIGH STEAM PRESSURE PIPE ON THE EAST WALL OF THE STORAGE AREA IN THE NORTHWEST QUADRANT.	15% AMOSITE ASBESTOS

PA0001344

HD00044256

ONE WORLD TRADE CENTER
FLOOR: 84

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
120	1WTC-00120	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE VALVE ON THE STEAM MANIFOLD AT THE EAST WALL.	5% CHRYSOTILE ASBESTOS
121	1WTC-00121	CEMENTITIOUS INSULATION MATERIAL FROM A VERTICAL HEAT TRANSFER PIPE ON THE STEAM MANIFOLD AT THE EAST WALL.	5% CHRYSOTILE ASBESTOS
123	1WTC-00123	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE VALVE ON THE STEAM MANIFOLD AT THE EAST WALL.	5% CHRYSOTILE ASBESTOS
125	1WTC-00125	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE VALVE AT THE NORTH WALL.	5% CHRYSOTILE ASBESTOS
141	1WTC-00141	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM WEST OF COLUMN 601.	5% CHRYSOTILE ASBESTOS
142	1WTC-00142	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM WEST OF COLUMN 701.	5% CHRYSOTILE ASBESTOS
143	1WTC-00143	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EAST OF COLUMN 701.	5% CHRYSOTILE ASBESTOS
144	1WTC-00144	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EAST OF COLUMN 701.	5% CHRYSOTILE ASBESTOS
145	1WTC-00145	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM SOUTH OF COLUMN 602.	5% CHRYSOTILE ASBESTOS
1382	1WTC-01382	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE VS-55-6 UNIT.	15% CHRYSOTILE ASBESTOS
1383	1WTC-01383	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE VS-55-6 UNIT.	20% CHRYSOTILE ASBESTOS
1384	1WTC-01384	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS-55-511 UNIT.	20% CHRYSOTILE ASBESTOS
1385	1WTC-01385	FLUFFY CONCRETE SLAB APPLICATION ABOVE ACS-55-511 UNIT.	25% CHRYSOTILE ASBESTOS
1386	1WTC-01386	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS-55-511 UNIT.	20% CHRYSOTILE ASBESTOS
1389	1WTC-01389	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 55-53 UNIT.	15% CHRYSOTILE ASBESTOS
1390	1WTC-01390	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM ABOVE VS 5-5-5 UNIT.	10% CHRYSOTILE ASBESTOS
1391	1WTC-01391	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE VS 55-4 UNIT.	30% CHRYSOTILE ASBESTOS
1392	1WTC-01392	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE VS 55-4 UNIT.	20% CHRYSOTILE ASBESTOS
1394	1WTC-01394	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE VS-55-3 UNIT.	30% CHRYSOTILE ASBESTOS
1395	1WTC-01395	FLUFFY FALLOUT MATERIAL ON TOP OF DUCT ABOVE ACS 55-1 UNIT.	30% CHRYSOTILE ASBESTOS
1396	1WTC-01396	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 55-1 UNIT.	20% CHRYSOTILE ASBESTOS
1397	1WTC-01397	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE ACS 55-6 UNIT.	15% CHRYSOTILE ASBESTOS

PA0001345

ONE WORLD TRADE CENTER
FLOOR: 36

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1398	1WTC-01398	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE AIR DUCT FROM ACR-33-37 UNIT.	15% CHRYSOTILE ASBESTOS
1399	1WTC-01399	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB ABOVE AIR DUCT FROM ACR-33-37 UNIT.	10% CHRYSOTILE ASBESTOS
1401	1WTC-01401	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE VS-33-37 UNIT AT COLUMN 837.	15% CHRYSOTILE ASBESTOS
1402	1WTC-01402	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE AIR DUCT FROM VS-33-7 UNIT.	15% CHRYSOTILE ASBESTOS
1403	1WTC-01403	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE AIR DUCT FROM VS-33-7 UNIT.	10% CHRYSOTILE ASBESTOS
1404	1WTC-01404	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE VS 3-5-8 UNIT.	30% CHRYSOTILE ASBESTOS
1405	1WTC-01405	FLUFFY FALLOUT INSULATION MATERIAL TAKEN FROM TOP OF VS 3-5-8 UNIT.	5% CHRYSOTILE ASBESTOS
1406	1WTC-01406	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE DUCT FROM VS 3-5-8 UNIT.	15% CHRYSOTILE ASBESTOS
1408	1WTC-01408	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE ROOF OVER PLENUM.	10% CHRYSOTILE ASBESTOS
1409	1WTC-01409	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE DUCT FROM VS-33-9 A, B, C UNIT.	20% CHRYSOTILE ASBESTOS
1410	1WTC-01410	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE VS3-3-9 A, B, C UNIT.	30% CHRYSOTILE ASBESTOS
1412	1WTC-01412	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE VS 33-10 UNIT.	20% CHRYSOTILE ASBESTOS
1413	1WTC-01413	FLUFFY SPRAYED ON AND ENCAPSULATED BEAM INSULATION ABOVE DUCT FROM VS 33 -11.	20% CHRYSOTILE ASBESTOS
1414	1WTC-01414	FLUFFY INSULATION MATERIAL SPRAYED ON AN ENCAPSULATED BEAM ABOVE EXIT OF STAIR K-1.	20% CHRYSOTILE ASBESTOS
1428	1WTC-01428	FLUFFY PRE-MOLDED HEAT TRANSFER PIPE INSULATION FALLOUT ON THE ROOF OF THE AIR TRANSFER PLENUM.	30% AMOSITE ASBESTOS
1429	1WTC-01429	FLUFFY CEMENTITIOUS PRE-MOLDED HEAT TRANSFER PIPE INSULATION FALLOUT ON THE ROOF OF THE AIR TRANSFER PLENUM.	25% AMOSITE ASBESTOS 3% CHRYSOTILE ASBESTOS
1430	1WTC-01430	FLUFFY PRE-MOLDED HEAT TRANSFER PIPE INSULATION FALLOUT ON THE ROOF OF THE AIR TRANSFER PLENUM.	30% AMOSITE ASBESTOS

PA0001346

HD00044258

ONE WORLD TRADE CENTER
FLOOR: 84

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
-043	1WTC-04C43	CLOTH GASKET MATERIAL ON HATCH OF ACS-S3-3 FAN UNIT.	90% CHRYSOTILE ASBESTOS
-067	1WTC-04C67	CLOTH GASKET MATERIAL OF HATCH OF ACS S3-1 FAN UNIT. (47)	80% CHRYSOTILE ASBESTOS
-937	1WTC-04937	FLUFFY PREFORMED PAD INSULATION MATERIAL FROM A 20" O.D. HEAT TRANSFER PIPE AT ACS-S3-2 UNIT.	40% AMOSITE ASBESTOS 10% CHRYSOTILE ASBESTOS

PA0001347

ONE WORLD TRADE CENTER
FLOOR: 1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
964	1WTC-00964	FLUFFY PRE-MOLDED INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED IN THE SLOP SINK CLOSET.	60% CHRYSOTILE ASBESTOS
965	1WTC-00965	FLUFFY PRE-MOLDED INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED IN THE SLOP SINK CLOSET.	60% CHRYSOTILE ASBESTOS
4542	1WTC-04542	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM WEST OF THE CATWALK ENTRANCE IN THE CRAWLSPACE UNDER THE FOUNTAIN.	5% CHRYSOTILE ASBESTOS

PA0001348

HD00044260

ONE WORLD TRADE CENTER
FLOOR: 2

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1453	1WTC-01453	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE NORTHWEST CRAWL SPACE OF ACCESS HATCH.	20% CHRYSOTILE ASBESTOS
1454	1WTC-01454	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE NORTHWEST CRAWL SPACE OF THE ACCESS HATCH.	30% CHRYSOTILE ASBESTOS
1455	1WTC-01455	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE SOUTHWEST CRAWL SPACE OF THE ACCESS HATCH.	30% CHRYSOTILE ASBESTOS
1456	1WTC-01456	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB IN THE SOUTHWEST CRAWL SPACE OF ACCESS HATCH.	30% CHRYSOTILE ASBESTOS
1457	1WTC-01457	FLUFFY INSULATION MATERIAL SPRAYED ON THE EXTERIOR COLUMN EXPOSED IN THE SOUTH PLAZA AREA.	10% CHRYSOTILE ASBESTOS
10867	1WTC-10867	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB IN THE PLENUM OF THE WEST CORE CORRIDOR.	30% CHRYSOTILE ASBESTOS
10868	1WTC-10868	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB IN THE PLENUM OF THE WEST CORE CORRIDOR.	25% CHRYSOTILE ASBESTOS
10869	1WTC-10869	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WEST CORE CORRIDOR.	25% CHRYSOTILE ASBESTOS
10870	1WTC-10870	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WEST CORE CORRIDOR.	5% CHRYSOTILE ASBESTOS
10871	1WTC-10871	FLUFFY SPRAYED ON BEAM INSULATION MATERIAL IN THE PLENUM OF WEST CORRIDOR.	40% CHRYSOTILE ASBESTOS
10872	1WTC-10872	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE ELEVATOR LOBBY.	35% CHRYSOTILE ASBESTOS
10873	1WTC-10873	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE ELEVATOR LOBBY.	30% CHRYSOTILE ASBESTOS
10874	1WTC-10874	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR.	25% CHRYSOTILE ASBESTOS
10875	1WTC-10875	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE ELEVATOR LOBBY.	20% CHRYSOTILE ASBESTOS
10876	1WTC-10876	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR.	40% CHRYSOTILE ASBESTOS
10877	1WTC-10877	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST STAIR VESTIBULE.	60% CHRYSOTILE ASBESTOS
15243	1WTC-15243	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE STORAGE AND ELECTRICAL CLOSET IN THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS

PA0001349

ONE WORLD TRADE CENTER
FLOOR: 3

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10878	1WTC-10878	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF ELEVATOR LOBBY.	30% CHRYSOTILE ASBESTOS
10879	1WTC-10879	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE ELEVATOR LOBBY.	60% CHRYSOTILE ASBESTOS
10880	1WTC-10880	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR.	60% CHRYSOTILE ASBESTOS
10881	1WTC-10881	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB IN THE PLENUM OF THE MENS LOCKER ROOM.	40% CHRYSOTILE ASBESTOS
10882	1WTC-10882	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE MENS LOCKER ROOM.	50% CHRYSOTILE ASBESTOS
10883	1WTC-10883	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF CORRIDOR AT SINK CLOSET.	40% CHRYSOTILE ASBESTOS
10884	1WTC-10884	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTH CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS
10885	1WTC-10885	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE ELEVATOR LOBBY.	50% CHRYSOTILE ASBESTOS
10886	1WTC-10886	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WEST CORE CORRIDOR.	40% CHRYSOTILE ASBESTOS
10887	1WTC-10887	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WOMENS LOCKER ROOM 2.	40% CHRYSOTILE ASBESTOS
10888	1WTC-10888	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WOMENS LOCKER ROOM 2.	40% CHRYSOTILE ASBESTOS
10889	1WTC-10889	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WOMENS LOCKER ROOM 1.	40% CHRYSOTILE ASBESTOS
10890	1WTC-10890	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WOMENS LOCKER ROOM 2.	35% CHRYSOTILE ASBESTOS
10891	1WTC-10891	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WEST CORE CORRIDOR.	30% CHRYSOTILE ASBESTOS
10892	1WTC-10892	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WOMENS ROOM.	40% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR: 4

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10893	1WTC-10893	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTH CORE CORRIDOR.	30% CHRYSOTILE ASBESTOS
10894	1WTC-10894	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE ELEVATOR LOBBY.	33% CHRYSOTILE ASBESTOS
10895	1WTC-10895	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WOMEN'S LOCKER ROOM 2.	40% CHRYSOTILE ASBESTOS
10897	1WTC-10897	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WEST CORE CORRIDOR.	25% CHRYSOTILE ASBESTOS
10898	1WTC-10898	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE ELEVATOR LOBBY.	65% CHRYSOTILE ASBESTOS
10899	1WTC-10899	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE STORAGE ROOM.	40% CHRYSOTILE ASBESTOS
10900	1WTC-10900	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE STORAGE ROOM.	25% CHRYSOTILE ASBESTOS
10901	1WTC-10901	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WOMEN'S LOCKER ROOM 1.	35% CHRYSOTILE ASBESTOS
10903	1WTC-10903	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONRETE SLAB IN THE PLENUM OF THE EAST CORE CORRIDOR.	30% CHRYSOTILE ASBESTOS
10904	1WTC-10904	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE MEN'S LOCKER ROOM 1.	35% CHRYSOTILE ASBESTOS

PA0001351

HD00044263

ONE WORLD TRADE CENTER
FLOOR, 5

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11415	1WTC-11415	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE CENTRAL CORE AREA IN FRONT OF TELEPHONE CLOSET 5.	35% CHRYSOTILE ASBESTOS
11416	1WTC-11416	INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST QUADRANT BETWEEN PASSENGER ELEVATORS #32-33.	40% CHRYSOTILE ASBESTOS
11417	1WTC-11417	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST QUADRANT BETWEEN PASSENGER ELEVATORS #30-31.	45% CHRYSOTILE ASBESTOS
11418	1WTC-11418	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT BETWEEN PASSENGER ELEVATORS #26-27.	30% CHRYSOTILE ASBESTOS
11419	1WTC-11419	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE MEN'S ROOM IN THE SOUTHEAST QUADRANT.	50% CHRYSOTILE ASBESTOS
11420	1WTC-11420	FLUFFY INSULATION MATERIAL IN THE PLENUM OF ZONE 3 CONSTRUCTION IN THE ELEVATORS AT THE CORE CORRIDOR INTERSECTION.	40% CHRYSOTILE ASBESTOS
11422	1WTC-11422	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM IN THE NORTHWEST QUADRANT BETWEEN PASSENGER ELEVATORS #43-44.	30% CHRYSOTILE ASBESTOS
11423	1WTC-11423	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM AT THE END OF THE WEST CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS
11424	1WTC-11424	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT BETWEEN PASSENGER ELEVATORS #38-39.	20% CHRYSOTILE ASBESTOS

PA0001352

HD00044264

ONE WORLD TRADE CENTER
FLOOR: 6

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1	1WTC-001CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHEAST 15	5% CHRYSOTILE ASBESTOS
2	1WTC-002CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHEAST 14.	5% CHRYSOTILE ASBESTOS
3	1WTC-003CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHEAST 8.	5% CHRYSOTILE ASBESTOS
4	1WTC-004CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHEAST 5.	5% CHRYSOTILE ASBESTOS
5	1WTC-005CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHEAST 2.	5% CHRYSOTILE ASBESTOS
6	1WTC-006CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHWEST 6.	5% CHRYSOTILE ASBESTOS
7	1WTC-007CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHWEST 3.	5% CHRYSOTILE ASBESTOS
9	1WTC-009CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHWEST 3.	10% CHRYSOTILE ASBESTOS
10	1WTC-010CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHWEST 12.	10% CHRYSOTILE ASBESTOS
11	1WTC-011CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHWEST 15.	5% CHRYSOTILE ASBESTOS
12	1WTC-012CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHEAST 11.	5% CHRYSOTILE ASBESTOS
13	1WTC-013CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHEAST 14.	5% CHRYSOTILE ASBESTOS
14	1WTC-014CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHEAST 9.	5% CHRYSOTILE ASBESTOS
15	1WTC-015CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHEAST 10.	10% CHRYSOTILE ASBESTOS
16	1WTC-016CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHEAST 7.	5% CHRYSOTILE ASBESTOS
17	1WTC-017CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHWEST 12.	10% CHRYSOTILE ASBESTOS
18	1WTC-018CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER NORTHWEST 13.	10% CHRYSOTILE ASBESTOS

PA0001353

HD00044265

ONE WORLD TRADE CENTER
FLOOR: 6

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
20	1WTC-020CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHWEST 7.	5% CHRYSOTILE ASBESTOS
21	1WTC-021CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHWEST 10.	10% CHRYSOTILE ASBESTOS
22	1WTC-022CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHEAST 5.	5% CHRYSOTILE ASBESTOS
23	1WTC-023CS	FLUFFY INSULATION MATERIAL SPRAYED ON CEILING OVER CHANDELIER SOUTHEAST 8.	20% CHRYSOTILE ASBESTOS
11402	1WTC-11402	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE CORE CORRIDOR INTERSECTION.	10% CHRYSOTILE ASBESTOS
11406	1WTC-11406	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE STAIR NUMBER 3 VESTIBULE AT THE END OF THE WEST CORE CORRIDOR.	25% CHRYSOTILE ASBESTOS
11408	1WTC-11408	FLUFFY INSULATION MATERIAL SPRAYED ON A PIPE IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
11409	1WTC-11409	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE STAIR NUMBER 1 VESTIBULE AT THE END OF THE EAST CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS
11411	1WTC-11411	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM BETWEEN PASSENGER ELEVATOR NUMBER 32 AND 33 IN THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11413	1WTC-11413	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EASTERN CLOSET ALONG THE NORTH CORE CORRIDOR.	30% CHRYSOTILE ASBESTOS TRACE AMOSITE ASBESTOS

PA0001354

HD00044266

ONE WORLD TRADE CENTER
FLOOR: 7

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
549	1WTC-00549	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN THE NORTHWEST RETURN AIR PLENUM.	20% CHRYSOTILE ASBESTOS
550	1WTC-00550	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN THE NORTHWEST RETURN AIR PLENUM.	20% CHRYSOTILE ASBESTOS
551	1WTC-00551	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN THE NORTHWEST RETURN AIR PLENUM.	20% CHRYSOTILE ASBESTOS
552	1WTC-00552	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN THE NORTHWEST RETURN AIR PLENUM.	20% CHRYSOTILE ASBESTOS
561	1WTC-00561	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A WALL IN THE NORTHWEST RETURN AIR PLENUM.	10% CHRYSOTILE ASBESTOS
573	1WTC-00573	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN IN THE SOUTHWEST RETURN AIR PLENUM.	15% CHRYSOTILE ASBESTOS
574	1WTC-00574	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN THE SOUTHWEST RETURN AIR PLENUM.	25% CHRYSOTILE ASBESTOS
575	1WTC-00575	FLUFFY INSULATION MATERIAL TROWELED ON A COLUMN IN THE SOUTHWEST RETURN AIR PLENUM.	1% CHRYSOTILE ASBESTOS
575	1WTC-03178	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN IN THE SOUTHWEST RETURN AIR PLENUM.	3% CHRYSOTILE ASBESTOS
575	1WTC-03179	FLUFFY INSULATION MATERIAL TROWELED ON A COLUMN IN THE SOUTHWEST RETURN AIR PLENUM NEAR SAMPLE #575.	NON ASBESTOS
576	1WTC-00576	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN THE SOUTHWEST RETURN AIR PLENUM.	15% CHRYSOTILE ASBESTOS
578	1WTC-00578	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.8 UNIT.	20% CHRYSOTILE ASBESTOS
579	1WTC-00579	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM ABOVE THE SOUTH ELECTRICAL SUB-STATION.	15% CHRYSOTILE ASBESTOS
580	1WTC-00580	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE SOUTH ELECTRICAL SUB-STATION.	15% CHRYSOTILE ASBESTOS 1% AMOSITE ASBESTOS
581	1WTC-00581	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE SOUTH ELECTRICAL SUB-STATION.	20% CHRYSOTILE ASBESTOS
582	1WTC-00582	FLUFFY FALLOUT MATERIAL FROM THE TOP OF THE DUCT ABOVE THE ACS 7.8 UNIT.	25% CHRYSOTILE ASBESTOS
590	1WTC-00590	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN THE SOUTHEAST CORNER OF THE MECHANICAL EQUIPMENT ROOM.	60% CHRYSOTILE ASBESTOS

PA0001355

ONE WORLD TRADE CENTER
FLOOR: 7

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
602	1WTC-00602	FLUFFY FALLOUT MATERIAL ON THE FLOOR AT THE E-7-20 UNIT.	30% CHRYSOTILE ASBESTOS
603	1WTC-00603	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE NORTH ELECTRICAL SUB-STATION.	40% CHRYSOTILE ASBESTOS
604	1WTC-00604	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE NORTH ELECTRICAL SUB-STATION.	20% CHRYSOTILE ASBESTOS
605	1WTC-00605	CEMENTITIOUS INSULATION MATERIAL FROM A 12" O.D. HEAT TRANSFER PIPE LOCATED IN THE NORTHEAST RETURN AIR PLENUM.	30% AMOSITE ASBESTOS 10% CHRYSOTILE ASBESTOS
606	1WTC-00606	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN THE NORTHEAST RETURN AIR PLENUM.	30% CHRYSOTILE ASBESTOS
608	1WTC-00608	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN THE SOUTHEAST RETURN AIR PLENUM.	20% CHRYSOTILE ASBESTOS
609	1WTC-00609	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN IN FRONT OF THE SOUTHEAST FAN IN THE SOUTHEAST AIR PLENUM.	20% CHRYSOTILE ASBESTOS
2398	1WTC-02398	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE NORTHWEST RETURN AIR PLENUM.	40% CHRYSOTILE ASBESTOS
2399	1WTC-02399	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE NORTHWEST RETURN AIR PLENUM.	40% CHRYSOTILE ASBESTOS 13% AMOSITE ASBESTOS
2402	1WTC-02402	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE COUPLING LOCATED IN THE NORTHWEST RETURN AIR PLENUM.	20% AMOSITE ASBESTOS 5% CHRYSOTILE ASBESTOS
2404	1WTC-02404	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE ELBOW LOCATED IN THE NORTHWEST RETURN AIR PLENUM.	40% AMOSITE ASBESTOS 10% CHRYSOTILE ASBESTOS
2405	1WTC-02405	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANFER PIPE ELBOW LOCATED IN THE NORTHWEST RETURN AIR PLENUM.	40% AMOSITE ASBESTOS 40% CHRYSOTILE ASBESTOS
2406	1WTC-02406	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE NORTHWEST RETURN AIR PLENUM.	20% CHRYSOTILE ASBESTOS
2407	1WTC-02407	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE NORTHWEST RETURN AIR PLENUM.	10% CHRYSOTILE ASBESTOS
2408	1WTC-02408	FLUFFY INSULATION MATERIAL FROM AHEAT TRANSFER PIPE LOCATED IN THE NORTHWEST RETURN AIR PLENUM.	30% AMOSITE ASBESTOS
4529	1WTC-04529	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.11 UNIT.	20% CHRYSOTILE ASBESTOS
4530	1WTC-04530	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACR 7.12 UNIT.	20% CHRYSOTILE ASBESTOS
4531	1WTC-04531	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.13 UNIT.	30% CHRYSOTILE ASBESTOS

PA0001356

HD00044268

ONE WORLD TRADE CENTER
FLOOR: 7

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4331	1WTC-04331	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS-7-1 UNIT.	30% CHRYSOTILE ASBESTOS
4333	1WTC-04333	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS-7-14 UNIT.	30% CHRYSOTILE ASBESTOS
4335	1WTC-04335	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM THE ABOVE ACS-7-3 UNIT.	30% CHRYSOTILE ASBESTOS

PA0001357

HD00044269

ONE WORLD TRADE CENTER
FLOOR: 9

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1150	1WTC-01150	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTH-WEST QUADRANT.	5% CHRYSOTILE ASBESTOS
1156	1WTC-01156	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT.	5% CHRYSOTILE ASBESTOS
1159	1WTC-01159	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1160	1WTC-01160	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1161	1WTC-01161	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1163	1WTC-01163	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST EXPOSED WITHIN THE PLENUM.	10% CHRYSOTILE ASBESTOS
13638	1WTC-13638	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	40% CHRYSOTILE ASBESTOS

PA0001358

ONE WORLD TRADE CENTER
FLOOR: 10

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
431	1WTC-00431	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
433	1WTC-00433	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
434	1WTC-00434	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
435	1WTC-00435	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
436	1WTC-00436	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
437	1WTC-00437	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
438	1WTC-00438	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
439	1WTC-00439	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
440	1WTC-00440	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
441	1WTC-00441	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
442	1WTC-00442	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
443	1WTC-00443	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
444	1WTC-00444	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
445	1WTC-00445	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
446	1WTC-00446	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
447	1WTC-00447	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
448	1WTC-00448	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS

PA0001359

HD00044271

ONE WORLD TRADE CENTER
FLOOR: 10

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
449	1WTC-00449	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
450	1WTC-00450	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
13633	1WTC-13633	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	25% CHRYSOTILE ASBESTOS
13634	1WTC-13634	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	40% CHRYSOTILE ASBESTOS

PA0001360

HD00044272

ONE WORLD TRADE CENTER
FLOOR: 11

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
431	1WTC-00431	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
433	1WTC-00433	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
435	1WTC-00435	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM.	20% CHRYSOTILE ASBESTOS
437	1WTC-00437	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
438	1WTC-00438	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
439	1WTC-00439	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
440	1WTC-00440	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM.	10% CHRYSOTILE ASBESTOS
441	1WTC-00441	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM.	5% CHRYSOTILE ASBESTOS
442	1WTC-00442	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM.	5% CHRYSOTILE ASBESTOS
446	1WTC-00446	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
447	1WTC-00447	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM.	5% CHRYSOTILE ASBESTOS
448	1WTC-00448	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM.	10% CHRYSOTILE ASBESTOS
449	1WTC-00449	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM.	5% CHRYSOTILE ASBESTOS
13441	1WTC-13441	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE TEL NORTHEAST TELEPHONE CLOSET.	35% CHRYSOTILE ASBESTOS

PA0001361

HD00044273

ONE WORLD TRADE CENTER
FLOOR: 32

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1169	1WTC-01169	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
1170	1WTC-01170	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
1171	1WTC-01171	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1172	1WTC-01172	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
1174	1WTC-01174	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1175	1WTC-01175	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
1176	1WTC-01176	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1177	1WTC-01177	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1178	1WTC-01178	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1179	1WTC-01179	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
1180	1WTC-01180	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1183	1WTC-01183	FLOOR TILE SAMPLE TAKEN FROM DEMOLISHED AREA OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
13639	1WTC-13639	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	10% CHRYSOTILE ASBESTOS
13640	1WTC-13640	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	10% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR: 33

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11514	1WTC-11514	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE CORE AREA CORRIDOR OPPOSITE THE PASSENGER ELEVATOR.	5% CHRYSOTILE ASBESTOS
11516	1WTC-11516	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE CORE CORRIDOR INTERSECTION.	10% CHRYSOTILE ASBESTOS
11517	1WTC-11517	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE CORRIDOR AT THE LADIES ROOM ENTRANCE.	20% CHRYSOTILE ASBESTOS
11518	1WTC-11518	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
11519	1WTC-11519	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
11520	1WTC-11520	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
11523	1WTC-11523	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
11524	1WTC-11524	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
11525	1WTC-11525	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	65% CHRYSOTILE ASBESTOS TRACE AMOSITE ASBESTOS
11526	1WTC-11526	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
11527	1WTC-11527	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS TRACE AMOSITE ASBESTOS
11528	1WTC-11528	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
11529	1WTC-11529	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
11530	1WTC-11530	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
11531	1WTC-11531	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11532	1WTC-11532	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
11534	1WTC-11534	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS

PA0001363

ONE WORLD TRADE CENTER
FLOOR: 13

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11335	1WTC-11335	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
11336	1WTC-11336	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
11337	1WTC-11337	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
11338	1WTC-11338	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11339	1WTC-11339	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11340	1WTC-11340	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
11341	1WTC-11341	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
11342	1WTC-11342	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
11343	1WTC-11343	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11344	1WTC-11344	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT	50% CHRYSOTILE ASBESTOS
11345	1WTC-11345	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	50% CHRYSOTILE ASBESTOS
11347	1WTC-11347	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
11350	1WTC-11350	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	3% CHRYSOTILE ASBESTOS
13633	1WTC-13633	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	20% CHRYSOTILE ASBESTOS
13634	1WTC-13634	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	20% CHRYSOTILE ASBESTOS

PA0001364

ONE WORLD TRADE CENTER
FLOOR: 14

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1085	1WTC-01085	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1086	1WTC-01086	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
1087	1WTC-01087	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1088	1WTC-01088	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
1089	1WTC-01089	FLUFFY FALLOUT MATERIAL IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1090	1WTC-01090	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
1091	1WTC-01091	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1092	1WTC-01092	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1093	1WTC-01093	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
1094	1WTC-01094	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1095	1WTC-01095	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1096	1WTC-01096	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1098	1WTC-01098	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
13631	1WTC-13631	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS

PAG001365

HD00044277

ONE WORLD TRADE CENTER
FLOOR: 15

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1070	1WTC-01070	IDENTITICOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	3% CHRYSOTILE ASBESTOS
1072	1WTC-01072	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM IN THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1073	1WTC-01073	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM IN THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1076	1WTC-01076	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM IN THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1077	1WTC-01077	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM IN THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1079	1WTC-01079	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
1080	1WTC-01080	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
1081	1WTC-01081	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1082	1WTC-01082	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1084	1WTC-01084	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
13629	1WTC-13629	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	20% CHRYSOTILE ASBESTOS
13630	1WTC-13630	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	25% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR: 16

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
912	1WTC-00912	FLUFFY FALLOUT MATERIAL IN THE PLENUM OF THE SOUTHEAST QUADRANT	20% CHRYSOTILE ASBESTOS
913	1WTC-00913	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
914	1WTC-00914	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS 5% AMOSITE ASBESTOS
915	1WTC-00915	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
916	1WTC-00916	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
917	1WTC-00917	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
918	1WTC-00918	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
919	1WTC-00919	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
920	1WTC-00920	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
922	1WTC-00922	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
923	1WTC-00923	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
924	1WTC-00924	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
13639	1WTC-13639	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	35% CHRYSOTILE ASBESTOS
13640	1WTC-13640	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	20% CHRYSOTILE ASBESTOS
14900	1WTC-14900	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTH CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS
14913	1WTC-14913	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
14916	1WTC-14916	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS

PA0001367

HD00044279

ONE WORLD TRADE CENTER
FLOOR: 16

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14917	1WTC-14917	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
14918	1WTC-14918	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS TRACE AMOSITE ASBESTOS
14919	1WTC-14919	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
14920	1WTC-14920	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR: 17

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11426	1WTC-11426	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR OUTSIDE OF THE ELEVATOR LOBBY.	30% CHRYSOTILE ASBESTOS
11427	1WTC-11427	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE CORE CORRIDORS INTERSECTION.	40% CHRYSOTILE ASBESTOS
11430	1WTC-11430	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	65% CHRYSOTILE ASBESTOS
11433	1WTC-11433	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11434	1WTC-11434	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	65% CHRYSOTILE ASBESTOS
11435	1WTC-11435	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	50% CHRYSOTILE ASBESTOS
11436	1WTC-11436	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
11437	1WTC-11437	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11441	1WTC-11441	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
11442	1WTC-11442	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11443	1WTC-11443	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
11444	1WTC-11444	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
11445	1WTC-11445	FLUFFY SPRAYED ON INSULATION MATERIAL FROM A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	50% CHRYSOTILE ASBESTOS
11446	1WTC-11446	FLUFFY SPRAYED ON INSULATION MATERIAL FROM A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
11447	1WTC-11447	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
11448	1WTC-11448	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
11449	1WTC-11449	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR: 17

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11430	1WTC-11430	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11431	1WTC-11431	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11432	1WTC-11432	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11433	1WTC-11433	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
11434	1WTC-11434	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	50% CHRYSOTILE ASBESTOS
11437	1WTC-11437	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
13441	1WTC-13441	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE NORTHEAST TELEPHONE CLOSET.	20% CHRYSOTILE ASBESTOS

PA0001370

ONE WORLD TRADE CENTER
FLOOR: 16

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1032	1WTC-01032	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
1033	1WTC-01033	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
1034	1WTC-01034	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	75% CHRYSOTILE ASBESTOS
1036	1WTC-01036	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1037	1WTC-01037	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	50% CHRYSOTILE ASBESTOS
1041	1WTC-01041	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
1042	1WTC-01042	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1043	1WTC-01043	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1044	1WTC-01044	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1045	1WTC-01045	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
1046	1WTC-01046	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1047	1WTC-01047	INTERLOCKING CEILING TILE SAMPLE IN THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1048	1WTC-01048	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
13444	1WTC-13444	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	5% CHRYSOTILE ASBESTOS
14921	1WTC-14921	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTH CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS
14922	1WTC-14922	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS

PA0001371

HD00044283

ONE WORLD TRADE CENTER
FLOOR: 19

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10917	1WTC-10917	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
10918	1WTC-10918	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
10919	1WTC-10919	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.OFFICE AREA.	1-3% CHRYSOTILE ASBESTOS
10920	1WTC-10920	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
10921	1WTC-10921	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	65% CHRYSOTILE ASBESTOS
10922	1WTC-10922	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
10923	1WTC-10923	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
10925	1WTC-10925	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	65% CHRYSOTILE ASBESTOS
10926	1WTC-10926	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	50% CHRYSOTILE ASBESTOS
10927	1WTC-10927	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
10928	1WTC-10928	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
10929	1WTC-10929	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
10930	1WTC-10930	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
10931	1WTC-10931	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
10932	1WTC-10932	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
10933	1WTC-10933	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	50% CHRYSOTILE ASBESTOS
10934	1WTC-10934	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS

PA0001372

HD00044284

ONE WORLD TRADE CENTER
FLOOR: 19

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10935	1WTC-10935	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
10936	1WTC-10936	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
10937	1WTC-10937	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
10938	1WTC-10938	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
10939	1WTC-10939	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
10940	1WTC-10940	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR NEAR THE CLOSET.	10% CHRYSOTILE ASBESTOS
10941	1WTC-10941	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WEST CORE CORRIDOR NEAR THE CLOSET.	50% CHRYSOTILE ASBESTOS
10942	1WTC-10942	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTH CORE CORRIDOR.	25% CHRYSOTILE ASBESTOS
10943	1WTC-10943	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTH CORE CORRIDOR.	25% CHRYSOTILE ASBESTOS
10944	1WTC-10944	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	65% CHRYSOTILE ASBESTOS
10945	1WTC-10945	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
10946	1WTC-10946	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
10947	1WTC-10947	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
10948	1WTC-10948	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	45% CHRYSOTILE ASBESTOS
13643	1WTC-13643	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE NORTHEAST TELEPHONE CLOSET	20% CHRYSOTILE ASBESTOS
13638	1WTC-13638	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE NORTHEAST TELEPHONE CLOSET.	25% CHRYSOTILE ASBESTOS

PA0001373

ONE WORLD TRADE CENTER
FLOOR: 20

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1033	1WTC-01033	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1034	1WTC-01034	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1035	1WTC-01035	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1039	1WTC-01039	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1040	1WTC-01040	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1041	1WTC-01041	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1042	1WTC-01042	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1043	1WTC-01043	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1049	1WTC-01049	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS

PA0001374

HD00044286

CWT WORLD TRADE CENTER
FLOOR: 21

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
890	1WTC-30890	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
892	1WTC-30892	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
894	1WTC-00894	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
897	1WTC-00897	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
898	1WTC-30898	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM O. THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
899	1WTC-30899	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
900	1WTC-00900	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
901	1WTC-00901	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
904	1WTC-00904	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
906	1WTC-00906	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
907	1WTC-00907	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
908	1WTC-00908	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
910	1WTC-00910	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
13447	1WTC-13447	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
13448	1WTC-13448	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	40% CHRYSOTILE ASBESTOS
14903	1WTC-14903	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
14904	1WTC-14904	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR 22

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14907	1WTC-14907	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
14908	1WTC-14908	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
14909	1WTC-14909	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
14910	1WTC-14910	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
14911	1WTC-14911	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR.	25% CHRYSOTILE ASBESTOS
14912	1WTC-14912	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTH CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS
14913	1WTC-14913	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WEST CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS
14914	1WTC-14914	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTH CORE CORRIDOR.	15% CHRYSOTILE ASBESTOS

PA0001376

HD00044288

ONE WORLD TRADE CENTER
FLOOR: 12

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1200	1WTC-01200	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
1201	1WTC-01201	FLUFFY FALLOUT MATERIAL IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1204	1WTC-01204	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1206	1WTC-01206	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
1207	1WTC-01207	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
1208	1WTC-01208	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
1209	1WTC-01209	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1210	1WTC-01210	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1213	1WTC-01213	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
1214	1WTC-01214	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1215	1WTC-01215	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
4464	1WTC-04464	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
4465	1WTC-04465	FLUFFY FALLOUT MATERIAL IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
4467	1WTC-04467	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
4470	1WTC-04470	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
4471	1WTC-04471	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
4472	1WTC-04472	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS

PA0001377

ED00044289

ONE WORLD TRADE CENTER
FLOOR: 22

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4474	1WTC-04474	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
4475	1WTC-04475	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
4479	1WTC-04479	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
4480	1WTC-04480	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
4481	1WTC-04481	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
4482	1WTC-04482	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
4483	1WTC-04483	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
4485	1WTC-04485	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
4486	1WTC-04486	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
4487	1WTC-04487	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35 CHRYSOTILE ASBESTOS 15 AMOSITE ASBESTOS
13629	1WTC-13629	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTHEAST TELEPHONE CLOSET.	40% CHRYSOTILE ASBESTOS
13630	1WTC-13630	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS

PA0001378

ONE WORLD TRADE CENTER
FLOOR: 23

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1184	1WTC-01184	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
1185	1WTC-01185	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
1187	1WTC-01187	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1188	1WTC-01188	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1189	1WTC-01189	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
1191	1WTC-01191	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1193	1WTC-01193	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1194	1WTC-01194	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
1195	1WTC-01195	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1196	1WTC-01196	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1199	1WTC-01199	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
7804	1WTC-07804	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	40% CHRYSOTILE ASBESTOS
7808	1WTC-07808	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB EXPOSED WITHIN THE SOUTHWEST TELEPHONE CLOSET.	70% CHRYSOTILE ASBESTOS
13432	1WTC-13432	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS

PA0001379

MD00044291

ONE WORLD TRADE CENTER
FLOOR: 24

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7796	1WTC-07796	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	60% CHRYSOTILE ASBESTOS
7799	1WTC-07799	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE NORTHWEST TELEPHONE CLOSET.	25% CHRYSOTILE ASBESTOS
7800	1WTC-07800	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB EXPOSED WITHIN THE SOUTHWEST TELEPHONE CLOSET.	20% CHRYSOTILE ASBESTOS
10993	1WTC-10993	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-1% CHRYSOTILE ASBESTOS
12005	1WTC-12005	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
12006	1WTC-12006	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12007	1WTC-12007	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12008	1WTC-12008	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12009	1WTC-12009	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
12011	1WTC-12011	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
12012	1WTC-12012	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12013	1WTC-12013	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12014	1WTC-12014	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
12015	1WTC-12015	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12016	1WTC-12016	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12017	1WTC-12017	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12018	1WTC-12018	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR: 24

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12019	1WTC-12019	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
12020	1WTC-12020	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
12021	1WTC-12021	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
12022	1WTC-12022	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
12023	1WTC-12023	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS TRACE AMOSITE ASBESTOS
12024	1WTC-12024	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
12025	1WTC-12025	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
12026	1WTC-12026	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
12027	1WTC-12027	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
12028	1WTC-12028	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
12029	1WTC-12029	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
12030	1WTC-12030	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
12031	1WTC-12031	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
12032	1WTC-12032	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
12033	1WTC-12033	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTH CORE CORRIDOR.	10% CHRYSOTILE ASBESTOS
12035	1WTC-12035	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB IN THE PLENUM OF THE NORTH CORE CORRIDOR.	10% CHRYSOTILE ASBESTOS
12036	1WTC-12036	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WEST CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS

PA0001381

ONE WORLD TRADE CENTER
FLOOR: 24

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12037	1WTC-12037	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE SOUTH SIDE OF THE PASSENGER ELEVATOR LOBBY.	50% CHRYSOTILE ASBESTOS
12038	1WTC-12038	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE EAST SIDE OF THE UNUSED PASSENGER ELEVATOR LOBBY.	35% CHRYSOTILE ASBESTOS
12039	1WTC-12039	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE WEST SIDE OF THE UNUSED PASSENGER ELEVATOR LOBBY.	35% CHRYSOTILE ASBESTOS
12040	1WTC-12040	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE EAST SIDE OF THE UNUSED PASSENGER ELEVATOR LOBBY.	40% CHRYSOTILE ASBESTOS
13633	1WTC-13633	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	40% CHRYSOTILE ASBESTOS
13634	1WTC-13634	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	45% CHRYSOTILE ASBESTOS

PA0001382

WTC00041294

ONE WORLD TRADE CENTER
FLOOR: 25

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1004	1WTC-01004	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1005	1WTC-01005	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1006	1WTC-01006	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1007	1WTC-01007	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1008	1WTC-01008	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
1009	1WTC-01009	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1010	1WTC-01010	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1011	1WTC-01011	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1012	1WTC-01012	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1013	1WTC-01013	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1014	1WTC-01014	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
3261	1WTC-03261	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3262	1WTC-03262	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3263	1WTC-03263	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3264	1WTC-03264	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3265	1WTC-03265	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3268	1WTC-03268	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS

PA0001383

ED00044295

ONE WORLD TRADE CENTER
FLOOR: 23

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3269	1WTC-03269	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3270	1WTC-03270	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3271	1WTC-03271	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3272	1WTC-03272	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3273	1WTC-03273	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3274	1WTC-03274	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
3276	1WTC-03276	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3277	1WTC-03277	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
7768	1WTC-07768	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	25% CHRYSOTILE ASBESTOS
7769	1WTC-07769	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	15% CHRYSOTILE ASBESTOS
7791	1WTC-07791	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHWEST TELEPHONE CLOSET.	20% CHRYSOTILE ASBESTOS
7792	1WTC-07792	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB EXPOSED WITHIN THE SOUTHWEST TELEPHONE CLOSET.	20% CHRYSOTILE ASBESTOS
7793	1WTC-07793	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE SOUTHWEST TELEPHONE CLOSET.	1-3% CHRYSOTILE ASBESTOS
11655	1WTC-11655	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
11656	1WTC-11656	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS

PA0001384

ONE WORLD TRADE CENTER
FLOOR: 26

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1017	1WTC-01017	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1018	1WTC-01018	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1019	1WTC-01019	CEILING TILE SAMPLE IN THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1020	1WTC-01020	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1021	1WTC-01021	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1022	1WTC-01022	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1023	1WTC-01023	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1024	1WTC-01024	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1026	1WTC-01026	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1027	1WTC-01027	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1028	1WTC-01028	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
1030	1WTC-01030	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1031	1WTC-01031	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
7579	1WTC-07579	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
7580	1WTC-07580	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	25% CHRYSOTILE ASBESTOS
7581	1WTC-07581	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB EXPOSED WITHIN THE SOUTHWEST TELEPHONE CLOSET.	50% CHRYSOTILE ASBESTOS
7582	1WTC-07582	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS

PA0001385

ONE WORLD TRADE CENTER
FLOOR. 27

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7369	1WTC-07369	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
7370	1WTC-07370	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	35% CHRYSOTILE ASBESTOS
7373	1WTC-07373	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTHWEST TELEPHONE CLOSET.	70% CHRYSOTILE ASBESTOS
7374	1WTC-07374	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTHWEST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
12033	1WTC-12033	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
12034	1WTC-12034	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12035	1WTC-12035	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12036	1WTC-12036	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12037	1WTC-12037	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12038	1WTC-12038	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12039	1WTC-12039	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12040	1WTC-12040	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12041	1WTC-12041	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12042	1WTC-12042	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	50% CHRYSOTILE ASBESTOS
12043	1WTC-12043	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12044	1WTC-12044	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12045	1WTC-12045	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS

PA0001386

HD00044298

ONE WORLD TRADE CENTER
FLOOR: 17

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12066	1WTC-12066	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
12067	1WTC-12067	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
12068	1WTC-12068	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
12069	1WTC-12069	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
12070	1WTC-12070	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
12071	1WTC-12071	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
12072	1WTC-12072	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
12073	1WTC-12073	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
12075	1WTC-12075	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
12076	1WTC-12076	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTH CORE CORRIDOR.	50% CHRYSOTILE ASBESTOS
12077	1WTC-12077	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTH CORE CORRIDOR.	40% CHRYSOTILE ASBESTOS
12078	1WTC-12078	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR.	40% CHRYSOTILE ASBESTOS
12079	1WTC-12079	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE WEST CORE CORRIDOR.	40% CHRYSOTILE ASBESTOS
12080	1WTC-12080	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
12081	1WTC-12081	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
12082	1WTC-12082	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
12084	1WTC-12084	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS

PA0001387

ONE WORLD TRADE CENTER
FLOOR: 28

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
985	1WTC-00985	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
986	1WTC-00986	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
987	1WTC-00987	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
988	1WTC-00988	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
989	1WTC-00989	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
991	1WTC-00991	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
992	1WTC-00992	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
993	1WTC-00993	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
997	1WTC-00997	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
998	1WTC-00998	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
999	1WTC-00999	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1000	1WTC-01000	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1001	1WTC-01001	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1003	1WTC-01003	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
7561	1WTC-07561	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB EXPOSED WITHIN THE NORTHWEST TELEPHONE CLOSET.	25% CHRYSOTILE ASBESTOS
7562	1WTC-07562	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHWEST TELEPHONE CLOSET.	25% CHRYSOTILE ASBESTOS
7563	1WTC-07563	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	25% CHRYSOTILE ASBESTOS

PA0001388

ONE WORLD TRADE CENTER
FLOOR: 19

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7533	1WTC-07533	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
7555	1WTC-07555	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB EXPOSED WITHIN THE NORTHWEST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
7556	1WTC-07556	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTHWEST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
7557	1WTC-07557	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB EXPOSED WITHIN THE SOUTHEAST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
7559	1WTC-07559	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB EXPOSED WITHIN THE SOUTHWEST TELEPHONE CLOSET.	30% CHRYSOTILE ASBESTOS
14925	1WTC-14925	FLUFFY FALLOUT MATERIAL IN THE PLENUM OF EAST CORE CORRIDOR.	30% CHRYSOTILE ASBESTOS
14926	1WTC-14926	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTH CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS
14927	1WTC-14927	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTH CORE CORRIDOR.	35% CHRYSOTILE ASBESTOS

PAG001390

HD00044302

ONE WORLD TRADE CENTER
FLOOR 30

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11482	1WTC-11482	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
11483	1WTC-11483	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
11484	1WTC-11484	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTH GENERAL OFFICE AREA NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
11485	1WTC-11485	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTH WEST GENERAL OFFICE AREA NORTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
11486	1WTC-11486	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
11487	1WTC-11487	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	65% CHRYSOTILE ASBESTOS
11493	1WTC-11493	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
11494	1WTC-11494	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11495	1WTC-11495	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	65% CHRYSOTILE ASBESTOS
11496	1WTC-11496	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11497	1WTC-11497	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11498	1WTC-11498	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11499	1WTC-11499	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAS QUADRANT.	25% CHRYSOTILE ASBESTOS
11500	1WTC-11500	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11501	1WTC-11501	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
11502	1WTC-11502	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
11503	1WTC-11503	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM IN THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS

PA0001391

HD00044393

ONE WORLD TRADE CENTER
FLOOR: 30

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11304	1WTC-11304	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11305	1WTC-11305	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11306	1WTC-11306	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
11307	1WTC-11307	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
11308	1WTC-11308	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	45% CHRYSOTILE ASBESTOS
11309	1WTC-11309	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
11310	1WTC-11310	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
11311	1WTC-11311	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
11312	1WTC-11312	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
11313	1WTC-11313	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS

PA0001392

ED00044304

ONE WORLD TRADE CENTER
FLOOR: 31

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
5763	1WTC-05763	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
5764	1WTC-05764	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
5765	1WTC-05765	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
5767	1WTC-05767	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
5869	1WTC-05869	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
5871	1WTC-05871	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
5872	1WTC-05872	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
5873	1WTC-05873	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
5874	1WTC-05874	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
5875	1WTC-05875	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
5876	1WTC-05876	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
5878	1WTC-05878	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
5879	1WTC-05879	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
5880	1WTC-05880	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
5881	1WTC-05881	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
5882	1WTC-05882	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
5883	1WTC-05883	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS

PA0001393

HD00044305

ONE WORLD TRADE CENTER
FLOOR: 31

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
5885	1WTC-05885	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
5886	1WTC-05886	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
5887	1WTC-05887	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
5888	1WTC-05888	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
5889	1WTC-05889	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
5890	1WTC-05890	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
5891	1WTC-05891	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
5893	1WTC-05893	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
5894	1WTC-05894	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
5895	1WTC-05895	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
5896	1WTC-05896	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
5898	1WTC-05898	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
5901	1WTC-05901	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
5902	1WTC-05902	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
5903	1WTC-05903	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS

PA0001394

HD00044306

ONE WORLD TRADE CENTER
FLOOR: 32

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3646	1WTC-03646	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
3646	1WTC-09003	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3646.	10% CHRYSOTILE ASBESTOS
3646	1WTC-09004	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3646.	NON ASBESTOS
3646	1WTC-09005	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3646.	40% CHRYSOTILE ASBESTOS
3646	1WTC-09006	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3646.	40% CHRYSOTILE ASBESTOS
3660	1WTC-03660	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
3660	1WTC-08995	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3660.	1-5% CHRYSOTILE ASBESTOS
3660	1WTC-08996	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3660.	1-5% CHRYSOTILE ASBESTOS
3660	1WTC-08997	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3660.	<1% CHRYSOTILE ASBESTOS *
3660	1WTC-08998	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3660.	20% CHRYSOTILE ASBESTOS
3661	1WTC-03661	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
3661	1WTC-08999	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3661.	1-5% CHRYSOTILE ASBESTOS
3661	1WTC-09000	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT BY SAMPLE #3661.	10% CHRYSOTILE ASBESTOS
3661	1WTC-09001	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3661.	NON ASBESTOS
3661	1WTC-09002	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE #3661.	15% CHRYSOTILE ASBESTOS
3798	1WTC-03798	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
3798	1WTC-11377	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT NEAR SAMPLE #3798.	40% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 384.

PAC001395

HD00044307

ONE WORLD TRADE CENTER
FLOOR: 32

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3798	1WTC-13378	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT NEAR SAMPLE 3798.	25% CHRYSOTILE ASBESTOS
3796	1WTC-13379	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT NEAR SAMPLE # 3796.	25% CHRYSOTILE ASBESTOS
3798	1WTC-13380	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT NEAR SAMPLE 3798.	10% CHRYSOTILE ASBESTOS
13391	1WTC-13391	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
13393	1WTC-13393	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
14390	1WTC-14390	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
14391	1WTC-14391	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	1-1% CHRYSOTILE ASBESTOS
14397	1WTC-14397	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
14401	1WTC-14401	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
14402	1WTC-14402	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	1-1% CHRYSOTILE ASBESTOS
14403	1WTC-14403	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
14404	1WTC-14404	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
14446	1WTC-14446	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
14450	1WTC-14450	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	1-1% CHRYSOTILE ASBESTOS
14451	1WTC-14451	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS

PA0001396

HD00044308

ONE WORLD TRADE CENTER
FLOOR: 33

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10961	1WTC-10961	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
10962	1WTC-10962	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
10963	1WTC-10963	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	50% CHRYSOTILE ASBESTOS
10965	1WTC-10965	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
10966	1WTC-10966	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTH-WEST QUADRANT.	20% CHRYSOTILE ASBESTOS
10967	1WTC-10967	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
10968	1WTC-10968	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
10969	1WTC-10969	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
10970	1WTC-10970	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
10971	1WTC-10971	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	50% CHRYSOTILE ASBESTOS
10972	1WTC-10972	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
10973	1WTC-10973	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
10974	1WTC-10974	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS

PA0001397

HD00044309

ONE WORLD TRADE CENTER
FLOOR: 34

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
973	1WTC-00973	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
974	1WTC-00974	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
975	1WTC-00975	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
976	1WTC-00976	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
979	1WTC-00979	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
980	1WTC-00980	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
982	1WTC-00982	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS

PA0001398

HD00044310

ONE WORLD TRADE CENTER
FLOOR: 33

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11321	1WTC-11321	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
11322	1WTC-11322	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTH CENTRAL OFFICE AREA BY THE NORTHEAST TELEPHONE CLOSET.	40% CHRYSOTILE ASBESTOS
11323	1WTC-11323	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
11324	1WTC-11324	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11325	1WTC-11325	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11326	1WTC-11326	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
11327	1WTC-11327	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
11328	1WTC-11328	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
11329	1WTC-11329	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
11330	1WTC-11330	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
11331	1WTC-11331	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
11332	1WTC-11332	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
11333	1WTC-11333	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
11335	1WTC-11335	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
11336	1WTC-11336	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
11337	1WTC-11337	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
11339	1WTC-11339	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS

PA0001399

ED00044311

ONE WORLD TRADE CENTER
FLOOR: 33

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11340	1WTC-11340	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
11341	1WTC-11341	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
11342	1WTC-11342	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
11343	1WTC-11343	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	50% CHRYSOTILE ASBESTOS
11344	1WTC-11344	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
11345	1WTC-11345	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
11346	1WTC-11346	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
11347	1WTC-11347	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	50% CHRYSOTILE ASBESTOS
11348	1WTC-11348	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR: 36

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10822	1WTC-10822	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
10823	1WTC-10823	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	50% CHRYSOTILE ASBESTOS
10824	1WTC-10824	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
10825	1WTC-10825	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	45% CHRYSOTILE ASBESTOS
10826	1WTC-10826	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	50% CHRYSOTILE ASBESTOS
10828	1WTC-10828	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
10829	1WTC-10829	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	45% CHRYSOTILE ASBESTOS
10830	1WTC-10830	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	45% CHRYSOTILE ASBESTOS
10831	1WTC-10831	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
10832	1WTC-10832	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	45% CHRYSOTILE ASBESTOS
10833	1WTC-10833	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
10834	1WTC-10834	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	55% CHRYSOTILE ASBESTOS
10835	1WTC-10835	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
10836	1WTC-10836	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
10837	1WTC-10837	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
10838	1WTC-10838	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT	40% CHRYSOTILE ASBESTOS
10839	1WTC-10839	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
FLOOR: 36

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10840	1WTC-10840	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
10841	1WTC-10841	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
10842	1WTC-10842	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
10844	1WTC-10844	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
10845	1WTC-10845	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
10846	1WTC-10846	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
10847	1WTC-10847	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
10848	1WTC-10848	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
10849	1WTC-10849	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
10860	1WTC-10860	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS

PA0001402

ONE WORLD TRADE CENTER
FLOOR: 37

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3591	1WTC-03591	FLUFFY FALLOUT INSULATION MATERIAL IN THE PLENUM BY NORTHEAST TELEPHONE CLOSET OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3592	1WTC-03592	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3593	1WTC-03593	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3594	1WTC-03594	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3595	1WTC-03595	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3596	1WTC-03596	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3597	1WTC-03597	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3598	1WTC-03598	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3901	1WTC-03901	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3902	1WTC-03902	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3903	1WTC-03903	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3904	1WTC-03904	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3905	1WTC-03905	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3906	1WTC-03906	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3907	1WTC-03907	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3908	1WTC-03908	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
3909	1WTC-03909	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS

PA0001403

HD00044315

ONE WORLD TRADE CENTER
FLOOR: 37

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11574	1WTC-11574	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTH-EST QUADRANT.	75% CHRYSOTILE ASBESTOS
14763	1WTC-14763	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
14765	1WTC-14765	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT..	35% CHRYSOTILE ASBESTOS
14766	1WTC-14766	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
14767	1WTC-14767	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
14768	1WTC-14768	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
14769	1WTC-14769	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
14770	1WTC-14770	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
14771	1WTC-14771	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
14772	1WTC-14772	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
14773	1WTC-14773	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
14774	1WTC-14774	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
14775	1WTC-14775	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
14782	1WTC-14782	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
14783	1WTC-14783	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
14784	1WTC-14784	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
14785	1WTC-14785	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS

PA0001404

HD00044316

ONE WORLD TRADE CENTER
FLOOR: 37

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14787	1WTC-14787	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
14790	1WTC-14790	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
14791	1WTC-14791	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
14792	1WTC-14792	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
14793	1WTC-14793	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS

PAG001405

HD00044317

ONE WORLD TRADE CENTER
FLOOR: 38

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2461	1WTC-02461	FLUFFY INSULATION MATERIAL SPRAYED ON A METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
2461	1WTC-10458	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE #2461.	TRACE CHRYSOTILE ASBESTOS *
2461	1WTC-10459	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE #2461.	1-3% CHRYSOTILE ASBESTOS
2461	1WTC-10460	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT 2 FEET NORTH OF SAMPLE #2461.	NON ASBESTOS
2461	1WTC-10461	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT 2 FEET EAST OF SAMPLE #2461.	TRACE CHRYSOTILE ASBESTOS *
2461	1WTC-10462	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT 2 FEET WEST OF SAMPLE #2461.	<1% CHRYSOTILE ASBESTOS *
2461	1WTC-10463	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT 2 FEET SOUTH OF SAMPLE #2461.	NON ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 384.

PA0001406

HD00044318

ONE WORLD TRADE CENTER
FLOOR: 39

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2642	1WTC-02642	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR.	10% CHRYSOTILE ASBESTOS
14633	1WTC-14633	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE EAST CORE CORRIDOR.	10% CHRYSOTILE ASBESTOS

PA0001407

HD00044319

ONE WORLD TRADE CENTER
FLOOR: 60

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2636	1WTC-02636	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
2637	1WTC-02637	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
2638	1WTC-02638	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
2639	1WTC-02639	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
2640	1WTC-02640	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
2641	1WTC-02641	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2642	1WTC-02642	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2643	1WTC-02643	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2645	1WTC-02645	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2648	1WTC-02648	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
3003	1WTC-03003	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
3004	1WTC-03004	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
3005	1WTC-03005	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
3006	1WTC-03006	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
3007	1WTC-03007	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
3009	1WTC-03009	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
3010	1WTC-03010	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS

PA0001408

ONE WORLD TRADE CENTER
FLOOR: 40

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3011	1WTC-03011	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
3012	1WTC-03012	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
3013	1WTC-03013	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
3015	1WTC-03015	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
3016	1WTC-03016	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
3017	1WTC-03017	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
3018	1WTC-03018	FLUFFY FALLOUT MATERIAL IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
3019	1WTC-03019	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
3021	1WTC-03021	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
3022	1WTC-03022	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
3023	1WTC-03023	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
3024	1WTC-03024	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
3026	1WTC-03026	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
13143	1WTC-13143	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE WEST CORE CORRIDOR OUTSIDE MEN'S ROOM.	1-3% CHRYSOTILE ASBESTOS
13145	1WTC-13145	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTH CORE CORRIDOR.	1-3% CHRYSOTILE ASBESTOS
13150	1WTC-13150	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
13151	1WTC-13151	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS

PA0001409

ONE WORLD TRADE CENTER
FLOOR: 40

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
15152	1WTC-15152	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS

PA0001410

HD00044322

ONE WORLD TRADE CENTER
FLOOR. 41

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
704	1WTC-00704	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED SOUTH OF THE ACS-41-6 UNIT.	23% CHRYSOTILE ASBESTOS
713	1WTC-00713	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE COUPLING NEAR THE SU-03 UNIT IN THE NORTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
738	1WTC-00738	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE COVER LOCATED WEST OF THE ACS-41-2 UNIT.	10% CHRYSOTILE ASBESTOS
739	1WTC-00739	FLUFFY FALLOUT MATERIAL ON FLOOR LOCATED NEAR THE ACS-41-6 UNIT.	15% CHRYSOTILE ASBESTOS
748	1WTC-00748	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE ELBOW LOCATED WEST OF THE ACS-41-7 UNIT.	5% CHRYSOTILE ASBESTOS
4071	1WTC-04071	FLUFFY PRE-MOLDED INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED 3 FEET EAST OF THE FRP 41-4 UNIT OF THE NORTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
4079	1WTC-04079	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK LOCATED SOUTHWEST OF COLUMN 807.	40% CHRYSOTILE ASBESTOS
4080	1WTC-04080	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK LOCATED NORTHEAST OF THE ACS 41-16 UNIT.	40% CHRYSOTILE ASBESTOS
4081	1WTC-04081	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM LOCATED SOUTH OF COLUMN 807.	5% TREMOLITE ASBESTOS
4090	1WTC-04090	CEMENTITIOUS INSULATION MATERIAL FROM A DUCT LOCATED ABOVE THE ACS 41-15 UNIT.	15% AMOSITE ASBESTOS 3% CHRYSOTILE ASBESTOS

PA0001411

HD00044323

ONE WORLD TRADE CENTER
FLOOR: 44

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7917	1WTC-07917	FLUFFY PAD INSULATION MATERIAL ON A DUCT IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% AMOSITE ASBESTOS 1-3% CHRYSOTILE ASBESTOS

PA0001412

HD00044324

ONE WORLD TRADE CENTER
FLOOR: 46

SA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
-147	1WTC-04147	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
147	1WTC-05320	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 4147.	15% CHRYSOTILE ASBESTOS
4147	1WTC-05321	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 4147.	TRACE CHRYSOTILE ASBESTOS *
4150	1WTC-04150	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
4150	1WTC-05318	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
4150	1WTC-05319	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 4150.	15% CHRYSOTILE ASBESTOS
4150	1WTC-14070	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED ONE FOOT EAST OF SAMPLE 4150.	<1% CHRYSOTILE ASBESTOS *
4150	1WTC-14071	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET EAST OF SAMPLE 4150.	NON ASBESTOS
5319	1WTC-14072	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED FOUR FEET OF SAMPLE 5319.	10% CHRYSOTILE ASBESTOS
5319	1WTC-14073	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED 2 FEET EAST OF SAMPLE NO. 5319.	NON ASBESTOS
4081	1WTC-14081	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
4084	1WTC-14084	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0001413

HD00044325

ONE WORLD TRADE CENTER
FLOOR: 56

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
9884	1WTC-09884	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT.	1-2% CHRYSOTILE ASBESTOS
9891	1WTC-09891	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM WITHIN THE SOUTH WALL CONVECTOR UNIT.	1-2% CHRYSOTILE ASBESTOS

PA0001414

HD00044326

ONE WORLD TRADE CENTER
FLOOR: 57

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10074	1WTC-10074	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS

PA0001415

HD00044327

ONE WORLD TRADE CENTER
FLOOR: 63

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3102	1WTC-03102	CEMENTITIOUS INSULATION MATERIAL TROWELED ON BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE IN THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
3102	1WTC-04016	CEMENTITIOUS INSULATION MATERIAL TROWELED ON BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT 2' NORTH OF SAMPLE NUMBER 3102.	5% CHRYSOTILE ASBESTOS
3102	1WTC-04017	CEMENTITIOUS INSULATION MATERIAL TROWELED ON BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT 1'-6' NORTH OF SAMPLE NUMBER 3102.	NON ASBESTOS
3102	1WTC-04018	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT APPROXIMATELY 15'-0" SOUTH OF SAMPLE NUMBER 3102.	12 CHRYSOTILE ASBESTOS *
3102	1WTC-04019	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT APPROXIMATELY 10'-0" NORTH OF SAMPLE NUMBER 3102.	NON ASBESTOS
3102	1WTC-10463	CEMENTITIOUS INSULATION MATERIAL TROWELED ON BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT NEAR SAMPLE NUMBER 3102.	TRACE CHRYSOTILE ASBESTOS *
3102	1WTC-10486	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT 2' SOUTH OF SAMPLE NUMBER 3102.	NON ASBESTOS
3102	1WTC-10487	CEMENTITIOUS INSULATION MATERIAL TROWELED ON BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT 2' NORTH OF SAMPLE NUMBER 3102.	TRACE CHRYSOTILE ASBESTOS *
3102	1WTC-10488	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT CLOSE TO SAMPLE NUMBER 4026.	NON ASBESTOS
3102	1WTC-10489	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT 2' SOUTH OF SAMPLE NUMBER 4026.	TRACE CHRYSOTILE ASBESTOS *
3102	1WTC-13490	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE THE EAST WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT 2' NORTH OF SAMPLE NUMBER 4026.	<1% CHRYSOTILE ASBESTOS *

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 166.

PA0001416

HD00044328

ONE WORLD TRADE CENTER
FLOOR 72

AEA Number	Sample Number	Location	Result
3364	1WTC-03364	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	3% CHRYSOTILE ASBESTOS
3364	1WTC-03889	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED THREE INCHES WEST OF SAMPLE 3364.	1% CHRYSOTILE ASBESTOS *
3364	1WTC-03890	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT NEAR SAMPLE 3364.	3% CHRYSOTILE ASBESTOS
3364	1WTC-03891	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OF THE WEST QUADRANT LOCATED TWO FEET WEST OF SAMPLE 3364.	NON ASBESTOS
3364	1WTC-03892	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED THREE FEET EAST OF SAMPLE 3364.	1% CHRYSOTILE ASBESTOS *
3364	1WTC-03893	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED THREE FEET EAST OF SAMPLE 3364.	3% CHRYSOTILE ASBESTOS
3364	1WTC-10413	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT NEAR SAMPLE 3364.	TRACE CHRYSOTILE ASBESTOS *
3364	1WTC-10414	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT NEAR SAMPLE 3364.	NON ASBESTOS
3364	1WTC-10415	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET EAST OF SAMPLE 3364.	NON ASBESTOS
3364	1WTC-10416	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET EAST OF SAMPLE 3364.	NON ASBESTOS
3364	1WTC-10417	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET WEST OF SAMPLE 3364.	<1% CHRYSOTILE ASBESTOS *
3364	1WTC-10418	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET WEST OF SAMPLE 3364.	NON ASBESTOS
3364	1WTC-10419	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT CLOSE TO SAMPLE #3890.	<1% CHRYSOTILE ASBESTOS *
3364	1WTC-10420	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT CLOSE TO SAMPLE #3890.	<1% CHRYSOTILE ASBESTOS *
3364	1WTC-10421	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT 2' EAST OF SAMPLE #3890.	<1% CHRYSOTILE ASBESTOS *
3364	1WTC-10422	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT 2' WEST OF SAMPLE #3890.	<1% CHRYSOTILE ASBESTOS *
3364	1WTC-10423	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT 2' SOUTH OF SAMPLE #3890.	NON ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 186.

PA0001417

HD00044329

ONE WORLD TRADE CENTER
FLOOR. 72

REA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3364	1WTC-10424	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT 2' SOUTH OF SAMPLE #3890.	NON ASBESTOS
3364	1WTC-10425	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT NEAR SAMPLE 3893.	TRACE CHRYSOTILE ASBESTOS *
3364	1WTC-10426	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT NEAR SAMPLE 3893.	1-3% CHRYSOTILE ASBESTOS
3364	1WTC-10427	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET EAST OF SAMPLE 3893.	NON ASBESTOS
3364	1WTC-10428	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET WEST OF SAMPLE 3893.	TRACE CHRYSOTILE ASBESTOS *
3364	1WTC-10429	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET SOUTH OF SAMPLE 3893.	<1% CHRYSOTILE ASBESTOS *
3364	1WTC-10430	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET SOUTH OF SAMPLE 3893.	<1% CHRYSOTILE ASBESTOS *

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 186.

PA0001418

HD00044330

ONE WORLD TRADE CENTER
FLOOR: 73

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3939	1WTC-03939	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0001419

ONE WORLD TRADE CENTER
FLOOR: 74

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2881	1WTC-02881	FLUFFY INSULATION MATERIAL SPRAYED ON BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
2882	1WTC-02882	FLUFFY INSULATION MATERIAL SPRAYED ON BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
2883	1WTC-02883	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
2885	1WTC-02885	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
2886	1WTC-02886	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2887	1WTC-02887	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2888	1WTC-02888	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
2889	1WTC-02889	FLUFFY INSULATION MATERIAL SPRAYED ON BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2891	1WTC-02891	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
2892	1WTC-02892	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2893	1WTC-02893	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2894	1WTC-02894	FLUFFY INSULATION MATERIAL SPRAYED ON BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2895	1WTC-02895	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
2896	1WTC-02896	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
2897	1WTC-02897	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
2899	1WTC-02899	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
11927	1WTC-11927	FLUFFY INSULATION MATERIAL SPRAYED ON BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS

PA0001420

HD00044332

ONE WORLD TRADE CENTER
FLOOR: 7A

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11928	1WTC-11928	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
11929	1WTC-11929	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
11930	1WTC-11930	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS

PA0001421

ONE WORLD TRADE CENTER
FLOOR: 73

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1731	1WTC-01731	CEMENTITIOUS MATERIAL ON THERMOSTAT IN FRONT OF THE ACS-73-3 UNIT.	85% CHRYSOTILE ASBESTOS
1868	1WTC-01868	FIBROUS INSULATION MATERIAL FROM A 24" DIAMETER HEAT TRANSFER PIPE AT THE FRV 73-2 IN THE NORTHEAST QUADRANT.	90% CHRYSOTILE ASBESTOS
1868	1WTC-05186	FLUFFY INSULATION MATERIAL FROM A 24" O.D. HEAT TRANSFER PIPE LOCATED AT THE FRV 73-2 UNIT IN THE NORTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
1868	1WTC-05187	FLUFFY INSULATION MATERIAL FROM A 24" DIAMETER HEAT TRANSFER PIPE LOCATED AT THE FRV 73-2 NEAR SAMPLE 1868.	60% CHRYSOTILE ASBESTOS
1870	1WTC-01870	FLUFFY INSULATION MATERIAL FROM A 24" O.D. HEAT TRANSFER PIPE LOCATED AT THE FRV 73-3 UNIT OF THE NORTHEAST QUADRANT.	20% AMOSITE ASBESTOS
1883	1WTC-01883	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 73-2 UNIT.	65% CHRYSOTILE ASBESTOS
1902	1WTC-01902	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE NORTH ELECTRICAL SUB-STATION.	5% CHRYSOTILE ASBESTOS
1904	1WTC-01904	FALLOUT MATERIAL ON TOP OF THE DUCT ABOVE THE E-73-21 UNIT.	10% CHRYSOTILE ASBESTOS
1905	1WTC-01905	FIBROUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE ABOVE THE E.S.S. E-73-21 UNIT.	15% AMOSITE ASBESTOS 10% CHRYSOTILE ASBESTOS
1910	1WTC-01910	FALLOUT MATERIAL FROM THE FLOOR OF THE NORTHWEST RETURN AIR PLENUM.	3% CHRYSOTILE ASBESTOS
1913	1WTC-01913	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE VALVE ABOVE PUMP P-73-2.	3% CHRYSOTILE ASBESTOS
1913	1WTC-05184	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE VALVE ON PUMP P-73-2 NEAR SAMPLE 1913.	5% CHRYSOTILE ASBESTOS
1913	1WTC-05185	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE VALVE ON PUMP P-73-2 NEAR SAMPLE 1913.	5% CHRYSOTILE ASBESTOS
1923	1WTC-01923	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE SOUTH ELECTRICAL SUB-STATION.	3% CHRYSOTILE ASBESTOS
1923	1WTC-05188	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE SOUTH ELECTRICAL SUB-STATION NEAR SAMPLE 1923.	10% CHRYSOTILE ASBESTOS
1923	1WTC-05189	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE SOUTH ELECTRICAL SUB-STATION NEAR SAMPLE 1923.	10% CHRYSOTILE ASBESTOS
1923	1WTC-05190	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE SOUTH ELECTRICAL SUB-STATION NEAR SAMPLE 1923.	20% CHRYSOTILE ASBESTOS
1928	1WTC-01928	HARD PAPER LIKE MATERIAL FROM PIPE SUPPORT ABOVE THE SOUTH ELECTRICAL SUB-STATION.	40% AMOSITE ASBESTOS

PA0001422

HD00044334

ONE WORLD TRADE CENTER
FLOOR: 77

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
8174	1WTC-08174	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
8173	1WTC-08175	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	3% CHRYSOTILE ASBESTOS

PA0001423

ONE WORLD TRADE CENTER
FLOOR: 79

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10022	1WTC-10022	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0001424

HD00044336

ONE WORLD TRADE CENTER
FLOOR: 82

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULTS
2919	1WTC-10385	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT LOCATED TWO FEET NORTH OF SAMPLE 2918.	<1% CHRYSOTILE ASBESTOS *
2919	1WTC-10386	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM AT NORTH OFFICE AREA ABOUT 2 FEET EAST OF SAMPLE #2919	<1% CHRYSOTILE ASBESTOS *
2919	1WTC-10387	FLUFFY SPRAYED ON DECKING INSULATION IN PLENUM AT NORTH OFFICE AREA ABOUT 2 FEET WEST OF SAMPLE #2919	1-3% CHRYSOTILE ASBESTOS
4918	1WTC-10388	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM AT NORTH OFFICE AREA ABOUT 2 FEET SOUTH OF SAMPLE #2918	<1% CHRYSOTILE ASBESTOS *
4187	1WTC-14187	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
4188	1WTC-14188	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
4189	1WTC-14189	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
4195	1WTC-14195	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
4213	1WTC-14213	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
4214	1WTC-14214	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 186.

PA0001426

HD00044338

ONE WORLD TRADE CENTER
FLOOR: 83

EPA SAMPLE NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3177	1WTC-03177	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
3177	1WTC-03880	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED SIX INCHES NORTH OF SAMPLE 3177.	NON ASBESTOS
3177	1WTC-03881	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT ABOVE SAMPLE 3177.	1% CHRYSOTILE ASBESTOS
3177	1WTC-03882	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED SIX FEET SOUTHEAST OF SAMPLE 3177.	3% CHRYSOTILE ASBESTOS
3177	1WTC-03883	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT ABOVE SAMPLE 3882.	3% CHRYSOTILE ASBESTOS
3177	1WTC-03884	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED 6 FEET WEST OF SAMPLE 3177.	3% CHRYSOTILE ASBESTOS
3177	1WTC-10365	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 3884.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10366	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM IN SOUTH EAST OFFICE AREA NEXT TO SAMPLE #3884.	1-3% CHRYSOTILE ASBESTOS
3177	1WTC-10367	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET EAST OF SAMPLE 3884.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10368	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET WEST OF SAMPLE 3884.	TRACE CHRYSOTILE ASBESTOS *
3177	1WTC-10369	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET SOUTH OF SAMPLE 3884.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10370	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET NORTH OF SAMPLE 3884.	TRACE CHRYSOTILE ASBESTOS *
3177	1WTC-10371	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 3177.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10372	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 3177.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10373	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET EAST OF SAMPLE 3177.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10374	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET WEST OF SAMPLE 3177.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10375	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED 2 FEET SOUTH OF SAMPLE 3177.	<1% CHRYSOTILE ASBESTOS *

* NOTE: Non Asbestos Containing Material as per OSHA - see note on page 386.

PAG001427

HD00044339

ONE WORLD TRADE CENTER
FLOOR: 81

LOA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3177	1WTC-10376	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET NORTH OF SAMPLE 3177.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10377	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM IN SOUTH EAST OFFICE AREA NEXT TO SAMPLE #3882.	NON ASBESTOS
3177	1WTC-10378	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM IN SOUTH EAST OFFICE AREA NEXT TO SAMPLE #3882.	TRACE CHRYSOTILE ASBESTOS *
3177	1WTC-10379	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM IN SOUTH EAST OFFICE AREA 2' EAST OF SAMPLE #3882.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10380	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM IN SOUTH EAST OFFICE AREA 2' WEST OF SAMPLE #3882.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-10381	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM IN SOUTH EAST OFFICE AREA 2' SOUTH OF SAMPLE #3882.	TRACE CHRYSOTILE ASBESTOS *
3177	1WTC-10382	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM IN SOUTH EAST OFFICE AREA 2' NORTH OF SAMPLE # 3882.	<1% CHRYSOTILE ASBESTOS *
3177	1WTC-11172	FLUFFY SPRAYED ON INSULATION MATERIAL TAKEN FROM A JOIST INSIDE THE PLENUM NEXT TO SAMPLE NO. 3884.	TRACE CHRYSOTILE ASBESTOS *

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0001428

HD00044340

ONE WORLD TRADE CENTER
FLOOR: 88

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
9024	1WTC-09024	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT.	1-1% CHRYSOTILE ASBESTOS

PA0001429

HD00044341

ONE WORLD TRADE CENTER
FLOOR: 97

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
9475	1WTC-09475	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT.	40% CHRYSOTILE ASBESTOS
9479	1WTC-09479	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS

PA0001430

HD00044342

ONE WORLD TRADE CENTER
FLOOR: 101

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
9291	1WTC-09291	CONDENSATION SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT.	1-5% CHRYSOTILE ASBESTOS

PA0001431

HD00044343

ONE WORLD TRADE CENTER
FLOOR: 102

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4773	1WTC-04773	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST EXPOSED IN THE SOUTHWEST TELEPHONE CLOSET.	3% CHRYSOTILE ASBESTOS
4773	1WTC-10326	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE SOUTHWEST TELEPHONE CLOSET NEAR SAMPLE 4773.	NON ASBESTOS
4773	1WTC-10327	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE SOUTHWEST TELEPHONE CLOSET NEAR SAMPLE 4773.	NON ASBESTOS
4773	1WTC-10328	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE SOUTHWEST TELEPHONE CLOSET NEAR SAMPLE 4773.	NON ASBESTOS
4773	1WTC-10329	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE SOUTHWEST TELEPHONE CLOSET NEAR SAMPLE 4773.	NON ASBESTOS
4773	1WTC-10330	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB IN THE SOUTHWEST TELEPHONE CLOSET LOCATED TWO FEET SOUTH OF SAMPLE 4773.	<1% CHRYSOTILE ASBESTOS *
4773	1WTC-10331	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB IN THE SOUTHWEST TELEPHONE CLOSET LOCATED TWO FEET NORTH OF SAMPLE 4773.	1-3% CHRYSOTILE ASBESTOS

* NOTE: Asbestos Containing Material as per USEPA - see note on page 186.

PA0001432

HD00044344

ONE WORLD TRADE CENTER
FLOOR: 103

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
8943	1WTC-08943	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT.	70% CHRYSOTILE ASBESTOS
8944	1WTC-08944	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT.	30% CHRYSOTILE ASBESTOS

FAT001433

ONE WORLD TRADE CENTER
FLOOR: 104

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4761	1WTC-04761	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
4761	1WTC-10320	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT NEAR SAMPLE 4761.	NON ASBESTOS
4761	1WTC-13321	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT NEAR SAMPLE 4761.	TRACE CHRYSOTILE ASBESTOS *
4761	1WTC-10322	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET NORTH OF SAMPLE 4761.	1-3% CHRYSOTILE ASBESTOS
4761	1WTC-10323	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET EAST OF SAMPLE 4761.	1-3% CHRYSOTILE ASBESTOS
4761	1WTC-10324	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET WEST SAMPLE 4761.	<1% CHRYSOTILE ASBESTOS *
4761	1WTC-10325	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT LOCATED TWO FEET SOUTH OF SAMPLE 4761.	1-3% CHRYSOTILE ASBESTOS
4762	1WTC-04762	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
4762	1WTC-10302	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 4762.	15% CHRYSOTILE ASBESTOS
4762	1WTC-10303	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 4762.	10% CHRYSOTILE ASBESTOS
4762	1WTC-10304	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET NORTH OF SAMPLE 4762.	10% CHRYSOTILE ASBESTOS
4762	1WTC-10305	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET EAST OF SAMPLE 4762.	15% CHRYSOTILE ASBESTOS
4762	1WTC-10306	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET WEST OF SAMPLE 4762.	<1% CHRYSOTILE ASBESTOS *
4762	1WTC-10307	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT LOCATED TWO FEET SOUTH OF SAMPLE 4762.	10% CHRYSOTILE ASBESTOS
3661	1WTC-03661	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
3661	1WTC-10290	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 3661.	NON ASBESTOS
3661	1WTC-10291	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 3661.	1-3% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PAG0014354

HD00044346

ONE WORLD TRADE CENTER
FLOOR: 10A

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
5461	1WTC-10292	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM AT SOUTH-EAST OFFICE AREA ABOUT 2 FEET NORTH OF SAMPLE #5461	NON ASBESTOS
5461	1WTC-10293	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM AT SOUTH-EAST OFFICE AREA ABOUT 2 FEET EAST OF SAMPLE #5461	NON ASBESTOS
5461	1WTC-10294	FLUFFY SPRAYED ON JOIST INSULATION IN PLENUM AT SOUTH-EAST OFFICE AREA ABOUT 2 FEET WEST OF SAMPLE #5461	10% CHRYSOTILE ASBESTOS
5461	1WTC-10295	FLUFFY SPRAYED ON DECKING INSULATION IN PLENUM AT SOUTH-EAST OFFICE AREA ABOUT 2 FEET SOUTH OF SAMPLE #5461	10% CHRYSOTILE ASBESTOS
15072	1WTC-15072	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
15073	1WTC-15073	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS

PA0001435

HD00044347

ONE WORLD TRADE CENTER
FLOOR: 103

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3739	1WTC-03739	CEMENTITIOUS TROWELED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT.	70% CHRYSOTILE ASBESTOS

PA0001436

HD00044348

ONE WORLD TRADE CENTER
FLOOR: 106

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
9204	1WTC-09204	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT.	1-1% CHRYSOTILE ASBESTOS

PA0001437

HD00044349

ONE WORLD TRADE CENTER
FLOOR: 107

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
9245	1WTC-09245	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT.	20% CHRYSOTILE ASBESTOS
9246	1WTC-09246	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
9247	1WTC-09247	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
9248	1WTC-09248	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
9249	1WTC-09249	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT.	3% CHRYSOTILE ASBESTOS
9258	1WTC-09258	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
9260	1WTC-09260	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
9261	1WTC-09261	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
9263	1WTC-09263	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST DINING AREA.	10% CHRYSOTILE ASBESTOS
9264	1WTC-09264	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST DINING AREA.	10% CHRYSOTILE ASBESTOS
9266	1WTC-09266	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST DINING AREA.	15% CHRYSOTILE ASBESTOS
9267	1WTC-09267	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST DINING AREA.	10% CHRYSOTILE ASBESTOS
9268	1WTC-09268	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST DINING AREA.	20% CHRYSOTILE ASBESTOS
9269	1WTC-09269	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST DINING AREA.	40% CHRYSOTILE ASBESTOS
9270	1WTC-09270	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST DINING AREA.	10% CHRYSOTILE ASBESTOS
9271	1WTC-09271	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST DINING AREA.	10% CHRYSOTILE ASBESTOS
9272	1WTC-09272	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAS DINING AREA.	15% CHRYSOTILE ASBESTOS

PAC001438

ONE WORLD TRADE CENTER
FLOOR: 107

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
9273	1WTC-09273	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST DINING AREA.	5% CHRYSOTILE ASBESTOS
9274	1WTC-09274	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST DINING AREA.	5% CHRYSOTILE ASBESTOS
9275	1WTC-09275	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST DINING AREA.	30% CHRYSOTILE ASBESTOS
9276	1WTC-09276	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST DINING AREA.	15% CHRYSOTILE ASBESTOS
9277	1WTC-09277	FLUFFY INSULATION MATERIAL SPRAYED ON BEAM IN THE PLENUM OF THE NORTHWEST DINING AREA.	10% CHRYSOTILE ASBESTOS
9278	1WTC-09278	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST DINING AREA.	20% CHRYSOTILE ASBESTOS
9279	1WTC-09279	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST DINING AREA.	60% CHRYSOTILE ASBESTOS
9280	1WTC-09280	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST DINING AREA.	40% CHRYSOTILE ASBESTOS
9281	1WTC-09281	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST DINING AREA.	50% CHRYSOTILE ASBESTOS
13498	1WTC-13498	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE KITCHEN AREA IN THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
13499	1WTC-13499	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE KITCHEN AREA IN THE NORTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
13500	1WTC-13500	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE KITCHEN AREA IN THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
13501	1WTC-13501	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE KITCHEN AREA IN THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS

PA0001459

ED00044251

ONE WORLD TRADE CENTER
FLOOR: 108

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13664	1WTC-13664	CEMENTITIOUS INSULATION MATERIAL FROM A 6" O.D. HEAT TRANSFER PIPE ELBOW ABOVE ACS-108-2.	3% CHRYSOTILE ASBESTOS
13666	1WTC-13666	CEMENTITIOUS INSULATION MATERIAL FROM AN 8" O.D. HEAT TRANSFER PIPE COUPLING LOCATED SOUTH OF ACS 108-13 UNIT.	3% CHRYSOTILE ASBESTOS
13669	1WTC-13669	CEMENTITIOUS INSULATION MATERIAL FROM A 6" O.D. HEAT TRANSFER PIPE ELBOW LOCATED WEST OF ACS-108-6 UNIT.	1-3% CHRYSOTILE ASBESTOS

PAC001440

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR SHAFT - 01

	SAMPLES
POSITIVE	8
TOTAL	8

ELEVATOR SHAFT - 02

	SAMPLES
POSITIVE	16
TOTAL	18

ELEVATOR SHAFT - 04

	SAMPLES
POSITIVE	1
TOTAL	10

ELEVATOR SHAFT - 05

	SAMPLES
POSITIVE	4
TOTAL	15

ELEVATOR SHAFT - 07

	SAMPLES
POSITIVE	3
TOTAL	24

ELEVATOR SHAFT - 08

	SAMPLES
POSITIVE	26
TOTAL	28

TA2001441

ED000044353

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR SHAFT - 09

	SAMPLES
POSITIVE	4
TOTAL	4

ELEVATOR SHAFT - 10

	SAMPLES
POSITIVE	13
TOTAL	13

ELEVATOR SHAFT - 11

	SAMPLES
POSITIVE	4
TOTAL	4

ELEVATOR SHAFT - 13

	SAMPLES
POSITIVE	13
TOTAL	19

ELEVATOR SHAFT - 15

	SAMPLES
POSITIVE	7
TOTAL	19

ELEVATOR SHAFT - 16

	SAMPLES
POSITIVE	5
TOTAL	17

PA0001442

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR SHAFT - 18

	SAMPLES
POSITIVE	6
TOTAL	17

ELEVATOR SHAFT - 20

	SAMPLES
POSITIVE	5
TOTAL	18

ELEVATOR SHAFT - 23

	SAMPLES
POSITIVE	14
TOTAL	14

ELEVATOR SHAFT - 25

	SAMPLES
POSITIVE	4
TOTAL	4

ELEVATOR SHAFT - 26

	SAMPLES
POSITIVE	17
TOTAL	18

ELEVATOR SHAFT - 29

	SAMPLES
POSITIVE	4
TOTAL	4

PA0001443

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR SHAFT - 31

	SAMPLES
POSITIVE	6
TOTAL	6

ELEVATOR SHAFT - 35

	SAMPLES
POSITIVE	6
TOTAL	6

ELEVATOR SHAFT - 37

	SAMPLES
POSITIVE	5
TOTAL	5

ELEVATOR SHAFT - 39

	SAMPLES
POSITIVE	5
TOTAL	5

ELEVATOR SHAFT - 43

	SAMPLES
POSITIVE	8
TOTAL	8

ELEVATOR SHAFT - 47

	SAMPLES
POSITIVE	8
TOTAL	8

PA0001444

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR SHAFT - 48

	SAMPLES
POSITIVE	7
TOTAL	7

ELEVATOR SHAFT - 49

	SAMPLES
POSITIVE	11
TOTAL	13

ELEVATOR SHAFT - 52

	SAMPLES
POSITIVE	3
TOTAL	3

ELEVATOR SHAFT - 55

	SAMPLES
POSITIVE	3
TOTAL	3

ELEVATOR SHAFT - 57

	SAMPLES
POSITIVE	4
TOTAL	4

ELEVATOR SHAFT - 61

	SAMPLES
POSITIVE	4
TOTAL	4

PAC001445

HD00044357

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR SHAFT - 65

	SAMPLES
POSITIVE	5
TOTAL	6

ELEVATOR SHAFT - 66

	SAMPLES
POSITIVE	4
TOTAL	5

ELEVATOR SHAFT - 70

	SAMPLES
POSITIVE	0
TOTAL	3

ELEVATOR SHAFT - 73

	SAMPLES
POSITIVE	5
TOTAL	5

ELEVATOR SHAFT - 74

	SAMPLES
POSITIVE	0
TOTAL	2

ELEVATOR SHAFT - 79

	SAMPLES
POSITIVE	0
TOTAL	1

FA0001446

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 03

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
393	1WTC-00393	FLUFFY FALLOUT INSULATION MATERIAL ON TOP OF ELEVATOR CAR #3.	15% CHRYSOTILE ASBESTOS
395	1WTC-00395	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 40TH FLOOR.	5% CHRYSOTILE ASBESTOS
396	1WTC-00396	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 38TH FLOOR.	10% CHRYSOTILE ASBESTOS
398	1WTC-00398	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 34TH FLOOR.	5% CHRYSOTILE ASBESTOS
399	1WTC-00399	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 32ND FLOOR.	5% CHRYSOTILE ASBESTOS
400	1WTC-00400	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 29TH FLOOR.	5% CHRYSOTILE ASBESTOS
401	1WTC-00401	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 26TH FLOOR.	20% CHRYSOTILE ASBESTOS
402	1WTC-00402	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 24TH FLOOR.	15% CHRYSOTILE ASBESTOS
403	1WTC-00403	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 20TH FLOOR.	10% CHRYSOTILE ASBESTOS
404	1WTC-00404	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 18TH FLOOR.	30% CHRYSOTILE ASBESTOS
405	1WTC-00405	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 10TH FLOOR.	5% CHRYSOTILE ASBESTOS
406	1WTC-00406	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 10TH FLOOR.	20% CHRYSOTILE ASBESTOS
407	1WTC-00407	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 7TH FLOOR.	20% CHRYSOTILE ASBESTOS
408	1WTC-00408	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 6TH FLOOR.	10% CHRYSOTILE ASBESTOS
409	1WTC-00409	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 3RD FLOOR.	15% CHRYSOTILE ASBESTOS
410	1WTC-00410	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 3RD FLOOR.	35% CHRYSOTILE ASBESTOS

PA0001450

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 04

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
15117	1WTC-15117	CEMENTITIOUS INSULATION MATERIAL FROM FILLED ON A COLUMN LOCATED ON THE WEST WALL AT THE 2ND FLOOR.	60% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 03

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14870	1WTC-14870	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 3RD FLOOR.	25% CHRYSOTILE ASBESTOS
14872	1WTC-14872	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 8TH FLOOR.	15% CHRYSOTILE ASBESTOS
14874	1WTC-14874	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE NORTH WALL AT THE 12TH FLOOR.	15% CHRYSOTILE ASBESTOS
14876	1WTC-14876	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 18TH FLOOR.	40% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 67

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14848	IWTC-14848	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL BELOW THE 6TH FLOOR.	25% CHRYSOTILE ASBESTOS
14853	IWTC-14853	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL BELOW THE 22ND FLOOR.	30% CHRYSOTILE ASBESTOS
14854	IWTC-14854	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM LOCATED ON THE WEST WALL BELOW THE 28TH FLOOR.	1-5% CHRYSOTILE ASBESTOS

PA0001453

HD00044362

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 88

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
376	1WTC-00376	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 44TH FLOOR.	10% CHRYSOTILE ASBESTOS
377	1WTC-00377	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 42ND FLOOR.	10% CHRYSOTILE ASBESTOS
378	1WTC-00378	FLUFFY FALLOUT INSULATION MATERIAL ON TOP OF ELEVATOR CAR #8.	10% CHRYSOTILE ASBESTOS
379	1WTC-00379	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 40TH FLOOR.	10% CHRYSOTILE ASBESTOS
380	1WTC-00380	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 37TH FLOOR.	20% CHRYSOTILE ASBESTOS
381	1WTC-00381	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 35TH FLOOR.	30% CHRYSOTILE ASBESTOS
384	1WTC-00384	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 31ST FLOOR.	20% CHRYSOTILE ASBESTOS
386	1WTC-00386	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 27TH FLOOR.	5% CHRYSOTILE ASBESTOS
387	1WTC-00387	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 27TH FLOOR.	20% CHRYSOTILE ASBESTOS
388	1WTC-00388	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 21ST FLOOR.	10% CHRYSOTILE ASBESTOS
389	1WTC-00389	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 16TH FLOOR.	20% CHRYSOTILE ASBESTOS
390	1WTC-00390	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 12TH FLOOR.	30% CHRYSOTILE ASBESTOS
391	1WTC-00391	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 7TH FLOOR.	10% CHRYSOTILE ASBESTOS
392	1WTC-00392	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE 3RD FLOOR.	15% CHRYSOTILE ASBESTOS
12714	1WTC-12714	FLUFFY FALLOUT INSULATION MATERIAL TAKEN FROM THE BEAM BETWEEN SHAFTS 8 AND 9	10% CHRYSOTILE ASBESTOS
12715	1WTC-12715	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE NORTHEAST WALL ABOVE CONCOURSE LEVEL.	30% CHRYSOTILE ASBESTOS
12716	1WTC-12716	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE CONCOURSE LEVEL.	20% CHRYSOTILE ASBESTOS
12717	1WTC-12717	FLUFFY FALLOUT INSULATION MATERIAL ON TOP OF ELEVATOR CAR #8.	5% CHRYSOTILE ASBESTOS

PA0001454

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 6B

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12718	1WTC-12718	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE CONCOURSE LEVEL.	15% CHRYSOTILE ASBESTOS
15118	1WTC-15118	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 2ND FLOOR.	60% CHRYSOTILE ASBESTOS
15119	1WTC-15119	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 9TH FLOOR.	50% CHRYSOTILE ASBESTOS
15120	1WTC-15120	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 19TH FLOOR.	50% CHRYSOTILE ASBESTOS
15121	1WTC-15121	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 27TH FLOOR.	40% CHRYSOTILE ASBESTOS
15122	1WTC-15122	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 36TH FLOOR.	5% CHRYSOTILE ASBESTOS
15123	1WTC-15123	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 41ST FLOOR.	5% CHRYSOTILE ASBESTOS
15124	1WTC-15124	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 44TH FLOOR.	5% CHRYSOTILE ASBESTOS

PA0001455

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 09

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12710	1WTC-12710	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE SOUTHWALL ABOVE THE CONCOURSE LEVEL.	30% CHRYSOTILE ASBESTOS
12711	1WTC-12711	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL ABOVE THE CONCOURSE LEVEL.	15% CHRYSOTILE ASBESTOS
12712	1WTC-12712	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL ABOVE THE CONCOURSE LEVEL.	25% CHRYSOTILE ASBESTOS
12713	1WTC-12713	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE NORTHWEST CORNER ABOVE THE CONCOURSE LEVEL.	60% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT. 10

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12705	1WTC-12705	FLUFFY FALLOUT MATERIAL ON A BEAM LOCATED ABOVE THE CONCOURSE LEVEL.	20% CHRYSOTILE ASBESTOS
12706	1WTC-12706	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED IN THE NORTHEAST CORNER ABOVE THE CONCOURSE LEVEL.	60% CHRYSOTILE ASBESTOS
12707	1WTC-12707	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE CONCOURSE LEVEL.	20% CHRYSOTILE ASBESTOS
12708	1WTC-12708	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE CONCOURSE LEVEL.	30% CHRYSOTILE ASBESTOS
12709	1WTC-12709	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE CONCOURSE LEVEL.	50% CHRYSOTILE ASBESTOS
13133	1WTC-13133	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 2ND FLOOR.	50% CHRYSOTILE ASBESTOS
13134	1WTC-13134	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 8TH FLOOR.	60% CHRYSOTILE ASBESTOS
13135	1WTC-13135	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 13TH FLOOR.	65% CHRYSOTILE ASBESTOS
13136	1WTC-13136	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 20TH FLOOR.	80% CHRYSOTILE ASBESTOS
13137	1WTC-13137	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 27TH FLOOR.	5% CHRYSOTILE ASBESTOS
13138	1WTC-13138	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 34TH FLOOR.	5% CHRYSOTILE ASBESTOS
13139	1WTC-13139	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 39TH FLOOR.	15% CHRYSOTILE ASBESTOS
13140	1WTC-13140	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 44TH FLOOR.	10% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 11

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12701	1WTC-12701	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED IN THE NORTHWEST CORNER ABOVE THE CONCOURSE.	50% CHRYSOTILE ASBESTOS
12702	1WTC-12702	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL ABOVE THE CONCOURSE.	40% CHRYSOTILE ASBESTOS
12703	1WTC-12703	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL ABOVE THE CONCOURSE.	75% CHRYSOTILE ASBESTOS
12704	1WTC-12704	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE CORNER ABOVE THE CONCOURSE.	40% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 13

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13153	1WTC-13153	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL AT THE 78TH FLOOR.	10% CHRYSOTILE ASBESTOS
13155	1WTC-13155	FLUFFY FALLOUT INSULATION MATERIAL ON TOP OF ELEVATOR CAR #13.	20% CHRYSOTILE ASBESTOS
13156	1WTC-13156	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL ABOVE THE 73RD FLOOR.	10% CHRYSOTILE ASBESTOS
13157	1WTC-13157	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WALL ABOVE THE 67TH FLOOR.	15% CHRYSOTILE ASBESTOS
13158	1WTC-13158	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL ABOVE THE 63RD FLOOR.	5% CHRYSOTILE ASBESTOS
13159	1WTC-13159	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL ABOVE THE 57TH FLOOR.	5% CHRYSOTILE ASBESTOS
13164	1WTC-13164	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL ABOVE THE 40TH FLOOR.	10% CHRYSOTILE ASBESTOS
13165	1WTC-13165	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL ABOVE THE 35TH FLOOR.	10% CHRYSOTILE ASBESTOS
13167	1WTC-13167	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WALL ABOVE THE 25TH FLOOR.	35% CHRYSOTILE ASBESTOS
13168	1WTC-13168	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL ABOVE THE 19TH FLOOR.	45% CHRYSOTILE ASBESTOS
13169	1WTC-13169	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL ABOVE THE 14TH FLOOR.	20% CHRYSOTILE ASBESTOS
13170	1WTC-13170	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL ABOVE THE 8TH FLOOR.	25% CHRYSOTILE ASBESTOS
13171	1WTC-13171	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WALL ABOVE THE 3RD FLOOR.	60% CHRYSOTILE ASBESTOS TRACE AMOSITE ASBESTOS

PA0001459

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 13

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13208	1WTC-13208	FLUFFY FALLOUT INSULATION MATERIAL ON TOP OF ELEVATOR CAR #13.	20% CHRYSOTILE ASBESTOS
13221	1WTC-13221	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE EAST WALL AT THE 25TH FLOOR.	1-3% CHRYSOTILE ASBESTOS
13222	1WTC-13222	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 25TH FLOOR.	25% CHRYSOTILE ASBESTOS
13223	1WTC-13223	FLUFFY INSULATION MATERIAL TROWELED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 19TH FLOOR.	25% CHRYSOTILE ASBESTOS
13224	1WTC-13224	FLUFFY INSULATION MATERIAL TROWELED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 13TH FLOOR.	5% CHRYSOTILE ASBESTOS
13225	1WTC-13225	FLUFFY INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 7TH FLOOR.	25% CHRYSOTILE ASBESTOS
13226	1WTC-13226	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 2ND FLOOR.	25% CHRYSOTILE ASBESTOS

PA0001460

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 16

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
15192	1WTC-15192	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 2ND FLOOR.	5% CHRYSOTILE ASBESTOS
15193	1WTC-15193	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 2ND FLOOR.	10% CHRYSOTILE ASBESTOS
15196	1WTC-15196	FLUFFY INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 19TH FLOOR.	20% CHRYSOTILE ASBESTOS
15197	1WTC-15197	FLUFFY INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 24TH FLOOR.	15% CHRYSOTILE ASBESTOS
15198	1WTC-15198	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 24TH FLOOR.	30% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 18

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13262	1WTC-13262	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 2ND FLOOR.	5% CHRYSOTILE ASBESTOS
13263	1WTC-13263	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 2ND FLOOR.	35% CHRYSOTILE ASBESTOS
13265	1WTC-13265	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 12TH FLOOR.	30% CHRYSOTILE ASBESTOS
13266	1WTC-13266	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 18TH FLOOR.	30% CHRYSOTILE ASBESTOS
13267	1WTC-13267	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 24TH FLOOR.	10% CHRYSOTILE ASBESTOS
13268	1WTC-13268	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 24TH FLOOR.	25% CHRYSOTILE ASBESTOS

PA0001462

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 20

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13235	1WTC-13235	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 20TH FLOOR.	1-3% CHRYSOTILE ASBESTOS
13236	1WTC-13236	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 23RD FLOOR.	40% CHRYSOTILE ASBESTOS
13237	1WTC-13237	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 15TH FLOOR.	25% CHRYSOTILE ASBESTOS
13238	1WTC-13238	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL ABOVE THE 10TH FLOOR.	35% CHRYSOTILE ASBESTOS
13240	1WTC-13240	FLUFFY FALLOUT INSULATION MATERIAL ON TOP OF ELEVATOR CAR #20.	15% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 23

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13172	1WTC-13172	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL AT THE 75TH FLOOR.	5% CHRYSOTILE ASBESTOS
13173	1WTC-13173	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 73RD FLOOR.	10% CHRYSOTILE ASBESTOS
13174	1WTC-13174	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 67TH FLOOR.	15% CHRYSOTILE ASBESTOS
13175	1WTC-13175	FLUFFY FALLOUT MATERIAL ON TOP OF ELEVATOR CAR #23.	5% CHRYSOTILE ASBESTOS
13176	1WTC-13176	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 6CTH FLOOR.	10% CHRYSOTILE ASBESTOS
13177	1WTC-13177	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 55RD FLOOR.	10% CHRYSOTILE ASBESTOS
13178	1WTC-13178	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 45TH FLOOR.	15% CHRYSOTILE ASBESTOS
13179	1WTC-13179	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 39TH FLOOR.	10% CHRYSOTILE ASBESTOS
13180	1WTC-13180	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 33RD FLOOR.	10% CHRYSOTILE ASBESTOS
13181	1WTC-13181	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 26TH FLOOR.	10% CHRYSOTILE ASBESTOS
13182	1WTC-13182	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 18TH FLOOR.	30% CHRYSOTILE ASBESTOS
13183	1WTC-13183	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 13TH FLOOR.	10% CHRYSOTILE ASBESTOS
13184	1WTC-13184	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 2ND FLOOR.	45% CHRYSOTILE ASBESTOS
13185	1WTC-13185	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 8TH FLOOR.	45% CHRYSOTILE ASBESTOS

PA0001464

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 25

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14431	1WTC-14431	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 2ND FLOOR.	70% CHRYSOTILE ASBESTOS
14432	1WTC-14432	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 6TH FLOOR.	40% CHRYSOTILE ASBESTOS
14433	1WTC-14433	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 10TH FLOOR.	35% CHRYSOTILE ASBESTOS
14434	1WTC-14434	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 15TH FLOOR.	60% CHRYSOTILE ASBESTOS

PA0001465

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 26

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
411	1WTC-00411	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 14TH FLOOR.	35% CHRYSOTILE ASBESTOS
412	1WTC-00412	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 14TH FLOOR.	10% CHRYSOTILE ASBESTOS
413	1WTC-00413	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 12TH FLOOR.	10% CHRYSOTILE ASBESTOS
414	1WTC-00414	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 10TH FLOOR.	15% CHRYSOTILE ASBESTOS
415	1WTC-00415	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 7TH FLOOR.	5% CHRYSOTILE ASBESTOS
416	1WTC-00416	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 5TH FLOOR.	10% CHRYSOTILE ASBESTOS
417	1WTC-00417	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 3TH FLOOR.	35% CHRYSOTILE ASBESTOS
418	1WTC-00418	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 3RD FLOOR.	15% CHRYSOTILE ASBESTOS
421	1WTC-00421	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 24TH FLOOR.	10% CHRYSOTILE ASBESTOS
422	1WTC-00422	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 23RD FLOOR.	20% CHRYSOTILE ASBESTOS
423	1WTC-00423	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 21ST FLOOR.	20% CHRYSOTILE ASBESTOS
424	1WTC-00424	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 17TH FLOOR.	40% CHRYSOTILE ASBESTOS
426	1WTC-00426	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT 13TH FLOOR.	20% CHRYSOTILE ASBESTOS
427	1WTC-00427	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 9TH FLOOR.	10% CHRYSOTILE ASBESTOS
428	1WTC-00428	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 9TH FLOOR.	30% CHRYSOTILE ASBESTOS
429	1WTC-00429	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 6TH FLOOR.	25% CHRYSOTILE ASBESTOS
430	1WTC-00430	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 4TH FLOOR.	20% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 29

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14405	1WTC-14405	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 16TH FLOOR.	50% CHRYSOTILE ASBESTOS
14406	1WTC-14406	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 13TH FLOOR.	40% CHRYSOTILE ASBESTOS
14407	1WTC-14407	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 9TH FLOOR.	35% CHRYSOTILE ASBESTOS
14408	1WTC-14408	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 2ND FLOOR.	50% CHRYSOTILE ASBESTOS

PA0001467

OKC WORLD TRADE CENTER
ELEVATOR SHAFT: 11

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14409	1WTC-14409	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 2ND FLOOR.	15% CHRYSOTILE ASBESTOS
14410	1WTC-14410	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 7TH FLOOR.	35% CHRYSOTILE ASBESTOS
14411	1WTC-14411	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 11TH FLOOR.	40% CHRYSOTILE ASBESTOS
14412	1WTC-14412	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 19TH FLOOR.	50% CHRYSOTILE ASBESTOS
14413	1WTC-14413	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 22ND FLOOR.	50% CHRYSOTILE ASBESTOS
14414	1WTC-14414	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 24TH FLOOR.	20% CHRYSOTILE ASBESTOS

PA0001468

HD00041377

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 35

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14415	1WTC-14415	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 7TH FLOOR.	40% CHRYSOTILE ASBESTOS
14416	1WTC-14416	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 11TH FLOOR.	30% CHRYSOTILE ASBESTOS
14417	1WTC-14417	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 18TH FLOOR.	70% CHRYSOTILE ASBESTOS
14418	1WTC-14418	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 22ND FLOOR.	30% CHRYSOTILE ASBESTOS
14419	1WTC-14419	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 24TH FLOOR.	10% CHRYSOTILE ASBESTOS
14420	1WTC-14420	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 2ND FLOOR.	1-3% CHRYSOTILE ASBESTOS

PA0001469

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 37

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14442	1WTC-14442	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 3RD FLOOR.	7% CHRYSOTILE ASBESTOS
14443	1WTC-14443	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 8TH FLOOR.	70% CHRYSOTILE ASBESTOS
14444	1WTC-14444	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 14TH FLOOR.	70% CHRYSOTILE ASBESTOS
14445	1WTC-14445	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 26TH FLOOR.	70% CHRYSOTILE ASBESTOS
14446	1WTC-14446	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 30TH FLOOR.	60% CHRYSOTILE ASBESTOS

PA0001470

HP00044379

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 39

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14437	1WTC-14437	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 32ND FLOOR.	40% CHRYSOTILE ASBESTOS
14438	1WTC-14438	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 27TH FLOOR.	70% CHRYSOTILE ASBESTOS
14439	1WTC-14439	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 23RD FLOOR.	70% CHRYSOTILE ASBESTOS
14440	1WTC-14440	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 18TH FLOOR.	40% CHRYSOTILE ASBESTOS
14441	1WTC-14441	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 4TH FLOOR.	25% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 43

AEA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14421	1WTC-14421	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 40TH FLOOR.	20% CHRYSOTILE ASBESTOS
14422	1WTC-14422	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 35TH FLOOR.	20% CHRYSOTILE ASBESTOS
14423	1WTC-14423	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 32ND FLOOR.	5% CHRYSOTILE ASBESTOS
14424	1WTC-14424	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 25TH FLOOR.	40% CHRYSOTILE ASBESTOS
14425	1WTC-14425	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 19TH FLOOR.	60% CHRYSOTILE ASBESTOS
14426	1WTC-14426	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 14TH FLOOR.	50% CHRYSOTILE ASBESTOS
14427	1WTC-14427	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 8TH FLOOR.	40% CHRYSOTILE ASBESTOS
14428	1WTC-14428	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 2ND FLOOR.	60% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 47

AEA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14429	1WTC-14429	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 40TH FLOOR.	50% CHRYSOTILE ASBESTOS
14430	1WTC-14430	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 36TH FLOOR.	5% CHRYSOTILE ASBESTOS
14431	1WTC-14431	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE WEST WALL AT THE 32ND FLOOR.	40% CHRYSOTILE ASBESTOS
14432	1WTC-14432	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 28TH FLOOR.	60% CHRYSOTILE ASBESTOS
14433	1WTC-14433	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 24TH FLOOR.	60% CHRYSOTILE ASBESTOS
14434	1WTC-14434	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE WEST WALL AT THE 16TH FLOOR.	40% CHRYSOTILE ASBESTOS
14435	1WTC-14435	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 10TH FLOOR.	70% CHRYSOTILE ASBESTOS
14436	1WTC-14436	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE B1 SUBLEVEL.	60% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 48

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
15291	1WTC-15291	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE B1 SUBLEVEL.	15% CHRYSOTILE ASBESTOS
15292	1WTC-15292	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL ABOVE THE 7TH FLOOR.	15% CHRYSOTILE ASBESTOS
15293	1WTC-15293	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL ABOVE THE 14TH FLOOR.	15% CHRYSOTILE ASBESTOS
15294	1WTC-15294	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 29TH FLOOR.	15% CHRYSOTILE ASBESTOS
15295	1WTC-15295	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 29TH FLOOR.	10% CHRYSOTILE ASBESTOS
15296	1WTC-15296	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL ABOVE THE 33TH FLOOR.	10% CHRYSOTILE ASBESTOS
15297	1WTC-15297	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE SOUTH WALL ABOVE THE 40TH FLOOR.	20% CHRYSOTILE ASBESTOS

PAG0001474

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 49

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13278	1WTC-13278	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 3RD FLOOR.	10% CHRYSOTILE ASBESTOS
13279	1WTC-13279	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE NORTH WALL ABOVE THE 9TH FLOOR.	25% CHRYSOTILE ASBESTOS
13280	1WTC-13280	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 15TH FLOOR.	20% CHRYSOTILE ASBESTOS
13282	1WTC-13282	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 26TH FLOOR.	25% CHRYSOTILE ASBESTOS
13283	1WTC-13283	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 32ND FLOOR.	30% CHRYSOTILE ASBESTOS
13284	1WTC-13284	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 39TH FLOOR.	25% CHRYSOTILE ASBESTOS
13286	1WTC-13286	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 49TH FLOOR.	25% CHRYSOTILE ASBESTOS
13287	1WTC-13287	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 58TH FLOOR.	20% CHRYSOTILE ASBESTOS
13288	1WTC-13288	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 63RD FLOOR.	20% CHRYSOTILE ASBESTOS
13289	1WTC-13289	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE WEST WALL ABOVE THE 69TH FLOOR.	10% CHRYSOTILE ASBESTOS
13290	1WTC-13290	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE EAST WALL ABOVE THE 74TH FLOOR.	20% CHRYSOTILE ASBESTOS

PA0001475

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 32

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14447	1WTC-14447	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 44TH FLOOR.	10% CHRYSOTILE ASBESTOS
14448	1WTC-14448	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 49TH FLOOR.	25% CHRYSOTILE ASBESTOS
14449	1WTC-14449	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 34TH FLOOR.	40% CHRYSOTILE ASBESTOS

HD00044385

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 55

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14450	1WTC-14450	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 44TH FLOOR.	50% CHRYSOTILE ASBESTOS
14451	1WTC-14451	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 30TH FLOOR.	20% CHRYSOTILE ASBESTOS
14452	1WTC-14452	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 22ND FLOOR.	60% CHRYSOTILE ASBESTOS

PA0001477

ONE WORLD TRADE CENTER
ELEVATOR SHAFT. 37

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14453	1WTC-14453	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 47TH FLOOR.	60% CHRYSOTILE ASBESTOS
14454	1WTC-14454	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 54TH FLOOR.	70% CHRYSOTILE ASBESTOS
14455	1WTC-14455	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 57TH FLOOR.	25% CHRYSOTILE ASBESTOS
14456	1WTC-14456	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 61ST FLOOR.	20% CHRYSOTILE ASBESTOS

PA0001478

HD00044397

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 61

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14457	1WTC-14457	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 45TH FLOOR.	20% CHRYSOTILE ASBESTOS
14458	1WTC-14458	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 50TH FLOOR.	10% CHRYSOTILE ASBESTOS
14459	1WTC-14459	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 55TH FLOOR.	30% CHRYSOTILE ASBESTOS
14460	1WTC-14460	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 59TH FLOOR.	30% CHRYSOTILE ASBESTOS

PA0001479

HD00044388

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 43

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14476	1WTC-14476	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 45TH FLOOR.	25% CHRYSOTILE ASBESTOS
14477	1WTC-14477	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 50TH FLOOR.	80% CHRYSOTILE ASBESTOS
14478	1WTC-14478	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 55TH FLOOR.	60% CHRYSOTILE ASBESTOS
14479	1WTC-14479	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 61ST FLOOR.	40% CHRYSOTILE ASBESTOS
14480	1WTC-14480	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL AT THE 65TH FLOOR.	35% CHRYSOTILE ASBESTOS

PA0001480

HD00044389

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 66

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14471	1WTC-14471	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 67TH FLOOR.	30% CHRYSOTILE ASBESTOS
14472	1WTC-14472	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 63RD FLOOR.	20% CHRYSOTILE ASBESTOS
14473	1WTC-14473	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 50TH FLOOR.	10% CHRYSOTILE ASBESTOS
14474	1WTC-14474	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 44TH FLOOR.	5% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR SHAFT: 73

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14461	1WTC-14461	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 74TH FLOOR.	13% CHRYSOTILE ASBESTOS
14462	1WTC-14462	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 67TH FLOOR.	10% CHRYSOTILE ASBESTOS
14463	1WTC-14463	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 61ST FLOOR.	13% CHRYSOTILE ASBESTOS
14464	1WTC-14464	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 53RD FLOOR.	1-3% CHRYSOTILE ASBESTOS
14465	1WTC-14465	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE WEST WALL AT THE 47TH FLOOR.	20% CHRYSOTILE ASBESTOS

PA 001482

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR PITS - 03-04

	SAMPLES
POSITIVE	2
TOTAL	2

ELEVATOR PITS - 08-09

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PITS - 10-11

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PITS - 12-13

	SAMPLES
POSITIVE	1
TOTAL	3

ELEVATOR PITS - 14-15

	SAMPLES
POSITIVE	10
TOTAL	18

ELEVATOR PITS - 20-21

	SAMPLES
POSITIVE	1
TOTAL	2

PA0001483

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR PIT - 24

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PITS - 25-26

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PIT - 29

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PIT - 30

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PITS - 33-34

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PIT - 35

	SAMPLES
POSITIVE	1
TOTAL	1

PA0001484

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR PITS - 37-38

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PITS - 39-40

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PITS - 43-44

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PITS - 43-44

	SAMPLES
POSITIVE	1
TOTAL	1

PA0001485

ONE WORLD TRADE CENTER
ELEVATOR PITS: 03-04

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
336	1WTC-00336	INSULATION MATERIAL LOCATED ON THE SOUTH WALL.	30% CHRYSOTILE ASBESTOS
337	1WTC-00337	FALLOUT MATERIAL IN THE ELEVATOR PIT.	30% CHRYSOTILE ASBESTOS

PAC 001486

ONE WORLD TRADE CENTER
ELEVATOR PITS: 12-13

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
139	1WTC-00139	INSULATION MATERIAL FROM A COLUMN IN THE ELEVATOR PIT.	40% CHRYSOTILE ASBESTOS

PA 0001487

ONE WORLD TRADE CENTER
ELEVATOR PITS: 08-09

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
134	1WTC-00134	INSULATION MATERIAL LOCATED ON THE SOUTH WALL OF THE ELEVATOR PIT.	25% CHRYSOTILE ASBESTOS

PAC001488

ONE WORLD TRADE CENTER
ELEVATOR PITS: 10-11

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
335	1WTC-00335	INSULATION MATERIAL FROM THE SOUTH WALL IN THE ELEVATOR PIT.	10% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR PITS: 14-15

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3401	1WTC-03401	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3402	1WTC-03402	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3403	1WTC-03403	FLUFFY INSULATION MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3404	1WTC-03404	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3406	1WTC-03406	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	10% CHRYSOTILE ASBESTOS
3407	1WTC-03407	CEMENTITIOUS FALLOUT MATERIAL FROM THE ELEVATOR PIT.	5% CHRYSOTILE ASBESTOS
3408	1WTC-03408	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3409	1WTC-03409	CEMENTITIOUS FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3411	1WTC-03411	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	5% CHRYSOTILE ASBESTOS
3412	1WTC-03412	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	5% CHRYSOTILE ASBESTOS
3413	1WTC-03413	FLUFFY MATERIAL FROM THE ELEVATOR PIT.	10% CHRYSOTILE ASBESTOS
3414	1WTC-03414	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3415	1WTC-03415	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3417	1WTC-03417	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3418	1WTC-03418	CEMENTITIOUS FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3419	1WTC-03419	FLUFFY MATERIAL IN THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3420	1WTC-03420	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3421	1WTC-03421	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	35% CHRYSOTILE ASBESTOS
3422	1WTC-03422	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	20% CHRYSOTILE ASBESTOS
3423	1WTC-03423	FLUFFY FALLOUT MATERIAL FROM THE ELEVATOR PIT.	15% CHRYSOTILE ASBESTOS

FAC001460

ONE WORLD TRADE CENTER
ELEVATOR PITS: 20-21

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
341	1WTC-00341	INSULATION MATERIAL ON A COLUMN FROM ELEVATOR PIT.	30% CHRYSOTILE ASBESTOS

PA0001491

ONE WORLD TRADE CENTER
ELEVATOR PIT: 2A

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
346	1WTC-00346	INSULATION MATERIAL FROM THE ELEVATOR PIT.	25% CHRYSOTILE ASBESTOS

PA0001492

ONE WORLD TRADE CENTER
ELEVATOR PITS: 23-26

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
347	1WTC-00347	INSULATION MATERIAL FROM THE ELEVATOR PIT.	5% CHRYSOTILE ASBESTOS

PA0001493

ONE WORLD TRADE CENTER
ELEVATOR PIT: 29

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
343	1WTC-00343	INSULATION MATERIAL FROM THE ELEVATOR PIT.	20% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR PIT: 3Q

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3+3	LVTC-00163	INSULATION MATERIAL FROM THE ELEVATOR PIT.	30% CHRYSOTILE ASBESTOS

ONE WORLD TRADE CENTER
ELEVATOR PITS: 33-34

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
368	1WTC-00368	INSULATION MATERIAL FROM THE ELEVATOR PIT.	5% CHRYSOTILE ASBESTOS

PA0001496

ONE WORLD TRADE CENTER
ELEVATOR PIT: 33

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
344	1WTC-00344	INSULATION MATERIAL FROM THE ELEVATOR PIT.	15% CHRYSOTILE ASBESTOS TRACE AMOSITE ASBESTOS

AA001497

HD00044406

ONE WORLD TRADE CENTER
ELEVATOR PITS: 17-16

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
155	1WTC-00155	INSULATION MATERIAL ON A COLUMN FROM THE ELEVATOR PIT.	20% CHRYSOTILE ASBESTOS

HD00044407

ONE WORLD TRADE CENTER
ELEVATOR PITS: 39-40

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
334	1WTC-00334	INSULATION MATERIAL ON A COLUMN FROM ELEVATOR PITS 39 AND 40.	15% CHRYSOTILE ASBESTOS

PA0001499

ONE WORLD TRADE CENTER
ELEVATOR PITS: 43-44

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
349	1WTC-00349	OUTER LAYER OF INSULATION MATERIAL FROM THE ELEVATOR PIT.	2% CHRYSOTILE ASBESTOS
350	1WTC-00350	INNER LAYER OF INSULATION MATERIAL FROM THE ELEVATOR PIT.	2% CHRYSOTILE ASBESTOS

PA0001500

ONE WORLD TRADE CENTER
ELEVATOR PITS: 43-44

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
331	1WTC-00331	FALLOUT MATERIAL ON THE FLOOR IN THE ELEVATOR PIT.	10% CHRYSOTILE ASBESTOS
332	1WTC-00332	INSULATION MATERIAL FROM A BEAM IN ELEVATOR PIT.	25% CHRYSOTILE ASBESTOS

PA0001501

ASBESTOS INVESTIGATION AND ANALYSIS REPORT
WORLD TRADE CENTER
VOLUME II OF II

ENVIRONMENTAL MANAGEMENT DIVISION
MARCH 21, 1988

PA0002562

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
B1	77	77
B3	1	1
B4	1	1
B6	26	25
2	9	9
3	33	33
4	26	26
5	18	18
9	36	36
14	40	40
15	40	40
16	38	38
17	50	50
18	39	39
19	42	39
20	69	67
21	42	42
22	33	33
23	40	40
24	40	40
25	41	41
27	42	42
28	73	73
29	40	40
30	78	78
31	38	38
34	42	42
35	40	40
36	60	60
37	40	40
38	40	40
39	41	41
44	43	43
45	53	53
46	42	42
47	50	50
48	69	69
49	65	65
50	40	40
51	33	33
52	36	36
53	34	34
54	23	23
55	30	30
56	52	52
57	60	60

PA0002564

HD00044006

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
58	33	33
59	92	92
60	36	36
61	36	36
62	36	36
63	33	33
64	41	41
65	42	42
66	41	41
67	32	32
68	37	37
69	48	48
70	30	30
71	36	36
72	32	32
73	34	34
77	35	35
78	33	33
79	32	32
80	32	32
81	32	32
82	31	31
83	32	32
84	34	34
85	31	31
86	32	32
87	31	31
88	30	30
89	30	30
90	32	32
91	30	30
92	33	33
93	35	33
94	42	42
95	43	43
96	44	44
97	32	32
98	37	37
99	33	33
100	32	32
101	30	30
102	49	49
103	49	49
104	33	33
105	32	32
106	32	32

PA0002565

HD00044007

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - B1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	83	77	0	15	1	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - B2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	1	0	1	0	0
TOTAL	19	8	0	11	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ASBESTOS

FLOOR - B3

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	3	1	0	2	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - B4

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	21	1	0	20	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - B6

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	1	0	0	0	0
TOTAL	44	26	0	18	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002566

HD00044008

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	3	0	0	0	0
TOTAL	12	12	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	9	9	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 3

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	33	33	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 4

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	28	26	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 5

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	21	18	0	0	2	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PAG0026367

HD00044009

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 6

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	18	18	0	0	0	0
TOTAL	22	22	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 7

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	73	65	0	7	1	0
TOTAL	163	127	8	27	6	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 9

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	0	2	0	0	0
TOTAL	74	56	16	0	0	2

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 10

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	26	26	0	0	0	0
TOTAL	31	30	0	0	0	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 11

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	32	32	0	0	0	0
TOTAL	33	30	0	0	0	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

PA00025S8

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
THE WORLD TRADE CENTER

FLOOR - 12

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	16	16	0	0	0	0
TOTAL	35	32	1	0	0	2

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 13

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	11	11	0	0	0	0
TOTAL	77	66	11	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 14

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	52	40	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 15

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	52	40	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 16

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	50	38	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002369

HD00044011

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 17

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	62	50	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 18

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	52	39	12	1	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 19

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	3	0	0	0	0
TOTAL	58	42	14	1	0	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 20

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	2	0	0	0	0
TOTAL	92	89	3	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 21

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	55	42	13	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002570

HD00044012

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 22

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	49	33	16	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 23

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	52	40	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 24

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	53	40	13	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 25

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	53	41	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 26

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	9	9	0	0	0	0
TOTAL	73	61	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

PA0002571

HD00044013

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 27

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	3	0	0	0	0
TOTAL	54	42	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 28

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	85	73	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 29

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	51	40	11	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 30

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	90	78	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 31

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	50	38	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002572

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 32

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	2	0	0	0	0
TOTAL	57	45	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 33

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	3	0	0	0	0
TOTAL	189	171	18	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 34

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	42	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 35

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	52	40	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 36

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	72	60	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002073

HD00044015

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 37

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	52	40	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 38

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	52	40	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 39

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	53	41	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 40

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	33	33	0	0	0	0
TOTAL	53	41	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 41

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	33	31	0	1	1	0
TOTAL	133	99	0	22	14	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

PA0002574

HD00044016

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 43

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	11	8	0	3	0	0
TOTAL	90	72		6	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: LOCALIZED ABATEMENT

FLOOR - 44

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	55	43	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 45

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	81	55	26	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 46

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	5	0	5	0	0	0
TOTAL	63	42	21	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 47

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	0	2	0	0	0
TOTAL	63	50	13	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002575

HD00044017

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 48

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	0	3	0	0	0
TOTAL	71	48	23	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 49

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	57	45	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 50

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	52	40	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 51

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	46	33	13	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 52

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	68	56	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002576

HD00044018

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 33

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	44	34	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 34

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	35	23	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 35

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	62	50	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 36

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	64	52	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 37

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	72	60	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002577

HD00044019

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 58

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 59

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	108	92	16	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 60

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	42	30	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 61

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	48	36	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 62

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	48	36	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002578

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
130 WORLD TRADE CENTER

FLOOR - 63

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	65	53	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 64

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	56	41	15	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 65

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	57	42	15	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 66

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	4	0	4	0	0	0
TOTAL	56	41	15	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 67

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	7	0	7	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002579

HD00044021

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 68

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	5	0	5	0	0	0
TOTAL	69	57	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 69

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	61	48	13	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 70

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	0	3	0	0	0
TOTAL	62	50	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 71

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	2	1	0	0	0
TOTAL	51	36	15	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 72

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	0	2	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002500

HD00044022

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 73

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	2	0	2	0	0	0
TOTAL	46	34	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 74

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	82	82	0	0	0	0
TOTAL	181	167	13	0	0	1

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 75

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	13	9	0	2	2	0
TOTAL	165	48	0	101	16	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: FULL ABATEMENT

FLOOR - 77

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	47	35	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 78

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	67	55	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002561

HD00044023

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 79

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 80

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 81

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 82

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	51	51	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 83

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002582

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 84

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	44	34	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 83

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	32	31	1	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 86

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 87

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	43	31	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 88

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	32	30	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002583

HD00044025

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 89

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	8	0	0	0	0	0
TOTAL	32	30	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 90

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 91

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	32	30	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 92

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	37	35	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 93

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	47	35	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002584

HD00044026

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 94

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	46	42	4	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 95

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	47	43	4	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 96

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	0	3	0	0	0
TOTAL	53	44	9	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 97

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	56	52	4	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 98

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	69	57	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002535

HD00044027

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 99

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	45	33	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 100

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	47	32	12	3	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 101

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	50	50	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 102

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	51	49	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 103

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	51	49	2	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002536

HD00044028

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 104

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	3
TOTAL	65	53	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 105

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 106

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	44	32	12	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 107

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	54	54	0	0	0	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

FLOOR - 108

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	1	0	1	0	0
TOTAL	112	74	0	23	11	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002587

HD00044029

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

FLOOR - 110

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	18	18	0	0	4	0

INSPECTION AND SAFETY DIVISION'S CLASSIFICATION: NON-ACM

PA0002588

HD00044030

TWO WORLD TRADE CENTER
FLOOR: 82

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13073	2WTC-13073	FLUFFY FALLOUT MATERIAL FROM THE FLOOR LOCATED WITHIN THE STEAM SHAFT CLOSET.	70% CHRYSOTILE ASBESTOS
13078	2WTC-13078	FLUFFY FRIMCLOTH INSULATION MATERIAL FROM A 24" O.D. HEAT TRANSFER PIPE LOCATED WITHIN THE STEAM SHAFT CLOSET.	60% CHRYSOTILE ASBESTOS

TWO WORLD TRADE CENTER
FLOOR: 84

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1374	2WTC-01374	CEMENTITIOUS TROWELED ON BEAM INSULATION ABOVE ACS 53.7.	5% TREMOLITE ASBESTOS

PA0002590

HD00044032

TWO WORLD TRADE CENTER
FLOOR: 1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
8496	2WTC-08496	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM ABOVE A LIGHT FIXTURE LOCATED IN THE EAST SIDE OF THE MEZZANINE OPPOSITE ELEVATOR NUMBER 1.	15% CHRYSOTILE ASBESTOS
8498	2WTC-08498	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM ABOVE A LIGHT FIXTURE LOCATED AT THE NORTH ELEVATOR BANK WALL IN THE MEZZANINE.	80% CHRYSOTILE ASBESTOS
8499	2WTC-08499	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM ABOVE A LIGHT FIXTURE LOCATED AT THE NORTH ELEVATOR BANK WALL IN THE MEZZANINE.	10% CHRYSOTILE ASBESTOS

PA0002591

HD00044033

TWO WORLD TRADE CENTER
FLOOR: 6

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
92	2WTC-092C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT SW 4 IN THE CATWALK AREA.	20% CHRYSOTILE ASBESTOS
94	2WTC-094C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT SE 1 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
95	2WTC-095C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT SE 11 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
96	2WTC-096C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT SE 14 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
97	2WTC-097C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT NE 10 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
98	2WTC-098C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT NE 13 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
99	2WTC-099C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT NE 16 IN THE CATWALK AREA.	20% CHRYSOTILE ASBESTOS
100	2WTC-100C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT NW 16 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
101	2WTC-101C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT NW 13 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
102	2WTC-102C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT NW 9 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
103	2WTC-103C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT NW 7 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
104	2WTC-104C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT NW 12 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
105	2WTC-105C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT SW 9 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
106	2WTC-106C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT SE 4 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
107	2WTC-107C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT SE 7 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
108	2WTC-108C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT SE 10 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS
109	2WTC-109C3	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT SE 5 IN THE CATWALK AREA.	10% CHRYSOTILE ASBESTOS

PAG0025?2

HD00044034

TWO WORLD TRADE CENTER
FLOOR: 6

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
113	2WTC-110CS	FLUFFY INSULATION MATERIAL SPRAYED ON OVER CHANDELIER UNIT #E 6 IN THE CATWALK AREA.	5% CHRYSOTILE ASBESTOS

PA0002593

HD00044035

TWO WORLD TRADE CENTER
FLOOR: 7

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1107	2WTC-01107	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE 13800 VOLT ROOM.	5% CHRYSOTILE ASBESTOS
1108	2WTC-01108	FLUFFY INSULATION MATERIAL SPRAYED ON A TRUSS ABOVE THE 13800 VOLT ROOM.	5% CHRYSOTILE ASBESTOS
1139	2WTC-01139	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE EXHAUST FAN E 7.21 UNIT.	5% CHRYSOTILE ASBESTOS
1142	2WTC-01142	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN ABOVE EXHAUST FAN E 7.21 UNIT.	5% CHRYSOTILE ASBESTOS
1143	2WTC-01143	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE EXHAUST FAN E 7.21 UNIT.	5% CHRYSOTILE ASBESTOS
1144	2WTC-01144	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE EXHAUST FAN E 7.21 UNIT.	10% CHRYSOTILE ASBESTOS
1216	2WTC-1216E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE E 7.21 UNIT.	20% CHRYSOTILE ASBESTOS
1216	2WTC-1216I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE E 7.21 UNIT.	1% CHRYSOTILE ASBESTOS *
1217	2WTC-1217E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A JOIST ABOVE E 7.21 UNIT.	20% CHRYSOTILE ASBESTOS
1217	2WTC-1217I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A JOIST ABOVE THE 7.21 UNIT.	1% CHRYSOTILE ASBESTOS *
1218	2WTC-1218E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE E 7.21 UNIT.	20% CHRYSOTILE ASBESTOS
1218	2WTC-1218I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE COLD WATER PIPE AT THE E 7.21 UNIT.	1% CHRYSOTILE ASBESTOS *
1219	2WTC-1219E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE E 7.21 UNIT.	80% CHRYSOTILE ASBESTOS
1219	2WTC-1219I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE E 7.21 UNIT.	1% CHRYSOTILE ASBESTOS *
1220	2WTC-1220E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE AIR DUCT OF THE E 7.21 UNIT.	10% CHRYSOTILE ASBESTOS
1220	2WTC-1220I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE AIR DUCT OF THE ACS 7.21 UNIT.	1% CHRYSOTILE ASBESTOS *
1221	2WTC-1221E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE AIR DUCT OF THE E 7.21 UNIT.	15% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0002594

HD00044036

TWO WORLD TRADE CENTER
FLOOR: 7

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1221	2WTC-1221I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE AIR DUCT OF THE 7.21 UNIT.	1% CHRYSOTILE ASBESTOS *
1222	2WTC-1222E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE AIR DUCT OF THE 7.21 UNIT.	40% CHRYSOTILE ASBESTOS
1222	2WTC-1222I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE AIR DUCT OF THE 7.21 UNIT.	3% CHRYSOTILE ASBESTOS
1224	2WTC-01224	FLUFFY FALLOUT MATERIAL ON TOP OF DUCT ABOVE THE E 7.21 UNIT.	30% CHRYSOTILE ASBESTOS
1226	2WTC-01226	FLUFFY FALLOUT MATERIAL ON TOP OF THE DUCT ABOVE THE E 7.21 UNIT.	30% CHRYSOTILE ASBESTOS
1227	2WTC-01227	FLUFFY FALLOUT MATERIAL ON TOP OF DUCT ABOVE THE E 7.21 UNIT.	50% CHRYSOTILE ASBESTOS
1229	2WTC-1229E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE SOUTHEAST ACS 7.8 UNIT.	30% CHRYSOTILE ASBESTOS
1229	2WTC-1229I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE SOUTHEAST ACS 7.8 UNIT.	3% CHRYSOTILE ASBESTOS
1230	2WTC-1230E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.8 UNIT.	50% CHRYSOTILE ASBESTOS
1230	2WTC-1230I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.8 UNIT.	NON ASBESTOS
1231	2WTC-1231E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A JOIST ABOVE THE ACS 7.11 UNIT.	50% CHRYSOTILE ASBESTOS
1231	2WTC-1231I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A JOIST ABOVE THE ACS 7.11 UNIT.	10% CHRYSOTILE ASBESTOS
1232	2WTC-1232E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.11 UNIT.	40% CHRYSOTILE ASBESTOS
1232	2WTC-1232I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.11 UNIT.	3% CHRYSOTILE ASBESTOS
1233	2WTC-1233E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.11 UNIT.	15% CHRYSOTILE ASBESTOS
1233	2WTC-1233I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.11 UNIT.	15% CHRYSOTILE ASBESTOS
1234	2WTC-1234E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.10 UNIT.	60% CHRYSOTILE ASBESTOS
1234	2WTC-1234I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.10 UNIT.	1% CHRYSOTILE ASBESTOS *

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0002395

HD00044037

TWO WORLD TRADE CENTER
FLOOR: 7

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1233	2WTC-1233E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACE 7.10 UNIT.	50% CHRYSOTILE ASBESTOS
1233	2WTC-1233I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACE 7.10 UNIT.	3% CHRYSOTILE ASBESTOS
1234	2WTC-01234	CEMENTITIOUS PRE-MOLDED INSULATION MATERIAL FROM A HEAT TRANSFER PIPE ABOVE THE ACE 7.10 UNIT.	20% AMOSITE ASBESTOS
1237	2WTC-1237E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACE 7.10 UNIT.	50% CHRYSOTILE ASBESTOS
1237	2WTC-1237I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACE 7.10 UNIT.	NON ASBESTOS
1238	2WTC-1238E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM IN THE SOUTHEAST RETURN AIR PLENUM.	40% CHRYSOTILE ASBESTOS
1238	2WTC-1238I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM IN THE SOUTHEAST RETURN AIR PLENUM.	3% CHRYSOTILE ASBESTOS
1239	2WTC-1239E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM IN THE SOUTHEAST RETURN AIR PLENUM.	30% CHRYSOTILE ASBESTOS
1239	2WTC-1239I	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE ACE 7 S.E. ROOM.	10% CHRYSOTILE ASBESTOS
1242	2WTC-1242E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACE 7.13 UNIT.	60% CHRYSOTILE ASBESTOS
1242	2WTC-1242I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACE 7.13 UNIT.	10% CHRYSOTILE ASBESTOS
1243	2WTC-1243E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACE 7.13 UNIT.	50% CHRYSOTILE ASBESTOS
1243	2WTC-1243I	FLUFFY INSULATION MATERIAL ON THE METAL DECK ABOVE ACE 7.13 E.	3% CHRYSOTILE ASBESTOS
1243	2WTC-1243E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACE 7.13 UNIT.	60% CHRYSOTILE ASBESTOS
1243	2WTC-1243I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACE 7.13 UNIT.	1% CHRYSOTILE ASBESTOS *
1247	2WTC-1247E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACE 7.13 UNIT.	13% CHRYSOTILE ASBESTOS
1247	2WTC-1247I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACE 7.13 UNIT.	NON ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0002596

HD00044038

TWO WORLD TRADE CENTER
FLOOR: 7

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1251	2WTC-12512	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A JOIST ABOVE THE ACS 7.9 UNIT.	30% CHRYSOTILE ASBESTOS
1251	2WTC-12511	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A JOIST ABOVE THE ACS 7.9 UNIT.	NON ASBESTOS
1252	2WTC-12522	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.9 UNIT.	45% CHRYSOTILE ASBESTOS
1252	2WTC-12521	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.9 UNIT.	5% CHRYSOTILE ASBESTOS
1253	2WTC-12532	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.9 UNIT.	40% CHRYSOTILE ASBESTOS TRACE AMOSITE ASBESTOS
1253	2WTC-12531	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.9 UNIT.	1% CHRYSOTILE ASBESTOS *
1254	2WTC-01254	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.9 UNIT.	20% CHRYSOTILE ASBESTOS
1262	2WTC-12622	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.9 UNIT.	20% CHRYSOTILE ASBESTOS
1262	2WTC-12621	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.9 UNIT.	1% CHRYSOTILE ASBESTOS *
1263	2WTC-02414	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE SOUTHWEST RETURN AIR PLENUM.	5% CHRYSOTILE ASBESTOS
1263	2WTC-02415	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE SOUTHWEST RETURN AIR PLENUM.	20% CHRYSOTILE ASBESTOS
1263	2WTC-02416	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE SOUTHWEST RETURN AIR PLENUM.	10% CHRYSOTILE ASBESTOS
1263	2WTC-12632	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE SOUTHWEST RETURN AIR PLENUM.	30% CHRYSOTILE ASBESTOS
1263	2WTC-12631	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE SOUTHWEST RETURN AIR PLENUM.	40% CHRYSOTILE ASBESTOS
1264	2WTC-01264	FLUFFY INSULATION MATERIAL FROM A STEAM PIPE AT THE ACS 7.9 UNIT.	40% AMOSITE ASBESTOS 1% CHRYSOTILE ASBESTOS
1264	2WTC-02489	FLUFFY INSULATION MATERIAL FROM A 8" O.D. HEAT TRANSFER PIPE INSIDE ACS 7.1 AND 2 RISERS.	30% CHRYSOTILE ASBESTOS 30% AMOSITE ASBESTOS
1264	2WTC-02490	CEMENTITIOUS INSULATION MATERIAL FROM A 8" O.D. HEAT TRANSFER PIPE ELBOW INSIDE THE ACS 7.1 AND 2 RISERS.	30% CHRYSOTILE ASBESTOS 30% AMOSITE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 186.

PA0002597

HD00044039

TWO WORLD TRADE CENTER
FLOOR: 7

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1264	2WTC-02413	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE COUPLING LOCATED INSIDE ACR 7 1+2 NORTH AND SOUTH RISERS.	NON ASBESTOS
1264	2WTC-02412	FLUFFY CEMENTITIOUS HEAT TRANSFER PIPE INSULATION ON ELBOW OF 8" PIPE EXPOSED INSIDE ACR 7 1+2 NORTH AND SOUTH RISERS	40% CHRYSOTILE ASBESTOS 40% AMOSITE ASBESTOS
1264	2WTC-02413	FLUFFY INSULATION MATERIAL FROM A 8" O.D. HEAT TRANSFER PIPE LOCATED ACR 7 1+2 NORTH AND SOUTH STEAM RISERS.	30% CHRYSOTILE ASBESTOS 30% AMOSITE ASBESTOS
1265	2WTC-1265E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM IN THE ACR 7.9 UNIT.	20% CHRYSOTILE ASBESTOS
1265	2WTC-1265I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM IN THE ACR 7.9 UNIT.	1% CHRYSOTILE ASBESTOS *
1266	2WTC-01266	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM AT THE ACR 7.3 UNIT.	5% CHRYSOTILE ASBESTOS
1267	2WTC-01267	AIR-CELL INSULATION MATERIAL ON A STEAM PIPE IN THE ACR 7.3 UNIT.	60% CHRYSOTILE ASBESTOS
1269	2WTC-1269E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.14 UNIT.	60% CHRYSOTILE ASBESTOS
1269	2WTC-1269I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.14 UNIT.	5% CHRYSOTILE ASBESTOS
1270	2WTC-1270E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.14 DUCT UNIT.	30% CHRYSOTILE ASBESTOS
1270	2WTC-1270I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.14 DUCT UNIT.	20% CHRYSOTILE ASBESTOS
1271	2WTC-1271E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.14 DUCT UNIT.	15% CHRYSOTILE ASBESTOS
1271	2WTC-1271I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.14 DUCT UNIT.	1% CHRYSOTILE ASBESTOS *
1272	2WTC-1272E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.14 DUCT UNIT.	30% CHRYSOTILE ASBESTOS
1272	2WTC-1272I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.14 DUCT UNIT.	1% CHRYSOTILE ASBESTOS *
1273	2WTC-1273E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.12 DUCT UNIT.	15% CHRYSOTILE ASBESTOS
1273	2WTC-1273I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.12 DUCT UNIT.	1% CHRYSOTILE ASBESTOS *

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0002598

HD00044040

TWO WORLD TRADE CENTER
FLOOR: 7

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1274	2WTC-1274E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.12 DUCT UNIT.	20% CHRYSOTILE ASBESTOS
1274	2WTC-1274I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.12 DUCT UNIT.	1% CHRYSOTILE ASBESTOS *
1275	2WTC-1275E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.12 UNIT.	40% CHRYSOTILE ASBESTOS
1275	2WTC-1275I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.12 UNIT.	5% CHRYSOTILE ASBESTOS
1276	2WTC-1276E	FLUFFY EXTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.12 UNIT.	20% CHRYSOTILE ASBESTOS
1276	2WTC-1276I	FLUFFY INTERIOR LAYER OF INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.12 UNIT.	1% CHRYSOTILE ASBESTOS *
5191	2WTC-05191	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE SOUTHWEST RETURN AIR PLENUM.	30% CHRYSOTILE ASBESTOS
5193	2WTC-05193	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.9 UNIT.	20% CHRYSOTILE ASBESTOS
5194	2WTC-05194	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 7.9 UNIT.	20% CHRYSOTILE ASBESTOS
5195	2WTC-05195	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE ACS 7.9 UNIT.	30% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0002599

HD00044041

TWO WORLD TRADE CENTER
FLOOR: 9

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7383	2WTC-07383	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
7383	2WTC-10434	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED IN THE NORTH WALL CONVECTOR UNIT AT SAMPLE #7383	1-3% CHRYSOTILE ASBESTOS
7383	2WTC-10435	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED IN THE NORTH WALL CONVECTOR UNIT APPROXIMATELY TWO FEET EAST OF SAMPLE #7383	<1% CHRYSOTILE ASBESTOS *
7383	2WTC-10436	CEMENTITIOUS SPRAYED ON BEAM INSULATION MATERIAL EXPOSED IN THE NORTH WALL CONVECTOR UNIT APPROXIMATELY TWO FEET WEST OF SAMPLE #7383	<1% CHRYSOTILE ASBESTOS *

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0002300

HD00044042

TWO WORLD TRADE CENTER
FLOOR: 16

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1614	2WTC-01614	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
1619	2WTC-01619	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1620	2WTC-01620	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1624	2WTC-01624	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1625	2WTC-01625	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	50% CHRYSOTILE ASBESTOS
1626	2WTC-01626	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
1629	2WTC-01629	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
9311	2WTC-09311	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9312	2WTC-09312	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
9313	2WTC-09313	CEMENTITIOUS SPRAYED ON CONCRETE ENCASED BEAM INSULATION MATERIAL IN THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
9314	2WTC-09314	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9315	2WTC-09315	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	80% CHRYSOTILE ASBESTOS
9316	2WTC-09316	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9318	2WTC-09318	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
9319	2WTC-09319	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
9320	2WTC-09320	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9321	2WTC-09321	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS

PA0002601

HD00044043

TWO WORLD TRADE CENTER
FLOOR: 10

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
9322	2WTC-09322	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
9323	2WTC-09323	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
9324	2WTC-09324	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	80% CHRYSOTILE ASBESTOS
9325	2WTC-09325	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	80% CHRYSOTILE ASBESTOS
9326	2WTC-09326	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9327	2WTC-09327	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9328	2WTC-09328	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9329	2WTC-09329	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
9330	2WTC-09330	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS

PA0002602

HD00044044

TWO WORLD TRADE CENTER
FLOOR: 11

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2287	2WTC-02287	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
2288	2WTC-02288	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
2289	2WTC-02289	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
2290	2WTC-02290	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
2292	2WTC-02292	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
2294	2WTC-02294	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
2295	2WTC-02295	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
2296	2WTC-02296	FLUFFY INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
2297	2WTC-02297	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
2298	2WTC-02298	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
2299	2WTC-02299	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	80% CHRYSOTILE ASBESTOS
2300	2WTC-02300	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
2301	2WTC-02301	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	60% CHRYSOTILE ASBESTOS
2302	2WTC-02302	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
2303	2WTC-02303	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	65% CHRYSOTILE ASBESTOS
2304	2WTC-02304	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
2305	2WTC-02305	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS

PA0002603

HD00044045

TWO WORLD TRADE CENTER
FLOOR: 11

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2306	2WTC-02306	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
2307	2WTC-02307	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
9299	2WTC-09299	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
9300	2WTC-09300	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	80% CHRYSOTILE ASBESTOS
9301	2WTC-09301	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9302	2WTC-09302	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9303	2WTC-09303	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
9304	2WTC-09304	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	90% CHRYSOTILE ASBESTOS
9305	2WTC-09305	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	80% CHRYSOTILE ASBESTOS
9306	2WTC-09306	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9307	2WTC-09307	FLUFFY FALLOUT MATERIAL IN THE PLENUM OF THE SOUTHWEST QUADRANT.	70% CHRYSOTILE ASBESTOS
9308	2WTC-09308	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	80% CHRYSOTILE ASBESTOS
9309	2WTC-09309	FLUFFY SPRAYED ON CONCRETE ENCASED BEAM INSULATION MATERIAL IN THE PLENUM OF THE SOUTHWEST QUADRANT.	60% CHRYSOTILE ASBESTOS
9316	2WTC-09316	CEMENTITIOUS INSULATION MATERIAL TROWELED ON THE METAL DECK IN THE PLENUM IN THE SOUTHWEST QUADRANT.	90% CHRYSOTILE ASBESTOS
12444	2WTC-12444	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM LOCATED ON THE WEST WALL OF THE SOUTHWEST TELEPHONE CLOSET IN THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS

PA0002604

HD00044046

TWO WORLD TRADE CENTER
FLOOR: 12

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1633	2WTC-01633	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1634	2WTC-01634	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1637	2WTC-01637	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1640	2WTC-01640	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
1641	2WTC-01641	FLUFFY ENCAPSULATED BEAM INSULATION MATERIAL IN THE PLENUM OF THE NORTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
1642	2WTC-01642	FLUFFY ENCAPSULATED BEAM INSULATION MATERIAL IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1644	2WTC-01644	FLUFFY ENCAPSULATED METAL DECK INSULATION MATERIAL IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
1645	2WTC-01645	FLUFFY ENCAPSULATED JOIST INSULATION MATERIAL IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1646	2WTC-01646	FLUFFY ENCAPSULATED BEAM INSULATION MATERIAL IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
1647	2WTC-01647	FLUFFY ENCAPSULATED JOIST INSULATION MATERIAL IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS
1648	2WTC-01648	FLUFFY ENCAPSULATED JOIST INSULATION MATERIAL IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
1650	2WTC-01650	FLUFFY ENCAPSULATED BEAM INSULATION MATERIAL IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
1651	2WTC-01651	FLUFFY ENCAPSULATED BEAM INSULATION MATERIAL IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1653	2WTC-01653	FLUFFY ENCAPSULATED BEAM INSULATION MATERIAL IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
1654	2WTC-01654	FLUFFY ENCAPSULATED METAL DECK INSULATION MATERIAL IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
1655	2WTC-01655	FLUFFY ENCAPSULATED BEAM INSULATION MATERIAL IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS

PA0002605

HD00044047

TWO WORLD TRADE CENTER
FLOOR: 13

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4899	2WTC-04899	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
4899	2WTC-07510	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 4899.	1-3% CHRYSOTILE ASBESTOS
4899	2WTC-07511	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 4899.	<1% CHRYSOTILE ASBESTOS *
4899	2WTC-07512	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 4899.	NON ASBESTOS
4899	2WTC-07513	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 4899.	1-3% CHRYSOTILE ASBESTOS
4899	2WTC-14219	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM 2 FEET NORTH OF SAMPLES 4899, 7510, AND 7513.	TRACE CHRYSOTILE ASBESTOS *
4899	2WTC-14220	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM 2 FEET SOUTH OF SAMPLES 4899, 7510 AND 7513.	<1% CHRYSOTILE ASBESTOS *
4899	2WTC-14221	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM 2 FEET EAST OF SAMPLES 4899,7510, AND 7513.	<1% CHRYSOTILE ASBESTOS *
4899	2WTC-14222	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM 2 FEET WEST SAMPLES 4899,7510,7513.	1-3% CHRYSOTILE ASBESTOS
7516	2WTC-07516	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
7516	2WTC-14231	FLUFFY INSULATION MATERIAL SPRAYED ON METAL DECK IN THE PLENUM 2 FEET NORTH OF SAMPLE 7516.	10% CHRYSOTILE ASBESTOS
7516	2WTC-14232	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK 2 FEET SOUTH OF SAMPLE 7516.	10% CHRYSOTILE ASBESTOS
7516	2WTC-14233	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM 2 FEET EAST OF SAMPLE 7516.	10% CHRYSOTILE ASBESTOS
7516	2WTC-14234	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM 2 FEET WEST OF SAMPLE 7516.	20% CHRYSOTILE ASBESTOS
14223	2WTC-14223	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
14226	2WTC-14226	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM 1 FOOT NORTH OF SAMPLE 7516.	10% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 384.

PA0002606

HD00044048

TWO WORLD TRADE CENTER
FLOOR: 14

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7128	2WTC-07128	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0002607

HD00044049

TWO WORLD TRADE CENTER
FLOOR: 19

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1228	2WTC-01228	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED IN THE PLENUM OF THE SERVICE ELEVATOR LOBBY IN THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
1228	2WTC-09732	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SERVICE ELEVATOR LOBBY IN THE NORTHEAST QUADRANT NEAR SAMPLE 1228.	1-3% CHRYSOTILE ASBESTOS
1228	2WTC-09733	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SERVICE ELEVATOR LOBBY IN THE NORTHEAST QUADRANT NEAR SAMPLE 1228.	1-1% CHRYSOTILE ASBESTOS
1228	2WTC-09734	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SERVICE ELEVATOR LOBBY IN THE NORTHEAST QUADRANT NEAR SAMPLE 1228.	<1% CHRYSOTILE ASBESTOS *
1228	2WTC-09735	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SERVICE ELEVATOR LOBBY IN THE NORTHEAST QUADRANT NEAR SAMPLE 1228.	<1% CHRYSOTILE ASBESTOS *

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0002608

HD00044050

TWO WORLD TRADE CENTER
FLOOR: 20

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1784	2WTC-01784	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
1784	2WTC-09720	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 1784.	<1% CHRYSOTILE ASBESTOS *
1784	2WTC-09721	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 1784.	1-3% CHRYSOTILE ASBESTOS
1784	2WTC-09722	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 1784.	NON ASBESTOS
1784	2WTC-09723	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 1784.	NON ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 144.

PA0002609

HD00044051

TWO WORLD TRADE CENTER
FLOOR: 22

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4461	2WTC-04461	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	3% CHRYSOTILE ASBESTOS

PA0002610

HD00044052

TWO WORLD TRADE CENTER
FLOOR: 23

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7870	2WTC-07870	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0002611

HD00044053

TWO WORLD TRADE CENTER
FLOOR: 24

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7871	2WTC-07871	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	1-2% CHRYSOTILE ASBESTOS

PA0002612

HD00044054

TWO WORLD TRADE CENTER
FLOOR: 26

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
5148	2WTC-05148	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
5148	2WTC-07359	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 5148.	30% CHRYSOTILE ASBESTOS
5148	2WTC-07360	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 5148.	5% CHRYSOTILE ASBESTOS
5148	2WTC-07361	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 5148.	30% CHRYSOTILE ASBESTOS
5148	2WTC-07362	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT NEAR SAMPLE 5148.	30% CHRYSOTILE ASBESTOS
14670	2WTC-14670	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
14671	2WTC-14671	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	35% CHRYSOTILE ASBESTOS
14672	2WTC-14672	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
14686	2WTC-14686	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	40% CHRYSOTILE ASBESTOS

PAG002613

HD00044055

TWO WORLD TRADE CENTER
FLOOR: 32

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7037	2WTC-07037	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
14466	2WTC-14466	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0002614

TWO WORLD TRADE CENTER
FLOOR: 33

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4114	2WTC-04114	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST APPROXIMATELY 15 FEET OUT FROM COLUMN #105 IN THE SOUTHWEST QUADRANT.	1% CHRYSOTILE ASBESTOS *
4114	2WTC-05239	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	TRACE CHRYSOTILE ASBESTOS *
4114	2WTC-05240	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTH SIDE OFFICE IN THE SOUTHWEST QUADRANT.	TRACE CHRYSOTILE ASBESTOS *
4114	2WTC-08802	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM NEAR SAMPLE #4114.	TRACE CHRYSOTILE ASBESTOS *
4114	2WTC-08803	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM NEAR SAMPLE #4114.	1-3% CHRYSOTILE ASBESTOS
4119	2WTC-04119	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST APPROXIMATELY 20 FEET OUT FROM COLUMN #147 IN THE NORTHWEST QUADRANT.	1% CHRYSOTILE ASBESTOS *
4119	2WTC-05248	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	NON ASBESTOS
4119	2WTC-05249	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
4119	2WTC-08796	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT NEAR SAMPLE #4119.	TRACE CHRYSOTILE ASBESTOS
4119	2WTC-08797	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT NEAR SAMPLE #4119.	1-3% CHRYSOTILE ASBESTOS
8792	2WTC-08792	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
9764	2WTC-09764	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 386.

PA0002615

HD00044057

TWO WORLD TRADE CENTER
FLOOR: 39

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6421	2WTC-06421	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	8% CHRYSOTILE ASBESTOS

PA0002616

HD00044058

TWO WORLD TRADE CENTER
FLOOR: 46

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6151	2WTC-06151	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
6159	2WTC-06159	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
6161	2WTC-06161	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
6162	2WTC-06162	FLUFFY INSULATION MATERIAL SPRAYED OVER CEMENTITIOUS TROWELED ON BEAM INSULATION MATERIAL IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
6163	2WTC-06163	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
6164	2WTC-06164	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
6165	2WTC-06165	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
6166	2WTC-06166	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
6167	2WTC-06167	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
6169	2WTC-06169	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
6170	2WTC-06170	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
6475	2WTC-06475	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
6476	2WTC-06476	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
6477	2WTC-06477	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
6478	2WTC-06478	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
6479	2WTC-06479	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
6480	2WTC-06480	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS

PA0002617

HD00044059

TWO WORLD TRADE CENTER
FLOOR: 40

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13038	2WTC-13038	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
13039	2WTC-13039	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
13044	2WTC-13044	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
13046	2WTC-13046	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS
13047	2WTC-13047	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS

TWO WORLD TRADE CENTER
FLOOR: 41

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
936	2WTC-00936	CEMENTITIOUS INSULATION MATERIAL FROM A PIPE ELBOW ON THE SOUTH SIDE OF THE ACS 41.11 UNIT.	5% CHRYSOTILE ASBESTOS
937	2WTC-00937	FLUFFY FALLOUT MATERIAL FOUND ON THE FLOOR ON THE SOUTHSIDE OF THE ACS 41.16 UNIT.	5% CHRYSOTILE ASBESTOS
940	2WTC-00940	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 41.16 UNIT.	6% CHRYSOTILE ASBESTOS
1283	2WTC-01283	FLUFFY FALLOUT MATERIAL ON FOUND TOP OF DUCT AT ACS 41.14 UNIT.	10% CHRYSOTILE ASBESTOS
1285	2WTC-01285	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE ACS 41.7 UNIT.	30% CHRYSOTILE ASBESTOS
1286	2WTC-01286	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE ACS 41.7 UNIT.	20% CHRYSOTILE ASBESTOS
1287	2WTC-01287	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 41.7 UNIT.	20% CHRYSOTILE ASBESTOS
1293	2WTC-01293	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE EAST ELECTRICAL SUB-STATION.	10% CHRYSOTILE ASBESTOS
1294	2WTC-01294	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE EAST ELECTRICAL SUB-STATION.	15% CHRYSOTILE ASBESTOS
1316	2WTC-01316	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE WEST ELECTRIC SUB-STATION.	5% CHRYSOTILE ASBESTOS
1320	2WTC-01320	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE MOTOR GENERATOR ROOM.	5% CHRYSOTILE ASBESTOS
3203	2WTC-03203	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE EX 41.3 UNIT.	20% CHRYSOTILE ASBESTOS
3206	2WTC-03206	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE EX 41.3 UNIT.	20% CHRYSOTILE ASBESTOS
3207	2WTC-03207	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE WEST ELECTRICAL SUB-STATION.	20% CHRYSOTILE ASBESTOS
3208	2WTC-03208	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE WEST ELECTRICAL SUB-STATION.	20% CHRYSOTILE ASBESTOS
3209	2WTC-03209	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE DUCT OF ACS 41.4 UNIT.	20% CHRYSOTILE ASBESTOS
3210	2WTC-03210	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ON THE DUCT OF THE ACS 41.4 UNIT.	20% CHRYSOTILE ASBESTOS
3211	2WTC-03211	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST ABOVE THE DUCT OF THE ACS 41.4 UNIT.	20% CHRYSOTILE ASBESTOS

TWO WORLD TRADE CENTER
FLOOR: 41

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
5212	2WTC-05212	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST ABOVE THE DUCT OF THE ACS 41.A UNIT.	20% CHRYSOTILE ASBESTOS
5213	2WTC-05213	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE DUCT OF THE ACS 41.A UNIT.	20% CHRYSOTILE ASBESTOS
5214	2WTC-05214	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE DUCT OF THE ACS 41.A UNIT.	20% CHRYSOTILE ASBESTOS
5215	2WTC-05215	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE WEST ELECTRICAL SUB-STATION.	20% CHRYSOTILE ASBESTOS
5216	2WTC-05216	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK ABOVE THE WEST ELECTRICAL SUB-STATION.	20% CHRYSOTILE ASBESTOS
5217	2WTC-05217	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST ABOVE THE EAST ELECTRICAL SUB-STATION	20% CHRYSOTILE ASBESTOS
5218	2WTC-05218	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST ABOVE THE EAST ELECTRICAL SUB-STATION.	20% CHRYSOTILE ASBESTOS
9186	2WTC-09186	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 41.13 UNIT.	30% CHRYSOTILE ASBESTOS
9187	2WTC-09187	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 41.13 UNIT.	30% CHRYSOTILE ASBESTOS
9188	2WTC-09188	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE THE ACS 41.1 UNIT.	30% CHRYSOTILE ASBESTOS
9189	2WTC-09189	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 41-1 UNIT.	40% CHRYSOTILE ASBESTOS
9190	2WTC-09190	FLUFFY FALLOUT MATERIAL FOUND ON TOP OF ACS 41-10 UNIT.	20% CHRYSOTILE ASBESTOS
9192	2WTC-09192	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 41-10 UNIT.	15% CHRYSOTILE ASBESTOS
9193	2WTC-09193	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 41-14 UNIT.	20% CHRYSOTILE ASBESTOS
9194	2WTC-09194	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 41-14 UNIT.	70% CHRYSOTILE ASBESTOS
9195	2WTC-09195	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 41-14 UNIT.	20% CHRYSOTILE ASBESTOS
9196	2WTC-09196	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM ABOVE ACS 41-26 UNIT.	30% CHRYSOTILE ASBESTOS

PA0002620

HD00044062

TWO WORLD TRADE CENTER
FLOOR: 43

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4933	2WTC-04933	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM AT THE BOTTOM OF THE ESCALATOR IN THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
4933	2WTC-05220	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	TRACE CHRYSOTILE ASBESTOS *
4933	2WTC-05221	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	3% CHRYSOTILE ASBESTOS
4933	2WTC-05222	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
4967	2WTC-04967	CLOTH MATERIAL CONNECTING FAN AND DUCT WORK IN FAN ROOM IN THE NORTH SIDE.	95% CHRYSOTILE ASBESTOS
4967	2WTC-05218	WOVEN BLANKET FAN DUCT WORK NORTH SIDE.	90% CHRYSOTILE ASBESTOS
4967	2WTC-05119	WOVEN BLANKET FAN DUCT WORK IN THE NORTHEAST QUADRANT.	90% CHRYSOTILE ASBESTOS
12099	2WTC-12099	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF SOUTH WALL OFFICE.	1-3% CHRYSOTILE ASBESTOS
12100	2WTC-12100	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM AT ESCALATOR LANDING IN THE SOUTHWEST QUADRANT.	3% CHRYSOTILE ASBESTOS
12101	2WTC-12101	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
13938	2WTC-13938	FLUFFY SPRAYED ON INSULATION MATERIAL TAKEN FROM A BEAM EXPOSED IN THE SOUTH WEST TELEPHONE CLOSET.	1-3% CHRYSOTILE ASBESTOS
14007	2WTC-14007	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 188.

PA0002621

HD00044063

TWO WORLD TRADE CENTER
FLOOR: 44

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6195	2WTC-06195	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	1-5% CHRYSOTILE ASBESTOS
6196	2WTC-06196	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	1-5% CHRYSOTILE ASBESTOS
6199	2WTC-06199	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-5% CHRYSOTILE ASBESTOS
6206	2WTC-06206	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	1-5% CHRYSOTILE ASBESTOS
6213	2WTC-06213	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	1-5% CHRYSOTILE ASBESTOS

PA0002622

HD00044064

TWO WORLD TRADE CENTER
FLOOR: 47

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4220	2WTC-04220	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
4222	2WTC-04222	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS

PA0002623

HD00044065

TWO WORLD TRADE CENTER
FLOOR: 48

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6242	2WTC-06242	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
6249	2WTC-06249	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
6249	2WTC-14247	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON FROM THE OUTER LAYER OF MATERIAL WITHIN CONVECTOR AT SAMPLE 6249.	25% CHRYSOTILE ASBESTOS
6249	2WTC-14248	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON FROM THE INNER LAYER OF MATERIAL WITHIN CONVECTOR AT SAMPLE 6249.	<1% CHRYSOTILE ASBESTOS *

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 186.

PA0002624

HD00044066

TWO WORLD TRADE CENTER
FLOOR: 51

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6628	2WTC-06628	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS

PA0002625

TWO WORLD TRADE CENTER
FLOOR: 33

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6711	1WTC-06711	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	15% CHRYSOTILE ASBESTOS

PA0002626

EP00044068

TWO WORLD TRADE CENTER
FLOOR: 57

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
4461	2WTC-06481	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-5% CHRYSOTILE ASBESTOS

PA0002627

TWO WORLD TRADE CENTER
FLOOR: 59

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
5875	2WTC-45875	CEMENTITIOUS TROWELED ON INSULATION MATERIAL AT THE NORTH WALL CONVECTOR.	1-3% CHRYSOTILE ASBESTOS

PA0002628

TWO WORLD TRADE CENTER
FLOOR: 65

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6438	2WTC-06408	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS

PA0002629

HD00044071

TWO WORLD TRADE CENTER
FLOOR: 66

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
5386	2WTC-65386	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
6419	2WTC-06419	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
6424	2WTC-06424	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
6425	2WTC-06425	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0002630

TWO WORLD TRADE CENTER
FLOOR: 67

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6336	2WTC-06336	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
6337	2WTC-06337	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE NORTH WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
6338	2WTC-06339	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
6341	2WTC-06341	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
6342	2WTC-06342	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
6344	2WTC-06344	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE SOUTH WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
6343	2WTC-06343	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE WEST WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS

PA0002631

HP00044073

TWO WORLD TRADE CENTER
FLOOR: 68

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6073	2WTC-06073	CEMENTITIOUS INSULATION MATERIAL TROWELED ON WITHIN THE SOUTH WALL CONVECTOR.	1-3% CHRYSOTILE ASBESTOS
6074	2WTC-06074	CEMENTITIOUS INSULATION MATERIAL TROWELED ON WITHIN THE EAST WALL CONVECTOR.	1-3% CHRYSOTILE ASBESTOS
6077	2WTC-06077	CEMENTITIOUS INSULATION MATERIAL TROWELED ON WITHIN THE NORTH WALL CONVECTOR.	1-3% CHRYSOTILE ASBESTOS
6079	2WTC-06079	CEMENTITIOUS INSULATION MATERIAL TROWELED ON WITHIN THE NORTH WALL CONVECTOR.	1-3% CHRYSOTILE ASBESTOS
6084	2WTC-06084	CEMENTITIOUS INSULATION MATERIAL TROWELED ON WITHIN THE SOUTH WALL CONVECTOR.	1-3% CHRYSOTILE ASBESTOS

PA0002632

HD00044074

TWO WORLD TRADE CENTER
FLOOR: 78

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6123	2WTC-06123	CEMENTITIOUS INSULATION MATERIAL TROWELED ON WITHIN THE WEST WALL CONVECTOR.	1-3% CHRYSOTILE ASBESTOS
6124	2WTC-06124	CEMENTITIOUS INSULATION MATERIAL TROWELED ON WITHIN THE WEST WALL CONVECTOR UNIT.	1-3% CHRYSOTILE ASBESTOS
6127	2WTC-06127	CEMENTITIOUS INSULATION MATERIAL TROWELED ON WITHIN THE NORTH WALL CONVECTOR.	1-3% CHRYSOTILE ASBESTOS

PA0002633

HD00044075

TWO WORLD TRADE CENTER
FLOOR: 71

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6030	2WTC-06030	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON AT THE EAST WALL IN THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
6133	2WTC-06133	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
6133	2WTC-14687	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM AT SAMPLE #6133.	<1% CHRYSOTILE ASBESTOS *
6133	2WTC-14688	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM AT SAMPLE #6133.	<1% CHRYSOTILE ASBESTOS *
6133	2WTC-14689	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM AT SAMPLE #6133.	5% CHRYSOTILE ASBESTOS

* NOTE: Non Asbestos Containing Material as per USEPA - see note on page 186.

PAG0026 54

HD00044076

TWO WORLD TRADE CENTER
FLOOR: 73

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
7176	2WTC-07176	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR.	5% CHRYSOTILE ASBESTOS
7177	2WTC-07177	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR.	15% CHRYSOTILE ASBESTOS

PA0002635

HD00044077

TWO WORLD TRADE CENTER
FLOOR: 72

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6011	2WTC-06011	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE EAST WALL CONVECTOR.	1-5% CHRYSOTILE ASBESTOS
6016	2WTC-06016	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED WITHIN THE NORTH WALL CONVECTOR.	1-5% CHRYSOTILE ASBESTOS

PA0002636

HD00044078

TWO WORLD TRADE CENTER
FLOOR: 7A

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
137	2WTC-07137	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	40% CHRYSOTILE ASBESTOS
137	2WTC-07138	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	30% CHRYSOTILE ASBESTOS
137	2WTC-07139	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	30% CHRYSOTILE ASBESTOS
137	2WTC-07140	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	30% CHRYSOTILE ASBESTOS
137	2WTC-07141	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	30% CHRYSOTILE ASBESTOS
137	2WTC-07142	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	15% CHRYSOTILE ASBESTOS
137	2WTC-07143	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	15% CHRYSOTILE ASBESTOS
137	2WTC-07144	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	15% CHRYSOTILE ASBESTOS
137	2WTC-137C5	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
139	2WTC-139C5	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM AT THE NORTH WALL IN THE PLENUM OF THE OF THE NORTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
140	2WTC-07137	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 140.	40% CHRYSOTILE ASBESTOS
140	2WTC-07138	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 140.	30% CHRYSOTILE ASBESTOS
140	2WTC-07139	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 140.	5% CHRYSOTILE ASBESTOS
140	2WTC-07140	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 140.	70% CHRYSOTILE ASBESTOS
140	2WTC-140C5	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
141	2WTC-07145	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 141.	50% CHRYSOTILE ASBESTOS
141	2WTC-07146	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 141.	30% CHRYSOTILE ASBESTOS

PA0002657

HD00044079

TWO WORLD TRADE CENTER
FLOOR: 7A

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
137	2WTC-07137	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	40% CHRYSOTILE ASBESTOS
137	2WTC-07138	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	30% CHRYSOTILE ASBESTOS
137	2WTC-07139	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	30% CHRYSOTILE ASBESTOS
137	2WTC-07140	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	30% CHRYSOTILE ASBESTOS
137	2WTC-07141	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	30% CHRYSOTILE ASBESTOS
137	2WTC-07142	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	15% CHRYSOTILE ASBESTOS
137	2WTC-07143	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	15% CHRYSOTILE ASBESTOS
137	2WTC-07144	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 137 AND 138.	10% CHRYSOTILE ASBESTOS
137	2WTC-137C5	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
139	2WTC-139C5	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM AT THE NORTH WALL IN THE PLENUM OF THE OF THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
140	2WTC-07137	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 140.	60% CHRYSOTILE ASBESTOS
140	2WTC-07138	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 140.	30% CHRYSOTILE ASBESTOS
140	2WTC-07139	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 140.	3% CHRYSOTILE ASBESTOS
140	2WTC-07140	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 140.	70% CHRYSOTILE ASBESTOS
140	2WTC-140C5	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
141	2WTC-07145	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 141.	30% CHRYSOTILE ASBESTOS
141	2WTC-07146	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 141.	30% CHRYSOTILE ASBESTOS

PA0002657

HD00044079

TWO WORLD TRADE CENTER
FLOOR: 74

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
141	2WTC-07147	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 141.	30% CHRYSOTILE ASBESTOS
141	2WTC-07148	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLE 141.	10% CHRYSOTILE ASBESTOS
141	2WTC-141CS	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
142	2WTC-07149	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 142 AND 143.	25% CHRYSOTILE ASBESTOS
142	2WTC-07150	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 142 AND 143.	15% CHRYSOTILE ASBESTOS
142	2WTC-07151	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 142 AND 143.	10% CHRYSOTILE ASBESTOS
142	2WTC-07152	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE NORTHEAST QUADRANT NEAR SAMPLES 142 AND 143.	20% CHRYSOTILE ASBESTOS
142	2WTC-142CS	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	3% CHRYSOTILE ASBESTOS
143	2WTC-143CS	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
147	2WTC-147CS	FLUFFY FALLOUT MATERIAL IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
149	2WTC-149CS	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	15% CHRYSOTILE ASBESTOS
152	2WTC-152CS	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OF THE SOUTHEAST QUADRANT.	25% CHRYSOTILE ASBESTOS
153	2WTC-153CS	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
157	2WTC-157CS	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
160	2WTC-160CS	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
161	2WTC-161CS	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
164	2WTC-164CS	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS

PAG0002638

TWO WORLD TRADE CENTER
FLOOR: 7A

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
165	2WTC-165C5	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
12904	2WTC-12904	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	10% CHRYSOTILE ASBESTOS
12906	2WTC-12906	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE CORE IN THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
12908	2WTC-12908	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE CORE IN THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
12910	2WTC-12910	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
12913	2WTC-12913	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
12916	2WTC-12916	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
12920	2WTC-12920	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
12923	2WTC-12923	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE ELECTRICAL CLOSET IN THE SOUTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
12925	2WTC-12925	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE A.C. AIR SHAFT IN THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
12928	2WTC-12928	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	30% CHRYSOTILE ASBESTOS
12929	2WTC-12929	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	65% CHRYSOTILE ASBESTOS
12930	2WTC-12930	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	20% CHRYSOTILE ASBESTOS
12939	2WTC-12939	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE PORTA CORE OFFICE AREA IN THE NORTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
12940	2WTC-12940	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12941	2WTC-12941	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
12942	2WTC-12942	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS

PA0002639

HD00044081

TWO WORLD TRADE CENTER
FLOOR: 74

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12944	2WTC-12944	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
12945	2WTC-12945	FLUFFY SPRAYED ON BEAM INSULATION MATERIAL IN THE PLENUM NEAR THE PIPE SHAFT IN THE SOUTHWEST QUADRANT.	25% CHRYSOTILE ASBESTOS
12946	2WTC-12946	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	30% CHRYSOTILE ASBESTOS
12949	2WTC-12949	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM NEAR THE SOUTHWEST TELEPHONE CLOSET.	10% CHRYSOTILE ASBESTOS
12950	2WTC-12950	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM NEAR PASSENGER ELEVATOR #12 IN THE SOUTHWEST QUADRANT.	35% CHRYSOTILE ASBESTOS
12976	2WTC-12976	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
12977	2WTC-12977	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
12981	2WTC-12981	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
12982	2WTC-12982	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
12987	2WTC-12987	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE NORTHEAST QUADRANT.	10% CHRYSOTILE ASBESTOS
12993	2WTC-12993	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
12994	2WTC-12994	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE NORTHWEST QUADRANT.	20% CHRYSOTILE ASBESTOS
12995	2WTC-12995	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	40% CHRYSOTILE ASBESTOS
12996	2WTC-12996	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHWEST QUADRANT.	45% CHRYSOTILE ASBESTOS
12997	2WTC-12997	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
12998	2WTC-12998	FLUFFY INSULATION MATERIAL SPRAYED ON A JOIST IN THE PLENUM OF THE SOUTHEAST QUADRANT.	45% CHRYSOTILE ASBESTOS
13931	2WTC-13931	CEMENTITIOUS TROWELED ON INSULATION MATERIAL TAKEN FROM A BEAM IN THE PLENUM AT SAMPLE 2WTC-12976.	10% CHRYSOTILE ASBESTOS

PAGE02640

TWO WORLD TRADE CENTER
FLOOR: 7A

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13933	2WTC-13933	CEMENTITIOUS TROWELED ON INSULATION MATERIAL TAKEN FROM THE METAL DECKING IN THE PLENUM OVER SAMPLE 2WTC-12976.	65% CHRYSOTILE ASBESTOS
13934	2WTC-13934	FLUFFY SPRAYED ON INSULATION MATERIAL TAKEN FROM THE METAL DECKING IN THE PLENUM UNDER SAMPLE 2WTC-13933.	5% CHRYSOTILE ASBESTOS
13935	2WTC-13935	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM AT SAMPLE 2WTC-12977.	1-5% CHRYSOTILE ASBESTOS
13937	2WTC-13937	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OVER SAMPLE 2WTC-12977.	20% CHRYSOTILE ASBESTOS
13938	2WTC-13938	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM UNDER UNDER SAMPLE 2WTC-13937.	25% CHRYSOTILE ASBESTOS
13939	2WTC-13938	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM ON THE WALL IN THE PLENUM AT SAMPLE 2WTC-12981.	5% CHRYSOTILE ASBESTOS
13941	2WTC-13941	CEMENTITIOUS SPRAYED ON INSULATION MATERIAL TAKEN FROM THE METAL DECKING IN THE PLENUM OVER SAMPLE 2WTC-12981.	40% CHRYSOTILE ASBESTOS
13942	2WTC-13942	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM UNDER UNDER SAMPLE 2WTC-13941.	1-5% CHRYSOTILE ASBESTOS
13943	2WTC-13943	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM AT SAMPLE 2WTC-12982.	5% CHRYSOTILE ASBESTOS
13945	2WTC-13945	CEMENTITIOUS INSULATION MATERIAL TROWELED ON THE METAL DECK IN THE PLENUM OVER SAMPLE 2WTC-12982.	40% CHRYSOTILE ASBESTOS
13946	2WTC-13946	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM UNDER UNDER SAMPLE 2WTC-13945.	20% CHRYSOTILE ASBESTOS
13947	2WTC-13947	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OVER SAMPLE 2WTC-12987.	25% CHRYSOTILE ASBESTOS
13949	2WTC-13949	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM OVER SAMPLE 2WTC-12987.	30% CHRYSOTILE ASBESTOS
13950	2WTC-13950	FLUFFY INSULATION MATERIAL SPRAYED ON THE METAL DECK IN THE PLENUM UNDER UNDER SAMPLE 2WTC-13949.	10% CHRYSOTILE ASBESTOS

PA0002641

HD00044083

TWO WORLD TRADE CENTER
FLOOR, 75

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1494	2WTC-01494	FLUFFY FALLOUT MATERIAL FROM THE FLOOR LOCATED NEAR THE ACS 75.3 UNIT.	10% CHRYSOTILE ASBESTOS
1531	2WTC-01531	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED NEAR SHAFT ROOM 2-1.	25% CHRYSOTILE ASBESTOS
1641	2WTC-01641	FALLOUT MATERIAL LOCATED INSIDE THE ACS 75.16 UNIT.	3% CHRYSOTILE ASBESTOS
1676	2WTC-01676	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM LOCATED ABOVE THE NORTHEAST RETURN AIR SHAFT.	25% CHRYSOTILE ASBESTOS
1677	2WTC-01677	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ABOVE THE NORTHEAST RETURN AIR SHAFT.	10% CHRYSOTILE ASBESTOS
1730	2WTC-01730	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB LOCATED ABOVE THE E.S.S. E-75-22 UNIT.	10% CHRYSOTILE ASBESTOS
1731	2WTC-01731	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ABOVE THE E.S.S. E-75-22 UNIT.	3% CHRYSOTILE ASBESTOS
1732	2WTC-01732	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB LOCATED ABOVE THE E.S.S. E-75-22 UNIT.	3% CHRYSOTILE ASBESTOS
1733	2WTC-01733	FLUFFY PRE-MOLDED INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED ABOVE THE E.S.S. E-75-22 UNIT.	20% AMOSITE ASBESTOS
1734	2WTC-01734	FLUFFY PRE-MOLDED INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED ABOVE THE E.S.S. E-75-22 UNIT.	30% AMOSITE ASBESTOS
1738	2WTC-01738	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB LOCATED ABOVE THE E.S.S. E-75-21 UNIT.	30% CHRYSOTILE ASBESTOS
1739	2WTC-01739	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ABOVE THE E.S.S. E-75-21 UNIT.	20% CHRYSOTILE ASBESTOS
1740	2WTC-01740	FLUFFY INSULATION MATERIAL SPRAYED ON THE CONCRETE SLAB LOCATED ABOVE THE E.S.S. E-75-21 UNIT.	40% CHRYSOTILE ASBESTOS

PAG002642

HD00044084

TWO WORLD TRADE CENTER
FLOOR: 78

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
8076	2WTC-08076	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON AT WEST WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-1% CHRYSOTILE ASBESTOS
8080	2WTC-08080	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON AT EAST WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-1% CHRYSOTILE ASBESTOS
8083	2WTC-08083	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON AT NORTH WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT.	1-1% CHRYSOTILE ASBESTOS

PA0002043
PA0002043

TWO WORLD TRADE CENTER
FLOOR: 79

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
8132	2WTC-08132	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON AT SOUTH WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	1-2% CHRYSOTILE ASBESTOS

PA0002644

HD00044086

TWO WORLD TRADE CENTER
FLOOR: 81

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
8367	2WTC-08367	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM AT THE EAST WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS
8373	2WTC-08373	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM AT THE SOUTH WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0002645

TWO WORLD TRADE CENTER
FLOOR: 64

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
6613	29TC-06613	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM AT THE NORTH WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0002646

HD00044088

TWO WORLD TRADE CENTER
FLOOR: 86

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
8581	2WTC-08581	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON AT WEST WALL CONVECTOR UNIT IN THE NORTHWEST QUADRANT.	3% CHRYSOTILE ASBESTOS

PA0002647

HD00044089

TWO WORLD TRADE CENTER
FLOOR: 87

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
8441	2WTC-08841	CEMENTITICUS INSULATION MATERIAL SPRAYED ON A BEAM AT THE WEST WALL CONVECTOR IN THE SOUTHWEST QUADRANT.	1-2% CHRYSOTILE ASBESTOS

PA0002648

TWO WORLD TRADE CENTER
FLOOR: 93

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
8755	2WTC-08755	CEMENTITIOUS INSULATION MATERIAL SPRAYED ON A BEAM AT THE WEST WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0002649

HD00044091

TWO WORLD TRADE CENTER
FLOOR: 94

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3474	2WTC-03474	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM AT THE EAST WALL CONVECTOR UNIT IN THE SOUTHEAST QUADRANT.	5% CHRYSOTILE ASBESTOS
3489	2WTC-03489	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM AT THE WEST WALL CONVECTOR UNIT IN THE SOUTHWEST QUADRANT.	5% CHRYSOTILE ASBESTOS
3703	2WTC-03703	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM AT THE NORTH WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT.	1-3% CHRYSOTILE ASBESTOS

PA0002650

HD00044092

TWO WORLD TRADE CENTER
FLOOR: 108

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
1822	TWTC-01822	CEMENTITIOUS INSULATION MATERIAL TAKEN FROM A 12" O.D. HEAT TRANSFER PIPE COUPLING LOCATED IN THE NORTH CORE CORRIDOR.	20% CHRYSOTILE ASBESTOS

PA0002651

HD00044093

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
ONE WORLD TRADE CENTER

ELEVATOR SHAFT - 01

	SAMPLES
POSITIVE	0
TOTAL	14

ELEVATOR SHAFT - 03

	SAMPLES
POSITIVE	1
TOTAL	12

ELEVATOR SHAFT - 05

	SAMPLES
POSITIVE	3
TOTAL	13

ELEVATOR SHAFT - 07

	SAMPLES
POSITIVE	0
TOTAL	28

ELEVATOR SHAFT - 08

	SAMPLES
POSITIVE	0
TOTAL	14

ELEVATOR SHAFT - 09

	SAMPLES
POSITIVE	0
TOTAL	1

PA0002652

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

ELEVATOR SHAFT - 10

	SAMPLES
POSITIVE	4
TOTAL	5

ELEVATOR SHAFT - 11

	SAMPLES
POSITIVE	11
TOTAL	13

ELEVATOR SHAFT - 13

	SAMPLES
POSITIVE	0
TOTAL	17

ELEVATOR SHAFT - 14

	SAMPLES
POSITIVE	3
TOTAL	14

ELEVATOR SHAFT - 15

	SAMPLES
POSITIVE	0
TOTAL	18

ELEVATOR SHAFT - 16

	SAMPLES
POSITIVE	0
TOTAL	14

PA0002653

HD00044095

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

ELEVATOR SHAFT - 21

	SAMPLES
POSITIVE	0
TOTAL	16

ELEVATOR SHAFT - 22

	SAMPLES
POSITIVE	0
TOTAL	17

ELEVATOR SHAFT - 24

	SAMPLES
POSITIVE	4
TOTAL	4

ELEVATOR SHAFT - 29

	SAMPLES
POSITIVE	4
TOTAL	4

ELEVATOR SHAFT - 31

	SAMPLES
POSITIVE	5
TOTAL	5

ELEVATOR SHAFT - 33

	SAMPLES
POSITIVE	5
TOTAL	5

PA0002654

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

ELEVATOR SHAFT - 38

	SAMPLES
POSITIVE	7
TOTAL	7

ELEVATOR SHAFT - 41

	SAMPLES
POSITIVE	7
TOTAL	7

ELEVATOR SHAFT - 44

	SAMPLES
POSITIVE	7
TOTAL	7

ELEVATOR SHAFT - 43

	SAMPLES
POSITIVE	5
TOTAL	6

ELEVATOR SHAFT - 44

	SAMPLES
POSITIVE	0
TOTAL	36

ELEVATOR SHAFT - 32

	SAMPLES
POSITIVE	0
TOTAL	4

PA0002655

HD00044097

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

ELEVATOR SHAFT - 54

	SAMPLES
POSITIVE	4
TOTAL	4

ELEVATOR SHAFT - 57

	SAMPLES
POSITIVE	3
TOTAL	3

ELEVATOR SHAFT - 62

	SAMPLES
POSITIVE	0
TOTAL	3

ELEVATOR SHAFT - 64

	SAMPLES
POSITIVE	0
TOTAL	7

ELEVATOR SHAFT - 66

	SAMPLES
POSITIVE	6
TOTAL	6

ELEVATOR SHAFT - 68

	SAMPLES
POSITIVE	0
TOTAL	10

PA0002656

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

ELEVATOR SHAFT - 74

	SAMPLES
POSITIVE	0
TOTAL	7

ELEVATOR SHAFT - 75

	SAMPLES
POSITIVE	0
TOTAL	4

ELEVATOR SHAFT - 78

	SAMPLES
POSITIVE	0
TOTAL	4

ELEVATOR SHAFT - 81

	SAMPLES
POSITIVE	0
TOTAL	5

ELEVATOR SHAFT - 83

	SAMPLES
POSITIVE	0
TOTAL	5

ELEVATOR SHAFT - 87

	SAMPLES
POSITIVE	0
TOTAL	7

PA0002657

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

ELEVATOR SHAFT - #2

	SAMPLES
POSITIVE	0
TOTAL	7

ELEVATOR SHAFT - #3

	SAMPLES
POSITIVE	0
TOTAL	8

ELEVATOR SHAFT - #4

	SAMPLES
POSITIVE	0
TOTAL	8

PA0002658

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 03

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14938	2WTC-14938	FLUFFY INSULATION MATERIAL SPRAYED ON THE WEST WALL ABOVE THE 10TH FLOOR.	75% CHRYSOTILE ASBESTOS

PA0002659

HD00044101

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 03

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14978	2WTC-14978	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 9TH FLOOR.	25% CHRYSOTILE ASBESTOS
14980	2WTC-14980	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 13TH FLOOR.	25% CHRYSOTILE ASBESTOS
14983	2WTC-14983	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 23RD FLOOR.	25% CHRYSOTILE ASBESTOS
14985	2WTC-14985	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 28TH FLOOR.	30% CHRYSOTILE ASBESTOS
14988	2WTC-14988	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE EAST WALL ABOVE THE 39TH FLOOR.	25% CHRYSOTILE ASBESTOS

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 10

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12678	2WTC-12678	FLUFFY INSULATION MATERIAL SPRAYED ON THE SOUTH OF THE CONCOURSE LEVEL DOORS.	20% CHRYSOTILE ASBESTOS
12680	2WTC-12680	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE NORTHWEST CORNER.	20% CHRYSOTILE ASBESTOS
12681	2WTC-12681	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE NORTH WALL.	20% CHRYSOTILE ASBESTOS
12682	2WTC-12682	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE NORTH WALL.	5% CHRYSOTILE ASBESTOS

PA0002661

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 11

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
12675	2WTC-12675	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE SOUTH WALL.	15% CHRYSOTILE ASBESTOS
12676	2WTC-12676	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE SOUTHWEST CORNER.	15% CHRYSOTILE ASBESTOS
12677	2WTC-12677	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE SOUTH WALL.	15% CHRYSOTILE ASBESTOS
14955	2WTC-14955	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE SOUTH WALL ABOVE THE 44TH FLOOR.	10% CHRYSOTILE ASBESTOS
14956	2WTC-14956	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE SOUTH WALL ABOVE THE 40TH FLOOR.	10% CHRYSOTILE ASBESTOS TRACE AMOSITE ASBESTOS
14958	2WTC-14958	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE SOUTH WALL ABOVE THE 36TH FLOOR.	20% CHRYSOTILE ASBESTOS
14960	2WTC-14960	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE SOUTH WALL ABOVE THE 30TH FLOOR.	10% CHRYSOTILE ASBESTOS
14961	2WTC-14961	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE SOUTH WALL ABOVE THE 28TH FLOOR.	20% CHRYSOTILE ASBESTOS
14962	2WTC-14962	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ON THE SOUTH WALL ABOVE THE 23RD FLOOR.	30% CHRYSOTILE ASBESTOS
14972	2WTC-14972	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE SOUTH WALL ABOVE THE 18TH FLOOR.	10% CHRYSOTILE ASBESTOS
14974	2WTC-14974	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED ON THE SOUTH WALL ABOVE THE 7TH FLOOR.	1-3% CHRYSOTILE ASBESTOS

PA0002662

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 14

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13019	2WTC-13019	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE SOUTH WALL ABOVE THE 11TH FLOOR.	15% CHRYSOTILE ASBESTOS
13020	2WTC-13020	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE SOUTH WALL ABOVE THE 6TH FLOOR.	10% CHRYSOTILE ASBESTOS
13021	2WTC-13021	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED ON THE SOUTH WALL ABOVE THE 1ST FLOOR.	3% CHRYSOTILE ASBESTOS

PA0002663

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 24

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14320	2WTC-14320	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 4TH FLOOR.	5% CHRYSOTILE ASBESTOS
14321	2WTC-14321	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 9TH FLOOR ENTRANCE.	10% CHRYSOTILE ASBESTOS
14322	2WTC-14322	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 12TH FLOOR ENTRANCE.	5% CHRYSOTILE ASBESTOS
14323	2WTC-14323	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 13TH FLOOR ENTRANCE.	10% CHRYSOTILE ASBESTOS

PA0002654

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 29

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14324	2WTC-14324	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 3RD FLOOR.	5% CHRYSOTILE ASBESTOS
14325	2WTC-14325	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 7TH FLOOR.	5% CHRYSOTILE ASBESTOS
14326	2WTC-14326	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 11TH FLOOR ENTRANCE.	15% CHRYSOTILE ASBESTOS
14327	2WTC-14327	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 14TH FLOOR ENTRANCE.	20% CHRYSOTILE ASBESTOS

PA0002665

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 31

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14328	2WTC-14328	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 23RD FLOOR ENTRANCE.	5% CHRYSOTILE ASBESTOS
14329	2WTC-14329	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 20TH FLOOR ENTRANCE.	10% CHRYSOTILE ASBESTOS
14330	2WTC-14330	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 17TH FLOOR ENTRANCE.	5% CHRYSOTILE ASBESTOS
14331	2WTC-14331	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 15TH FLOOR.	5% CHRYSOTILE ASBESTOS
14332	2WTC-14332	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 2ND FLOOR.	35% CHRYSOTILE ASBESTOS

PA0002666

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 33

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14333	2WTC-14333	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 3RD FLOOR.	10% CHRYSOTILE ASBESTOS
14334	2WTC-14334	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 14TH FLOOR.	15% CHRYSOTILE ASBESTOS
14335	2WTC-14335	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 19TH FLOOR ENTRANCE.	15% CHRYSOTILE ASBESTOS
14336	2WTC-14336	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 21ST FLOOR ENTRANCE.	20% CHRYSOTILE ASBESTOS
14337	2WTC-14337	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 23RD FLOOR ENTRANCE.	15% CHRYSOTILE ASBESTOS

PA0002667

IWC WORLD TRADE CENTER
ELEVATOR SHAFT: 16

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14358	IWTC-14358	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 2ND FLOOR.	60% CHRYSOTILE ASBESTOS
14359	IWTC-14359	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 6TH FLOOR.	20% CHRYSOTILE ASBESTOS
14360	IWTC-14360	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 23RD FLOOR.	15% CHRYSOTILE ASBESTOS
14361	IWTC-14361	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 25TH FLOOR ENTRANCE.	20% CHRYSOTILE ASBESTOS
14362	IWTC-14362	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 28TH FLOOR ENTRANCE.	70% CHRYSOTILE ASBESTOS
14363	IWTC-14363	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 30TH FLOOR ENTRANCE.	65% CHRYSOTILE ASBESTOS
14364	IWTC-14364	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 32ND FLOOR ENTRANCE.	60% CHRYSOTILE ASBESTOS

PA0002668

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: #1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14351	2WTC-14351	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 3RD FLOOR.	20% CHRYSOTILE ASBESTOS
14352	2WTC-14352	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 11TH FLOOR.	10% CHRYSOTILE ASBESTOS
14353	2WTC-14353	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 18TH FLOOR.	20% CHRYSOTILE ASBESTOS
14354	2WTC-14354	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 25TH FLOOR ENTRANCE.	20% CHRYSOTILE ASBESTOS
14355	2WTC-14355	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 28TH FLOOR ENTRANCE.	15% CHRYSOTILE ASBESTOS
14356	2WTC-14356	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 30TH FLOOR ENTRANCE.	10% CHRYSOTILE ASBESTOS
14357	2WTC-14357	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 32ND FLOOR ENTRANCE.	10% CHRYSOTILE ASBESTOS

PA0002669

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 4A

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14344	2WTC-14344	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 2ND FLOOR.	40% CHRYSOTILE ASBESTOS
14345	2WTC-14345	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 12TH FLOOR.	30% CHRYSOTILE ASBESTOS
14346	2WTC-14346	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 31ST FLOOR.	25% CHRYSOTILE ASBESTOS
14347	2WTC-14347	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 33RD FLOOR ENTRANCE.	5% CHRYSOTILE ASBESTOS
14348	2WTC-14348	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 35TH FLOOR ENTRANCE.	15% CHRYSOTILE ASBESTOS
14349	2WTC-14349	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 37TH FLOOR ENTRANCE.	30% CHRYSOTILE ASBESTOS
14350	2WTC-14350	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 39TH FLOOR ENTRANCE.	40% CHRYSOTILE ASBESTOS

PA0002670

HD00044112

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 45

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14338	2WTC-14338	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 3RD FLOOR.	30% CHRYSOTILE ASBESTOS
14339	2WTC-14339	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 10TH FLOOR.	20% CHRYSOTILE ASBESTOS
14341	2WTC-14341	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 33RD FLOOR ENTRANCE.	15% CHRYSOTILE ASBESTOS
14342	2WTC-14342	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 36TH FLOOR ENTRANCE.	10% CHRYSOTILE ASBESTOS
14343	2WTC-14343	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 39TH FLOOR ENTRANCE.	25% CHRYSOTILE ASBESTOS

PA0002671

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 3A

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14369	2WTC-14369	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 45TH FLOOR.	70% CHRYSOTILE ASBESTOS
14370	2WTC-14370	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 48TH FLOOR ENTRANCE.	30% CHRYSOTILE ASBESTOS
14371	2WTC-14371	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 51ST FLOOR ENTRANCE.	25% CHRYSOTILE ASBESTOS
14372	2WTC-14372	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 54TH FLOOR ENTRANCE.	75% CHRYSOTILE ASBESTOS

PA0002672

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 57

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14373	2WTC-14373	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 45TH FLOOR.	25% CHRYSOTILE ASBESTOS
14374	2WTC-14374	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 55TH FLOOR ENTRANCE.	40% CHRYSOTILE ASBESTOS
14375	2WTC-14375	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 57TH FLOOR ENTRANCE.	60% CHRYSOTILE ASBESTOS
14376	2WTC-14376	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 59TH FLOOR ENTRANCE.	50% CHRYSOTILE ASBESTOS
14377	2WTC-14377	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 61ST FLOOR ENTRANCE.	75% CHRYSOTILE ASBESTOS

PA0002673

HD00044115

TWO WORLD TRADE CENTER
ELEVATOR SHAFT: 44

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
14707	2WTC-14707	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 43TH FLOOR.	50% CHRYSOTILE ASBESTOS
14708	2WTC-14708	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 51ST FLOOR.	40% CHRYSOTILE ASBESTOS
14709	2WTC-14709	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 57TH FLOOR.	30% CHRYSOTILE ASBESTOS
14710	2WTC-14710	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 63RD FLOOR ENTRANCE.	55% CHRYSOTILE ASBESTOS
14711	2WTC-14711	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 65TH FLOOR ENTRANCE.	5% CHRYSOTILE ASBESTOS
14712	2WTC-14712	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE 67TH FLOOR ENTRANCE.	30% CHRYSOTILE ASBESTOS

PA0002674

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

ELEVATOR PITS - 01-02

	SAMPLES
POSITIVE	0
TOTAL	3

ELEVATOR PITS - 03-04

	SAMPLES
POSITIVE	0
TOTAL	2

ELEVATOR PIT - 05

	SAMPLES
POSITIVE	0
TOTAL	1

ELEVATOR PITS - 06-07

	SAMPLES
POSITIVE	0
TOTAL	2

ELEVATOR PITS - 16-17

	SAMPLES
POSITIVE	0
TOTAL	2

ELEVATOR PITS - 18-19

	SAMPLES
POSITIVE	0
TOTAL	3

PA0002675A

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

ELEVATOR PITS - 20-21

	SAMPLES
POSITIVE	0
TOTAL	3

ELEVATOR PITS - 24-25

	SAMPLES
POSITIVE	1
TOTAL	3

ELEVATOR PIT - 27

	SAMPLES
POSITIVE	0
TOTAL	2

ELEVATOR PITS - 28-29

	SAMPLES
POSITIVE	2
TOTAL	3

ELEVATOR PITS - 30-31

	SAMPLES
POSITIVE	4
TOTAL	4

ELEVATOR PIT - 32

	SAMPLES
POSITIVE	1
TOTAL	1

PA0002675

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
TWO WORLD TRADE CENTER

ELEVATOR PIT - 33

	SAMPLES
POSITIVE	1
TOTAL	1

ELEVATOR PITS - 34-35

	SAMPLES
POSITIVE	1
TOTAL	3

ELEVATOR PIT - 36

	SAMPLES
POSITIVE	1
TOTAL	3

ELEVATOR PITS - 37-38

	SAMPLES
POSITIVE	3
TOTAL	3

ELEVATOR PITS - 39-40

	SAMPLES
POSITIVE	2
TOTAL	2

ELEVATOR PIT - 41

	SAMPLES
POSITIVE	1
TOTAL	3

PAG002676

HD00044119

ELEVATOR PIT - 42

	SAMPLES
POSITIVE	2
TOTAL	3

ELEVATOR PITS - 43-44

	SAMPLES
POSITIVE	1
TOTAL	3

ELEVATOR PITS - 45-46

	SAMPLES
POSITIVE	2
TOTAL	3

ELEVATOR PIT - 47

	SAMPLES
POSITIVE	1
TOTAL	3

ELEVATOR PIT - 48

	SAMPLES
POSITIVE	2
TOTAL	2

ELEVATOR PIT - 49

	SAMPLES
POSITIVE	0
TOTAL	3

PA0002677

TWO WORLD TRADE CENTER
ELEVATOR PITS: 24-25

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3032	2WTC-03032	FLUFFY FALLOUT MATERIAL FROM THE FLOOR LOCATED AT THE B1 LEVEL.	13% CHRYSOTILE ASBESTOS
3033	2WTC-03033	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	13% CHRYSOTILE ASBESTOS

PA0002678

TWO WORLD TRADE CENTER
ELEVATOR PITS: 28-29

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3028	2WTC-03028	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	15% CHRYSOTILE ASBESTOS
3030	2WTC-03030	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	15% CHRYSOTILE ASBESTOS

TWO WORLD TRADE CENTER
ELEVATOR PITS: 30-31

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2347	2WTC-02347	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	13% CHRYSOTILE ASBESTOS
2348	2WTC-02348	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED AT THE B1 LEVEL.	15% CHRYSOTILE ASBESTOS
2349	2WTC-02349	FLUFFY FALLOUT MATERIAL FROM THE FLOOR LOCATED AT THE B1 LEVEL.	20% CHRYSOTILE ASBESTOS
2350	2WTC-02350	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	10% CHRYSOTILE ASBESTOS

PA0002600

TWO WORLD TRADE CENTER
ELEVATOR PIT: 32

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2367	TWTC-02367	FALLOUT MATERIAL FROM THE ELEVATOR PIT FLOOR LOCATED AT THE 33 LEVEL.	15% CHRYSOTILE ASBESTOS

PA0002681

TWO WORLD TRADE CENTER
ELEVATOR PIT: 33

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2348	2WTC-01348	FALLOUT MATERIAL FROM THE ELEVATOR PIT FLOOR LOCATED AT THE 33 LEVEL.	5% CHRYSOTILE ASBESTOS

AC002002

TWO WORLD TRADE CENTER
ELEVATOR PITS: 34-35

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2351	PATC-02351	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	15% CHRYSOTILE ASBESTOS

PA0002633

HD00044126

TWO WORLD TRADE CENTER
ELEVATOR PIT: 36

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3048	2WTC-01048	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B3 LEVEL.	40% CHRYSOTILE ASBESTOS

PA0002684

TWO WORLD TRADE CENTER
ELEVATOR PITS: 37-38

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULTS
2334	2WTC-02334	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	10% CHRYSOTILE ASBESTOS
2333	2WTC-02335	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A COLUMN LOCATED AT THE B1 LEVEL.	15% CHRYSOTILE ASBESTOS
2336	2WTC-02336	FLUFFY FALLOUT MATERIAL FROM THE FLOOR LOCATED AT THE B1 LEVEL.	20% CHRYSOTILE ASBESTOS

PA0002685

TWO WORLD TRADE CENTER
ELEVATOR PITS: 39-40

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2337	IWTC-02337	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	3% CHRYSOTILE ASBESTOS
2338	IWTC-02338	FLUFFY INSULATION MATERIAL SPRAYED ON COLUMN LOCATED AT THE B1 LEVEL.	15% CHRYSOTILE ASBESTOS

PA0002686

TWO WORLD TRADE CENTER
ELEVATOR PIT: 41

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3301	1WTC-01102	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B3 LEVEL.	1% CHRYSOTILE ASBESTOS

PA0002687

HD00044130

TWO WORLD TRADE CENTER
ELEVATOR PIT: 42

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3308	2WTC-03308	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B3 LEVEL.	15% CHRYSOTILE ASBESTOS
3310	2WTC-03310	FALLOUT MATERIAL FROM THE ELEVATOR PIT FLOOR LOCATED AT THE B3 LEVEL.	13% CHRYSOTILE ASBESTOS

PA0002668

TWO WORLD TRADE CENTER
ELEVATOR PITS, 43-44

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3037	2WTC-03037	FLUFFY FALLOUT MATERIAL FROM THE FLOOR LOCATED AT THE B1 LEVEL.	15% CHRYSOTILE ASBESTOS
3039	2WTC-03039	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	10% CHRYSOTILE ASBESTOS

PA0002689

TWO WORLD TRADE CENTER
ELEVATOR PITS: A5-A6

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3034	2WTC-03034	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	15% CHRYSOTILE ASBESTOS
3036	2WTC-03036	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B1 LEVEL.	15% CHRYSOTILE ASBESTOS

PA0002690

HD00044133

TWO WORLD TRADE CENTER
ELEVATOR PIT: 47

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
3305	2WTC-03305	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B3 LEVEL.	15% CHRYSOTILE ASBESTOS

PA0002691

TWO WORLD TRADE CENTER
ELEVATOR PIT: 48

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2564	2WTC-02564	FLUFFY INSULATION MATERIAL SPRAYED ON A COLUMN LOCATED AT THE B3 LEVEL.	10% CHRYSOTILE ASBESTOS
2565	2WTC-02565	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED AT THE B3 LEVEL.	10% CHRYSOTILE ASBESTOS

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
THREE WORLD TRADE CENTER

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
1	10	10

PA0002693

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
THREE WORLD TRADE CENTER

FLOOR - 1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	FITTING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	10	10	0	0	0	0

PA0002694

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
FOUR WORLD TRADE CENTER

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
2	43	43
3	43	43
4	43	43
5	43	43
6	86	86
7	61	61
8	30	30
9	43	43

PA0002695

HD00044138

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
FOUR WORLD TRADE CENTER

FLOOR - 2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	45	43	0	2	0	0

FLOOR - 3

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	45	45	0	0	0	0

FLOOR - 4

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	45	45	0	0	0	0

FLOOR - 5

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	45	45	0	0	0	0

FLOOR - 6

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	86	86	0	0	0	0

PA00002696

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
FOUR WORLD TRADE CENTER

FLOOR - 7

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	6	0	0	6	0	0
TOTAL	61	61	6	0	0	0

FLOOR - 8

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	30	30	0	0	0	0

FLOOR - 9

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	83	63	0	17	1	0

PA0002697

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
FIVE WORLD TRADE CENTER

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
1	28	28
2	94	94
3	92	92
4	84	84
6	111	111
7	98	98
8	89	89

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
FIVE WORLD TRADE CENTER

FLOOR - 1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	38	28	0	10	0	0

FLOOR - 2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	0	0	3	0	0
TOTAL	98	94	0	4	0	0

FLOOR - 3

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	92	92	0	0	0	0

FLOOR - 4

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	1	0	0	0
TOTAL	90	84	6	0	0	0

FLOOR - 5

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	6	6	0	0	0	0
TOTAL	102	96	6	0	0	0

PA0002698

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
FIVE WORLD TRADE CENTER

FLOOR - 6

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	111	111	0	0	0	0

FLOOR - 7

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	96	96	0	0	0	0

FLOOR - 8

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	90	89	0	1	0	0

FLOOR - 9

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	3	1	0	2	0	0
TOTAL	132	86	0	33	9	1

PAG002699

FIVE WORLD TRADE CENTER
FLOOR: 2

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10776	5WTC-13776	CEMENTITIOUS INSULATION MATERIAL TAKEN FROM A HEAT TRANSFER PIPE ELBOW LOCATED IN THE NORTHWEST QUADRANT OF THE EAST WING.	80% CHRYSOTILE ASBESTOS
13369	5WTC-13369	FIBROUS PRE-MOLDED INSULATION MATERIAL TAKEN FROM AN EXPOSED DUCT LOCATED IN SHAFT NO. 4A. OF THE WEST WING.	50% CHRYSOTILE ASBESTOS
13370	5WTC-13370	CEMENTITIOUS INSULATION MATERIAL TROWELED ON AN EXPOSED DUCT LOCATED IN SHAFT NO. 4A OF THE WEST WING.	50% CHRYSOTILE ASBESTOS

PA0002700

FIVE WORLD TRADE CENTER
FLOOR: 6

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10302	5WTC-10302	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM AT THE EAST WALL CONVECTOR UNIT IN THE NORTHEAST QUADRANT OF THE SOUTH WING.	1-2% CHRYSOTILE ASBESTOS

PA0002701

FIVE WORLD TRADE CENTER
FLOOR: 5

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
11048	5WTC-11048	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT OF THE SOUTH WING.	70% CHRYSOTILE ASBESTOS
11048	5WTC-14296	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT OF SOUTH WING.	NON ASBESTOS
11048	5WTC-14297	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT OF THE SOUTH WING.	70% CHRYSOTILE ASBESTOS
11048	5WTC-14298	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT OF THE SOUTH WING.	25% CHRYSOTILE ASBESTOS
11048	5WTC-14299	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT OF THE SOUTH WING.	35% CHRYSOTILE ASBESTOS
11048	5WTC-14300	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT OF THE SOUTH WING.	75% CHRYSOTILE ASBESTOS
11048	5WTC-14301	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM IN THE PLENUM OF THE SOUTHWEST QUADRANT OF THE SOUTH WING.	70% CHRYSOTILE ASBESTOS

PA0002702

FIVE WORLD TRADE CENTER
FLOOR: 9

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2270	5WTC-02270	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED WEST OF ACS-9-1N UNIT IN THE MECHANICAL EQUIPMENT ROOM.	40% AMOSITE ASBESTOS 40% CHRYSOTILE ASBESTOS
2273	5WTC-02273	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED WEST OF THE RETURN AIR SHAFT.	60% CHRYSOTILE ASBESTOS
2274	5WTC-02274	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM WEST OF THE RETURN AIR SHAFT.	50% CHRYSOTILE ASBESTOS

PA0002703

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
SIX WORLD TRADE CENTER

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
2	10	10

PA0002704

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
SIX WORLD TRADE CENTER

FLOOR - 2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	10	10	0	0	0	0

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
NORTHEAST W.T.C. SUBLEVELS

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
81	19	19
82	90	90
84	73	73

PA0002706

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
NORTHEAST W.T.C. SUBLEVELS

FLOOR - B1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	1	0	0	1	0	0
TOTAL	45	19	0	20	6	0

FLOOR - B2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	95	90	0	5	0	0

FLOOR - BA

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	75	75	0	0	0	0

PA0002707

NORTHEAST W.T.C. SUBLEVELS
FLOOR: B1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
2088	SUTC-C2088	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE ELBOW AT SWE-B2-1A UNIT IN THE MECHANICAL EQUIPMENT ROOM.	5% CHRYSOTILE ASBESTOS

PA0002708

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
NORTHWEST V.T.C. SUBLEVELS

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
B3	28	28

PA0002709

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
NORTHWEST V.T.C. SUBLEVELS

FLOOR - B1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	28	27	0	1	0	0
TOTAL	88	77	0	10	1	0

FLOOR - B2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	14	10	0	3	1	0
TOTAL	54	40	0	13	1	0

FLOOR - B3

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	41	28	0	12	1	0

FLOOR - B4

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	4	3	0	1	0	0
TOTAL	30	25	0	4	1	0

FLOOR - B5

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	3	0	0	3	0	0

PA0002710

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
NORTHWEST M.E.C. SUBLEVELS

FLOOR - B6

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	15	0	0	15	0	0

PA0002711

WD00044155

NORTHWEST W.T.C. SUBLEVELS
FLOOR: B1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
477	1WTC-00477	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM LOCATED NEAR THE BARCLAY STREET RAMP.	5% CHRYSOTILE ASBESTOS
478	1WTC-00478	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED NEAR THE BARCLAY STREET RAMP.	5% CHRYSOTILE ASBESTOS
482	1WTC-00482	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED NEAR THE BARCLAY STREET RAMP.	5% CHRYSOTILE ASBESTOS
483	1WTC-00483	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED NEAR THE BARCLAY STREET RAMP.	10% CHRYSOTILE ASBESTOS
485	1WTC-00485	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED NEAR THE BARCLAY STREET RAMP.	10% CHRYSOTILE ASBESTOS
487	1WTC-00487	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED NEAR THE BARCLAY STREET RAMP.	5% CHRYSOTILE ASBESTOS
488	1WTC-00488	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED NEAR THE BARCLAY STREET RAMP.	5% CHRYSOTILE ASBESTOS
489	1WTC-00489	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED NEAR THE BARCLAY STREET RAMP.	5% CHRYSOTILE ASBESTOS
832	1WTC-00832	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE INVILCO VENDING ROOM.	20% CHRYSOTILE ASBESTOS
833	1WTC-00833	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE INVILCO VENDING ROOM.	20% CHRYSOTILE ASBESTOS
83A	1WTC-0083A	CEMENTITIOUS INSULATION MATERIAL FROM A 8" O.D. HEAT TRANSFER PIPE COUPLING LOCATED WITHIN THE INVILCO VENDING ROOM.	10% CHRYSOTILE ASBESTOS
10464	1WTC-10464	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE EAST SIDE OF THE W.T.C. MAINTENANCE STOCKROOM.	25% CHRYSOTILE ASBESTOS
10465	1WTC-10465	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE SOUTH SIDE OF THE W.T.C. MAINTENANCE STOCKROOM.	20% CHRYSOTILE ASBESTOS
10466	1WTC-10466	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM EXPOSED AT THE SOUTH SIDE OF THE W.T.C. MAINTENANCE STOCKROOM.	30% CHRYSOTILE ASBESTOS
10467	1WTC-10467	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE SOUTH WEST CORNER OF THE W.T.C. MAINTENANCE STOCKROOM.	30% CHRYSOTILE ASBESTOS
10469	1WTC-10469	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE WEST SIDE OF THE W.T.C. MAINTENANCE STOCKROOM.	20% CHRYSOTILE ASBESTOS
10470	1WTC-10470	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE NORTH SIDE OF THE W.T.C. MAINTENANCE STOCKROOM AT COLUMN J-21.	40% CHRYSOTILE ASBESTOS

PA0002712

NORTHWEST W.T.C. SUBLEVELS
FLOOR: B1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
10471	1WTC-10471	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE NORTH SIDE OF THE W.T.C. MAINTENANCE STOCKROOM.	15% CHRYSOTILE ASBESTOS
10472	1WTC-10472	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE NORTH SIDE OF THE W.T.C. STOCKROOM.	20% CHRYSOTILE ASBESTOS
10474	1WTC-10474	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED EAST OF COLUMN J-21 IN THE W.T.C. MAINTENANCE STOCKROOM.	60% CHRYSOTILE ASBESTOS
10475	1WTC-10475	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE WEST SIDE OF THE W.T.C. MAINTENANCE STOCKROOM.	60% CHRYSOTILE ASBESTOS
10479	1WTC-10479	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM EXPOSED AT THE SOUTH SIDE OF THE W.T.C. MAINTENANCE STOCKROOM.	70% CHRYSOTILE ASBESTOS
13271	6WTC-13271	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED BEAM LOCATED ABOVE THE TRUCK DOCK AREA NEAR COLUMN J72.4.	30% CHRYSOTILE ASBESTOS
14250	6WTC-14250	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED BEAM LOCATED IN THE OLD U.S. CUSTOMS HOUSE PARKING AREA NEAR COLUMN J2-4.	1-5% CHRYSOTILE ASBESTOS
14252	6WTC-14252	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED BEAM LOCATED IN THE OLD U.S. CUSTOMS HOUSE PARKING AREA NEAR COLUMN J2-4.	50% CHRYSOTILE ASBESTOS
14253	6WTC-14253	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED BEAM LOCATED ABOVE THE BARCLAY STREET RAMP NEAR COLUMN J2-20.	40% CHRYSOTILE ASBESTOS
14496	6WTC-14496	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED BEAM LOCATED AT THE EAST WALL SOUTH OF COLUMN J12-1.	35% CHRYSOTILE ASBESTOS
14499	6WTC-14499	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED BEAM SOUTH OF COLUMN J12-1.	60% CHRYSOTILE ASBESTOS

PA0002713

NORTHWEST W.T.C. SUBLEVELS
FLOOR: S2

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
659	1WTC-00659	FLUFFY INSULATION MATERIAL SPRAYED ON A TRUSS LOCATED AT COLUMN J3-4.	10% CHRYSOTILE ASBESTOS
660	1WTC-00660	FLUFFY INSULATION MATERIAL SPRAYED ON A TRUSS LOCATED AT COLUMN J4-4.	10% CHRYSOTILE ASBESTOS
661	1WTC-00661	CEMENTITIOUS INSULATION MATERIAL TROWELED ON A BEAM LOCATED AT COLUMN J2-7.	5% CHRYSOTILE ASBESTOS
662	1WTC-00662	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED BETWEEN COLUMNS J2-7 AND J3-6.	15% CHRYSOTILE ASBESTOS
666	1WTC-00666	FLUFFY FALLOUT MATERIAL FROM THE FLOOR LOCATED NEAR COLUMN J3-4.	15% CHRYSOTILE ASBESTOS
668	1WTC-00668	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE ELBOW LOCATED BY COLUMN J7-12.	15% AMOSITE ASBESTOS 5% CHRYSOTILE ASBESTOS
669	1WTC-00669	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED BY COLUMN J8-10.	15% CHRYSOTILE ASBESTOS
670	1WTC-00670	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE LOCATED BY COLUMN J9-8.	15% CHRYSOTILE ASBESTOS
13277	6WTC-13277	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED TRUSS IN THE PARKING AREA NEAR COLUMN J4-1.	30% CHRYSOTILE ASBESTOS
13280	6WTC-13280	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED TRUSS LOCATED IN THE PARKING AREA NEAR COLUMN J3.4.	45% CHRYSOTILE ASBESTOS
13281	6WTC-13281	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED BEAM LOCATED IN THE PARKING AREA BETWEEN COLUMNS J3.6 AND J4.3.	20% CHRYSOTILE ASBESTOS
13284	6WTC-13284	CEMENTITIOUS INSULATION MATERIAL TROWELED ON AN EXPOSED BEAM LOCATED NEAR RAMP "F" BY COLUMN J72.6.	5% CHRYSOTILE ASBESTOS
13298	6WTC-13298	FLUFFY INSULATION MATERIAL SPRAYED ON AN EXPOSED BEAM LOCATED IN THE PARKING AREA NEAR COLUMN J75.6.	1-5% CHRYSOTILE ASBESTOS
13299	6WTC-13299	CEMENTITIOUS INSULATION MATERIAL TROWELED ON AND EXPOSED BEAM LOCATED IN THE PARKING AREA NEAR COLUMN J75.7.	5% CHRYSOTILE ASBESTOS

PA0002714

NORTHWEST W.T.C. SUBLEVELS
FLOOR: B4

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
617	1WTC-00617	FLUFFY SPRAYED ON TRUSS INSULATION MATERIAL BETWEEN COLUMNS J-3-16 AND J-4-16.	5% CHRYSOTILE ASBESTOS
621	1WTC-00621	FALLOUT MATERIAL FROM TRUSS BETWEEN COLUMNS J-5-14 AND J-6-13.	5% CHRYSOTILE ASBESTOS
626	1WTC-00626	FLUFFY INSULATION MATERIAL SPRAYED ON COLUMN J-73-2.	30% CHRYSOTILE ASBESTOS
627	1WTC-00627	TROWELED ON PATCH INSULATION MATERIAL ON A BEAM NEAR COLUMN J-73-2.	3% CHRYSOTILE ASBESTOS
628	1WTC-00628	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM NEAR COLUMN J-74-2.	25% CHRYSOTILE ASBESTOS
629	1WTC-00629	CEMENTITIOUS INSULATION MATERIAL ON A PIPE AT COLUMN J-6-10.	25% CHRYSOTILE ASBESTOS

PA0002715

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
SOUTHEAST W.T.C. SUBLEVELS

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
B1	24	24
B2	86	86
B4	27	27

PA0002716

HD00044160

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
SOUTHEAST W.T.C. SUBLEVELS

FLOOR - B1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	37	24	0	13	0	0

FLOOR - B2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	96	86	0	10	0	0

FLOOR - B4

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	27	27	0	0	0	0

PA0002717

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
SOUTHWEST W.T.C. SUBLEVELS

FLOORS WITH NON-ACM CEILING STRUCTURES

FLOOR	SAMPLES	NON-ACM SAMPLES
B3	11	11
B4	3	3
B6	10	10

PA0002718

HD00044162

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
SOUTHWEST W.T.C. SUBLEVELS

FLOOR - B1

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	30	16	0	14	0	0
TOTAL	253	185	0	65	3	0

FLOOR - B2

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	4	2	0	2	0	0
TOTAL	45	23	0	22	0	0

FLOOR - B3

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	28	11	0	17	0	0

FLOOR - B4

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	19	3	0	7	0	0

FLOOR - B5

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	19	0	0	19	0	0

PA0002719

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
SOUTHWEST W.T.C. SUBLEVELS

FLOOR - B6

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	28	0	0	28	0	0
TOTAL	68	10	0	78	0	0

PA0002720

SOUTHWEST V.T.C. SYLLEVELS
FLOOR: B1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
784	1WTC-00784	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE POLICE TERMINAL ROOM.	10% CHRYSOTILE ASBESTOS
785	1WTC-00785	FLUFFY INSULATION MATERIAL FROM A 6" O.D. HEAT TRANSFER PIPE LOCATED IN THE POLICE TERMINAL ROOM.	20% AMOSITE ASBESTOS 5% CHRYSOTILE ASBESTOS
786	1WTC-00786	FLUFFY INSULATION MATERIAL FROM A 8" O.D. HEAT TRANSFER PIPE LOCATED IN THE POLICE TERMINAL ROOM.	25% AMOSITE ASBESTOS
789	1WTC-00789	FLUFFY INSULATION MATERIAL FROM A 8" O.D. HEAT TRANSFER PIPE LOCATED IN THE POLICE CORRIDOR.	30% AMOSITE ASBESTOS
814	1WTC-00814	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF THE INHILCO CORRIDOR.	15% CHRYSOTILE ASBESTOS
815	1WTC-00815	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE INHILCO ENGINEERING SHOP.	15% CHRYSOTILE ASBESTOS
816	1WTC-00816	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE INHILCO ENGINEERING SHOP.	20% CHRYSOTILE ASBESTOS
818	1WTC-00818	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED WITHIN THE INHILCO ENGINEERING SHOP.	15% CHRYSOTILE ASBESTOS
820	1WTC-00820	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF THE INHILCO LOCKER AREA.	35% CHRYSOTILE ASBESTOS
822	1WTC-00822	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF INHILCO LOCKER AREA.	30% CHRYSOTILE ASBESTOS
825	1WTC-00825	FLUFFY INSULATION MATERIAL LOCATED IN THE PLENUM OF THE INHILCO CORRIDOR.	20% CHRYSOTILE ASBESTOS
826	1WTC-00826	FLUFFY FALLOUT INSULATION MATERIAL LOCATED WITHIN THE INHILCO COLD KITCHEN.	20% CHRYSOTILE ASBESTOS
827	1WTC-00827	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE PLENUM OF THE INHILCO COLD KITCHEN CLOSET.	25% CHRYSOTILE ASBESTOS
840	1WTC-00840	FLUFFY INSULATION MATERIAL FROM A 4" O.D. HEAT TRANSFER PIPE LOCATED WITHIN THE INHILCO CANNED FOOD STORAGE ROOM.	30% AMOSITE ASBESTOS 10% CHRYSOTILE ASBESTOS
878	1WTC-00878	FLUFFY INSULATION MATERIAL FROM A 8" O.D. HIGH PRESSURE STEAM PIPE LOCATED ABOVE THE LOADING DOCK PLATFORM.	20% AMOSITE ASBESTOS 5% CHRYSOTILE ASBESTOS
887	1WTC-00887	CEMENTITIOUS INSULATION MATERIAL FROM A HIGH PRESSURE STEAM PIPE ELBOW LOCATED ABOVE THE LOADING DOCK PLATFORM.	20% AMOSITE ASBESTOS
888	1WTC-00888	CEMENTITIOUS INSULATION MATERIAL FROM A 12" O.D. HIGH PRESSURE STEAM PIPE LOCATED ABOVE THE LOADING DOCK PLATFORM.	60% AMOSITE ASBESTOS

PA0002721

SOUTHWEST W.T.C. SUBLEVELS
FLOOR: B1

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
9017	2WTC-09017	CEMENTITIOUS INSULATION MATERIAL FROM A 24" O.D. HEAT TRANSFER PIPE GATE VALVE STEM LOCATED WITHIN THE TRUCK DOCK AREA VALVE ROOM.	70% CHRYSOTILE ASBESTOS
13219	0WTC-13219	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED ABOVE THE EXIT SIDE OF RAMP "H".	40% CHRYSOTILE ASBESTOS
13221	0WTC-13221	FLUFFY INSULATION MATERIAL SPRAYED ON A CONCRETE SLAB LOCATED ABOVE THE EXIT SIDE OF RAMP "H".	30% CHRYSOTILE ASBESTOS
13237	0WTC-13237	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED NEAR THE VISTA HOTEL GENERAL STORAGE ROOM.	35% CHRYSOTILE ASBESTOS
13238	0WTC-13238	FLUFFY INSULATION MATERIAL SPRAYED ON A BEAM LOCATED IN THE VISTA HOTEL GENERAL STORAGE ROOM.	35% CHRYSOTILE ASBESTOS
13249	0WTC-13249	CEMENTITIOUS INSULATION MATERIAL FROM A 4" O.D. HEAT TRANSFER PIPE VALVE LOCATED IN THE NORTHEAST CORNER OF THE IDELCO MECHANICAL EQUIPMENT ROOM.	20% CHRYSOTILE ASBESTOS
13254	0WTC-13254	CEMENTITIOUS INSULATION MATERIAL FROM A 4" O.D. HEAT TRANSFER PIPE COUPLING LOCATED ON THE LARGE DUCT IN THE IDELCO MECHANICAL EQUIPMENT ROOM.	20% CHRYSOTILE ASBESTOS
14501	0WTC-14501	FLUFFY INSULATION MATERIAL FROM A PAD COVERING A 6" O.D. HEAT TRANSFER PIPE LOCATED WEST OF THE ENTRANCE TO THE ELEVATOR MACHINE ROOM.	1-3% AMOSITE ASBESTOS
14515	0WTC-14515	FLUFFY INSULATION MATERIAL FROM A PRE-MOLDED 10" O.D. HEAT TRANSFER PIPE LOCATED IN THE NORTHEAST CORNER OF THE FIRE COMMAND STATION.	15% AMOSITE ASBESTOS <1% CHRYSOTILE ASBESTOS
15234	0WTC-15234	FIBROUS PRE-MOLDED INSULATION MATERIAL FROM A 20" O.D. HEAT TRANSFER PIPE LOCATED AT THE TRUCK DOCK AREA VALVE ROOM.	90% AMOSITE ASBESTOS
15235	0WTC-15235	FIBROUS PRE-MOLDED INSULATION MATERIAL FROM A 24" O.D. HEAT TRANSFER PIPE LOCATED AT THE TRUCK DOCK AREA VALVE ROOM.	70% CHRYSOTILE ASBESTOS
15237	0WTC-15237	FIBROUS PRE-MOLDED INSULATION MATERIAL FROM A 20" O.D. HEAT TRANSFER PIPE LOCATED AT THE TRUCK DOCK AREA VALVE ROOM.	85% AMOSITE ASBESTOS
15240	0WTC-15240	FIBROUS PRE-MOLDED INSULATION MATERIAL FROM A 24" O.D. HEAT TRANSFER PIPE LOCATED AT THE TRUCK DOCK AREA VALVE ROOM.	90% AMOSITE ASBESTOS

PAG002722

SOUTHWEST W.T.C. SUBLEVELS
FLOOR: 32

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
13306	GWTC-13306	CEMENTITIOUS INSULATION MATERIAL TROWELED ON AN EXPOSED BEAM LOCATED IN THE PARKING AREA NEAR COLUMN K75.19.	3% CHRYSOTILE ASBESTOS
13315	GWTC-13315	CEMENTITIOUS INSULATION MATERIAL TROWELED ON AN EXPOSED BEAM LOCATED IN THE PARKING AREA NEAR COLUMN K70.5.	70% CHRYSOTILE ASBESTOS
13321	GWTC-13321	CEMENTITIOUS INSULATION MATERIAL TAKEN FROM A 3" O.D. HEAT TRANSFER PIPE ELBOW LOCATED ABOVE THE EXIT LANE ALONG THE SOUTH WALL OF TOWER ONE.	1-3% CHRYSOTILE ASBESTOS
13322	GWTC-13322	FIBROUS PRE-MOLDED INSULATION MATERIAL TAKEN FROM A 18" O.D. HEAT TRANSFER PIPE LOCATED ABOVE THE EXIT LANE ALONG THE SOUTH WALL OF TOWER ONE.	1-3% AMOSITE ASBESTOS

SOUTHWEST W.T.C. SUBLEVELS
FLOOR: S6

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
160	1WTC-00160	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
162	1WTC-00162	CEMENTITIOUS INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
163	1WTC-00163	FLUFFY INSULATION MATERIAL IN THE SOUTHWEST CORNER OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
164	1WTC-00164	FLUFFY INSULATION MATERIAL AT THE WEST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
165	1WTC-00165	FLUFFY INSULATION MATERIAL IN THE CEILING OF THE MAINTENANCE STOREROOM.	5% AMOSITE ASBESTOS
166	1WTC-00166	FLUFFY INSULATION MATERIAL IN THE CEILING OF THE MAINTENANCE STOREROOM.	5% AMOSITE ASBESTOS
167	1WTC-00167	FLUFFY INSULATION MATERIAL IN THE CEILING OF THE MAINTENANCE STOREROOM.	5% AMOSITE ASBESTOS
168	1WTC-00168	FLUFFY INSULATION MATERIAL IN THE CEILING OF THE MAINTENANCE STOREROOM.	5% AMOSITE ASBESTOS
275	1WTC-00275	FLUFFY INSULATION MATERIAL AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
276	1WTC-00276	FLUFFY INSULATION MATERIAL AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
279	1WTC-00279	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
280	1WTC-00280	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
281	1WTC-00281	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
283	1WTC-00283	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
287	1WTC-00287	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
289	1WTC-00289	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
291	1WTC-00291	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
293	1WTC-00293	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
294	1WTC-00294	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS

SOUTHWEST W.T.C. SUBLEVELS
FLOOR: 36

AREA NUMBER	SAMPLE NUMBER	LOCATION	RESULT
295	1WTC-00295	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
296	1WTC-00296	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
300	1WTC-00300	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% CHRYSOTILE ASBESTOS
301	1WTC-00301	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
307	1WTC-00307	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
309	1WTC-00309	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
311	1WTC-00311	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% CHRYSOTILE ASBESTOS
312	1WTC-00312	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% AMOSITE ASBESTOS
313	1WTC-00313	FLUFFY INSULATION MATERIAL FROM A HEAT TRANSFER PIPE AT THE EAST WALL OF THE STEAM METER ROOM.	5% CHRYSOTILE ASBESTOS

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING REPORT
RIVER WATER PUMPING STATION

FLOOR - RENT

	SAMPLES	CEILING STRUCTURES	CONVECTOR UNITS	PIPING/HVAC	FALLOUT	OTHER
POSITIVE	0	0	0	0	0	0
TOTAL	0	0	0	4	0	0

PA0002726

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
CONCOURSE

TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
199	10	170	0	21	10	7	0	1	0

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
ONE WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
B1	86	47	58	44	0	0	23	1	1	1	4	1
B2	20	8	9	6	0	0	10	1	1	1	0	0
B3	2	1	0	0	0	0	1	1	0	0	1	0
B4	4	1	0	0	0	0	2	1	1	0	1	0
B5	11	0	3	0	0	0	8	0	0	0	0	0
B6	187	42	81	30	0	0	99	8	7	4	0	0
1	11	3	9	1	0	0	2	2	0	0	0	0
2	20	17	20	17	0	0	0	0	0	0	0	0
3	15	15	15	15	0	0	0	0	0	0	0	0
4	12	10	12	10	0	0	0	0	0	0	0	0
5	11	9	12	9	0	0	0	0	0	0	0	0
6	35	27	35	27	0	0	0	0	0	0	0	0
7	84	37	39	31	0	0	43	4	2	2	0	0
9	18	7	16	6	2	1	0	0	0	0	0	0
10	23	21	23	21	0	0	0	0	2	0	0	0
11	21	14	21	14	0	0	0	0	0	0	0	0
12	30	14	25	12	1	1	0	0	0	0	4	1
13	47	32	35	30	12	2	0	0	0	0	0	0
14	19	14	16	12	2	2	0	0	0	0	1	0
15	19	12	16	12	2	0	0	0	0	0	1	0
16	33	21	28	21	5	0	0	0	0	0	0	0
17	47	24	35	24	12	0	0	0	0	0	0	0
18	24	16	19	14	1	1	0	0	0	0	4	1

PA000027 28

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
ONE WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
19	48	33	36	33	12	0	0	0	0	0	0	0
20	21	9	17	9	1	0	0	0	0	0	3	0
21	43	25	32	25	8	0	0	0	0	0	3	0
22	43	29	36	29	5	0	0	0	0	0	2	0
23	28	14	27	14	0	0	0	0	0	0	1	0
24	58	40	46	39	12	1	0	0	0	0	0	0
25	42	32	40	32	2	0	0	0	0	0	0	0
26	23	17	20	15	1	0	0	0	0	0	2	2
27	54	34	42	34	12	0	0	0	0	0	0	0
28	27	21	24	21	0	0	0	0	0	0	3	0
29	12	8	12	8	0	0	0	0	0	0	0	0
30	52	27	40	27	12	0	0	0	0	0	0	0
31	33	32	31	32	4	0	0	0	0	0	0	0
32	147	29	142	29	5	0	0	0	0	0	0	0
33	64	13	32	13	12	0	0	0	0	0	0	0
34	19	7	18	7	0	0	0	0	0	0	1	0
35	47	26	13	26	12	0	0	0	0	0	0	0
36	47	27	35	26	12	1	0	0	0	0	0	0
37	37	19	24	19	13	0	0	0	0	0	0	0
38	78	2	67	2	9	0	0	0	0	0	2	0
39	67	2	61	2	6	0	0	0	0	0	0	0
40	61	33	33	33	7	0	0	0	0	0	1	0
41	83	18	30	3	0	0	52	4	2	1	1	0

PA0002729

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
ONE WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
43	50	0	35	0	12	0	0	0	3	0	0	0
44	48	1	35	0	12	0	1	1	0	0	0	0
45	49	0	48	0	1	0	0	0	0	0	0	0
46	30	0	28	0	2	0	0	0	0	0	0	0
47	30	0	29	0	1	0	0	0	0	0	0	0
48	77	0	74	0	3	0	0	0	0	0	0	0
49	38	0	36	0	2	0	0	0	0	0	0	0
50	53	0	41	0	12	0	0	0	0	0	0	0
51	46	0	44	0	2	0	0	0	0	0	0	0
52	64	0	52	0	12	0	0	0	0	0	0	0
53	44	0	33	0	11	0	0	0	0	0	0	0
54	60	0	57	0	3	0	0	0	0	0	0	0
55	41	0	40	0	1	0	0	0	0	0	0	0
56	44	2	32	0	12	1	0	0	0	0	0	0
57	55	1	43	0	12	1	0	0	0	0	0	0
58	44	0	32	0	12	0	0	0	0	0	0	0
59	44	0	32	0	12	0	0	0	0	0	0	0
60	44	0	32	0	12	0	0	0	0	0	0	0
61	42	0	40	0	2	0	0	0	0	0	0	0
62	44	0	44	0	0	0	0	0	0	0	0	0
63	47	0	32	0	15	0	0	0	0	0	0	0
64	31	0	31	0	0	0	0	0	0	0	0	0
65	67	2	47	0	20	2	0	0	0	0	0	0

PA0002730

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
ONE WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
66	42	0	42	0	0	0	0	0	0	0	0	0
67	50	0	47	0	3	0	0	0	0	0	0	0
68	41	0	41	0	0	0	0	0	0	0	0	0
69	31	0	31	0	0	0	0	0	0	0	0	0
70	43	0	43	0	0	0	0	0	0	0	0	0
71	38	0	38	0	0	0	0	0	0	0	0	0
72	68	4	68	4	0	0	0	0	0	0	0	0
73	54	1	50	0	4	1	0	0	0	0	0	0
74	29	20	29	20	0	0	0	0	0	0	0	0
75	90	18	32	6	0	0	41	10	17	2	0	0
77	44	2	32	0	12	2	0	0	0	0	0	0
78	53	0	41	0	12	0	0	0	0	0	0	0
79	45	1	33	0	12	1	0	0	0	0	0	0
80	47	0	41	0	6	0	0	0	0	0	0	0
81	48	0	45	0	2	0	1	0	0	0	0	0
82	96	18	96	18	0	0	0	0	0	0	0	0
83	38	3	36	3	2	0	0	0	0	0	0	0
84	43	0	42	0	1	0	0	0	0	0	0	0
85	44	0	32	0	12	0	0	0	0	0	0	0
86	25	0	25	0	0	0	0	0	0	0	0	0
87	39	0	38	0	1	0	0	0	0	0	0	0
88	44	1	32	0	12	1	0	0	0	0	0	0
89	44	0	32	0	12	0	0	0	0	0	0	0

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
ONE WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
90	44	0	32	0	12	0	0	0	0	0	0	0
91	31	0	30	0	1	0	0	0	0	0	0	0
92	32	0	30	0	2	0	0	0	0	0	0	0
93	28	0	25	0	3	0	0	0	0	0	0	0
94	43	0	31	0	12	0	0	3	0	0	0	0
95	44	0	32	0	12	0	0	0	0	0	0	0
96	53	0	37	0	16	0	0	0	0	0	0	0
97	44	2	32	0	12	2	0	0	0	0	0	0
98	43	0	32	0	11	0	0	2	0	0	0	0
99	44	0	32	0	12	0	0	0	0	0	0	0
100	57	0	45	0	12	0	0	0	0	0	0	0
101	45	1	33	0	12	1	0	0	0	0	0	0
102	60	2	60	2	0	0	0	0	0	0	0	0
103	44	2	32	0	12	2	0	0	0	0	0	0
104	83	16	82	16	1	0	0	0	0	0	0	0
105	44	1	40	0	4	1	0	0	0	0	0	0
106	66	1	54	0	12	1	0	0	0	0	0	0
107	51	30	39	25	12	5	0	0	0	0	0	0
108	93	3	51	0	8	0	33	3	9	0	0	0
110	7	0	7	0	0	0	0	0	0	0	0	0
*** Total ***												
	3180	1043	4175	960	605	31	318	38	45	11	17	3

PA0002732

HD000044176

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
ONE WORLD TRADE CENTER
ELEVATOR SHAFTS

ELEVATOR SHAFT	TOTAL SAMPLES	POSITIVE SAMPLES
01	8	8
03	18	16
04	10	1
05	13	4
07	24	3
08	28	24
09	4	4
10	13	13
11	4	4
13	19	13
15	19	7
16	17	5
18	17	6
20	16	5
23	14	14
25	4	4
28	18	17
29	4	4
31	6	6
33	6	6
37	3	3
39	3	3
43	8	8

PA0002733

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
ONE WORLD TRADE CENTER
ELEVATOR SHAFTS

ELEVATOR SHAFT	TOTAL SAMPLES	POSITIVE SAMPLES
47	8	8
48	7	7
49	13	11
52	3	3
53	3	3
57	4	4
61	4	4
65	6	5
66	5	4
70	5	0
73	5	5
76	2	0
79	2	0
81	6	0
82	2	0
83	2	0
84	5	0
85	2	0
86	3	0
89	4	0
91	4	0
93	6	0
98	4	0

PA0002734

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
ONE WORLD TRADE CENTER
ELEVATOR SHAFTS

ELEVATOR SHAFT	TOTAL SAMPLES	POSITIVE SAMPLES
*** Total ***	389	238

PA0002735

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
ONE WORLD TRADE CENTER
ELEVATOR PITS

ELEVATOR PIT	TOTAL SAMPLES	POSITIVE SAMPLES
03-04	2	2
08-09	1	1
10-11	1	1
12-13	1	1
14-15	28	20
20-21	2	1
24	1	1
25-26	1	1
29	1	1
30	1	1
33-34	1	1
35	1	1
37-38	1	1
39-40	2	1
43-44	2	2
45-46	1	1
--- Total ---	50	38

PA0002756

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
TWO WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
B1	93	0	77	0	0	0	15	0	1	0	0	0
B2	19	2	8	1	0	0	11	1	0	0	0	0
B3	3	0	1	0	0	0	2	0	0	0	0	0
B4	21	0	1	0	0	0	20	0	0	0	0	0
B6	44	1	26	1	0	0	18	0	0	0	0	0
1	12	3	12	3	0	0	0	0	0	0	0	0
2	9	0	9	0	0	0	0	0	0	0	0	0
3	33	0	33	0	0	0	0	0	0	0	0	0
4	26	0	26	0	0	0	0	0	0	0	0	0
5	21	0	18	0	0	0	0	0	2	0	1	0
6	22	18	22	18	0	0	0	0	0	0	0	0
7	143	75	127	65	0	0	27	7	8	3	1	0
9	74	2	36	0	16	2	0	0	0	0	2	0
10	31	26	30	26	0	0	0	0	0	0	1	0
11	51	32	50	32	0	0	0	0	0	0	1	0
12	35	16	32	16	1	0	0	0	0	0	2	0
13	77	11	66	11	11	0	0	0	0	0	0	0
14	52	1	40	0	12	1	0	0	0	0	0	0
15	32	0	40	0	12	0	0	0	0	0	0	0
16	30	0	38	0	12	0	0	0	0	0	0	0
17	62	0	50	0	12	0	0	0	0	0	0	0
18	52	0	38	0	12	0	1	0	0	0	0	0
19	58	1	42	1	14	0	1	0	0	0	1	0

PA0002757

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
TWO WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
20	92	2	89	2	3	0	0	0	0	0	0	0
21	53	0	42	0	13	0	0	0	0	0	0	0
22	69	1	52	0	16	1	0	0	0	0	0	0
23	52	1	40	0	12	1	0	0	0	0	0	0
24	53	1	40	0	13	1	0	0	0	0	0	0
25	53	0	41	0	12	0	0	0	0	0	0	0
26	73	9	61	9	12	0	0	0	0	0	0	0
27	54	0	42	0	12	0	0	0	0	0	0	0
28	85	0	73	0	12	0	0	0	0	0	0	0
29	51	0	40	0	11	0	0	0	0	0	0	0
30	90	6	78	0	12	0	0	0	0	0	0	0
31	50	0	38	0	12	0	0	0	0	0	0	0
32	57	2	45	2	12	0	0	0	0	0	0	0
33	189	5	171	5	18	0	0	0	0	0	0	0
34	44	0	42	0	2	0	0	0	0	0	0	0
35	52	0	40	0	12	0	0	0	0	0	0	0
36	72	8	60	0	12	8	0	0	0	0	0	0
37	52	0	40	0	12	0	0	0	0	0	0	0
38	52	0	40	0	12	0	0	0	0	0	0	0
39	53	1	41	0	12	1	0	0	0	0	0	0
40	55	22	43	22	12	0	0	0	0	0	0	0
41	133	35	99	31	0	0	22	1	14	3	0	0
42	90	11	72	5	12	0	6	3	0	0	0	0

PA0002738

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
TWO WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
44	53	0	43	0	12	0	0	0	0	0	0	0
45	81	0	55	0	26	0	0	0	0	0	0	0
46	63	5	42	0	21	5	0	0	0	0	0	0
47	63	2	50	0	13	2	0	0	0	0	0	0
48	74	3	49	0	25	3	0	0	0	0	0	0
49	57	0	45	0	12	0	0	0	0	0	0	0
50	52	0	40	0	12	0	0	0	0	0	0	0
51	46	1	33	0	13	1	0	0	0	0	0	0
52	48	0	36	0	12	0	0	0	0	0	0	0
53	44	1	34	0	12	1	0	0	0	0	0	0
54	35	0	23	0	12	0	0	0	0	0	0	0
55	42	0	30	0	12	0	0	0	0	0	0	0
56	44	0	32	0	12	0	0	0	0	0	0	0
57	72	1	60	0	12	1	0	0	0	0	0	0
58	44	0	32	0	12	0	0	0	0	0	0	0
59	108	1	92	0	16	1	0	0	0	0	0	0
60	42	0	30	0	12	0	0	0	0	0	0	0
61	48	0	36	0	12	0	0	0	0	0	0	0
62	48	0	36	0	12	0	0	0	0	0	0	0
63	45	0	33	0	12	0	0	0	0	0	0	0
64	56	0	41	0	15	0	0	0	0	0	0	0
65	57	1	42	0	13	1	0	0	0	0	0	0
66	54	4	41	0	13	4	0	0	0	0	0	0

PA0002739

HD00044183

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
TWO WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
67	44	7	32	0	12	7	0	0	0	0	0	0
68	49	5	37	0	12	5	0	0	0	0	0	0
69	61	0	48	0	13	0	0	0	0	0	0	0
70	42	3	30	0	12	3	0	0	0	0	0	0
71	51	3	36	2	13	1	0	0	0	0	0	0
72	44	2	32	0	12	2	0	0	0	0	0	0
73	44	2	34	0	12	2	0	0	0	0	0	0
74	181	82	167	82	13	0	0	0	0	0	1	0
75	165	13	48	9	0	0	101	2	14	2	0	0
77	47	0	35	0	12	0	0	0	0	0	0	0
78	47	3	33	0	12	3	0	0	0	0	0	0
79	44	1	32	0	12	1	0	0	0	0	0	0
80	44	0	32	0	12	0	0	0	0	0	0	0
81	44	2	32	0	12	2	0	0	0	0	0	0
82	31	0	31	0	0	0	0	0	0	0	0	0
83	44	0	32	0	12	0	0	0	0	0	0	0
84	46	1	34	0	12	1	0	0	0	0	0	0
85	32	0	31	0	1	0	0	0	0	0	0	0
86	44	1	32	0	12	1	0	0	0	0	0	0
87	43	1	31	0	12	1	0	0	0	0	0	0
88	32	0	30	0	2	0	0	0	0	0	0	0
89	32	0	30	0	2	0	0	0	0	0	0	0
90	44	0	32	0	12	0	0	0	0	0	0	0

PA0002740

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
TWO WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
91	52	0	50	0	2	0	0	0	0	0	0	0
92	57	0	55	0	2	0	0	0	0	0	0	0
93	47	1	35	0	12	1	0	0	0	0	0	0
94	46	0	42	0	4	0	0	0	0	0	0	0
95	47	0	43	0	4	0	0	0	0	0	0	0
96	53	3	44	0	9	3	0	0	0	0	0	0
97	36	0	32	0	4	0	0	0	0	0	0	0
98	69	0	57	0	12	0	0	0	0	0	0	0
99	45	0	33	0	12	0	0	0	0	0	0	0
100	47	0	32	0	12	0	3	0	0	0	0	0
101	33	0	30	0	0	0	0	0	0	0	0	0
102	51	0	49	0	2	0	0	0	0	0	0	0
103	51	0	49	0	2	0	0	0	0	0	0	0
104	65	0	53	0	12	0	0	0	0	0	0	0
105	44	0	32	0	12	0	0	0	0	0	0	0
106	44	0	32	0	12	0	0	0	0	0	0	0
107	34	0	34	0	0	0	0	0	0	0	0	0
108	112	1	76	0	0	0	23	1	11	0	0	0
110	18	0	18	0	0	0	0	0	0	0	0	0
--- Total ---												
	4535	430	3197	348	1024	59	252	15	32	6	10	0

PAG002741

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
TWO WORLD TRADE CENTER
ELEVATOR SHAFTS

ELEVATOR SHAFT	TOTAL SAMPLES	POSITIVE SAMPLES
01	14	0
03	12	1
05	15	3
07	26	0
08	14	0
09	3	0
10	3	4
11	13	11
13	17	0
14	14	3
16	18	0
18	14	0
21	16	0
23	17	0
24	4	4
29	4	4
31	5	5
33	5	5
38	7	7
41	7	7
44	7	7
45	6	5
48	36	0

PA0002742

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
TWO WORLD TRADE CENTER
ELEVATOR SHAFTS

ELEVATOR SHAFT	TOTAL SAMPLES	POSITIVE SAMPLES
32	4	0
34	4	4
57	5	5
62	5	0
64	7	0
66	4	4
69	10	0
74	7	0
75	4	0
78	4	0
81	5	0
83	3	0
87	7	0
90	7	0
93	6	0
98	8	0
*** Total ***	377	83

PA0002743

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
TWO WORLD TRADE CENTER
ELEVATOR PITS

ELEVATOR PIT	TOTAL SAMPLES	POSITIVE SAMPLES
01-02	3	0
03-04	2	0
05	1	0
06-07	2	0
16-17	2	0
18-19	3	0
20-21	3	0
24-25	3	2
27	2	0
28-29	3	2
30-31	4	4
32	1	1
33	1	1
34-35	3	1
36	3	1
37-38	3	3
39-40	3	2
41	3	1
42	3	2
43-44	3	2
45-46	3	2
47	3	1
48	2	2

PA0002744

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
TWO WORLD TRADE CENTER
ELEVATOR PITS

ELEVATOR PIT	TOTAL SAMPLES	POSITIVE SAMPLES
49	3	0
*** Total ***	61	27

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
THREE WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES
1	10	0	10	0
*** Total ***	10	0	10	0

PA0002746

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
FOUR WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
2	43	0	43	0	0	0	2	0	0	0	0	0
3	43	0	43	0	0	0	0	0	0	0	0	0
4	43	0	43	0	0	0	0	0	0	0	0	0
5	43	0	43	0	0	0	0	0	0	0	0	0
6	86	0	86	0	0	0	0	0	0	0	0	0
7	81	0	81	0	0	0	0	0	0	0	0	0
8	30	0	30	0	0	0	0	0	0	0	0	0
9	83	0	63	0	0	0	17	0	1	0	0	0
*** Total ***												
	440	0	420	0	0	0	19	0	1	0	0	0

PA0002747

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
FIVE WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL CONVECTOR SAMPLES	POSITIVE CONVECTOR SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES	TOTAL TILE/OTHER SAMPLES	POSITIVE TILE/OTHER SAMPLES
1	38	0	28	0	0	0	10	0	0	0	0	0
2	98	3	94	0	0	0	4	3	0	0	0	0
3	92	0	92	0	0	0	0	0	0	0	0	0
4	90	1	84	0	6	1	0	0	0	0	0	0
5	102	6	96	6	6	0	0	0	0	0	0	0
6	111	0	111	0	0	0	0	0	0	0	0	0
7	98	0	98	0	0	0	0	0	0	0	0	0
8	90	0	89	0	0	0	1	0	0	0	0	0
9	132	1	89	1	0	0	33	2	9	0	1	0
*** Total ***												
	851	13	781	7	12	1	48	3	9	0	1	0

PA0002748

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
SIX WORLD TRADE CENTER

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES
2	10	0	10	0
*** Total ***	10	0	10	0

PA0002749

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
NORTHEAST W.T.C. SUBLEVELS

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES
B1	43	1	19	0	20	1	6	0
B2	95	0	90	0	5	0	0	0
B4	75	0	75	0	0	0	0	0
*** Total ***	213	1	184	0	25	1	6	0

PA0002750

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
NORTHWEST W.T.C. SUBLEVELS

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES
B1	88	28	77	27	10	1	1	0
B2	54	14	40	10	13	3	1	1
B3	41	0	28	0	12	0	1	0
B4	30	6	25	5	4	1	1	0
B5	5	0	0	0	5	0	0	0
B6	15	0	0	0	15	0	0	0
*** Total ***	231	48	170	42	57	5	4	1

[redacted]

PA0002751

HD00044195

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
SOUTHEAST W.T.C. SUBLEVELS

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES
B1	37	0	24	0	23	0	8	0
B2	96	0	86	0	10	0	0	0
B4	27	0	27	0	0	0	0	0
*** Total ***	160	0	137	0	33	0	8	0

PA0002752

HD00044196

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
SOUTHWEST W.T.C. SUBLEVELS

FLOOR	TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL CEILING SAMPLES	POSITIVE CEILING SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES	TOTAL FALLOUT SAMPLES	POSITIVE FALLOUT SAMPLES
B1	233	30	185	16	45	14	3	0
B2	45	4	23	2	22	2	0	0
B3	28	0	11	0	17	0	0	0
B4	10	0	3	0	7	0	0	0
B5	19	0	0	0	19	0	0	0
B6	88	28	10	0	78	28	0	0
*** Total ***	443	62	232	18	208	44	3	0

PA0002753

WORLD TRADE CENTER
ASBESTOS BULK SAMPLING SUMMARY
RIVER WATER PUMPING STATION

TOTAL SAMPLES	POSITIVE SAMPLES	TOTAL PIPING/DUCT SAMPLES	POSITIVE PIPING/DUCT SAMPLES
8	0	8	0

PA0002754

HD00044198

LABORATORY PROCEDURES

The analytical techniques used in this project are EPA-600/M4-82-020 and NIOSH 7400. Samples were analyzed in the Environmental/Industrial Hygiene Laboratory located at 25 Journal Square, Jersey City, New Jersey. All analyses were performed by Hans Brown, Marc Fish and Iradj Youssefnia under the supervision of David Platt.

The laboratory staff participates in the USEPA Bulk Asbestos Quality Assurance Program, identification number 2159; and NIOSH Proficiency Analytical Testing Program, identification number 07036-001. The laboratory has maintained a quality control and assurance program using McCrone Environmental Services Inc., Norcross, Ga., as the reference laboratory.

All samples are documented from sample procurement, through analysis, to disposal using a state approved contractor. Disposal contractor's receipts are required to insure a legal final disposition of all asbestos waste.

* Note: "Asbestos Containing Material" (ACM) is defined by the United States Environmental Protection Agency as any substance which contains more than 1% asbestos.

The symbol "<" means less than, and "TRACE" means a barely perceivable indication of asbestos that is much less than the USEPA limit for ACM.

PA0002755

HD00044199
